

dc

Date: 26.11.2024

To,
The Director
Northern Regional Office (MoEF),
Bays No. 24 -25, Sector- 31-A,
Dakshin Marg, Chandigarh,
Haryana - 160030

Subject: Submission of half yearly environment compliance report for IT/ Information Technology Enabled Services (SEZ) project at Village- Gwal Pahari in Tehsil Wazirabad, District- Gurugram, Haryana by M/s ASF Insignia SEZ Pvt. Ltd.

Reference No: *SEIAA/HR/2014/331 Dated: 21/02/2014; and amendment thereto vide a letter No. SEIAA/HR/2019/201 dated 22.07.2019 and SEIAA (125)/HR/2021/254 Dated 04.03.2021 and Extension of validity of EC vide memo No. SEIAA/HR/2021/465 Dated 11.05.2021).*

Dear Sir,

This is with reference to the above captioned subject; Six monthly compliance report for the period; **April 2024 – September 2024** on the status of compliance stipulated in the EC condition as mentioned in *Para – II, Part-B* of general condition of SEIAA letter quoted above (attached as an *Annexure I* for your ready reference) is appended herein along with Lab Monitoring reports and necessary annexures. and no construction activities happening at site for last 4 years.

**Thanking you,
For ASF INSIGNIA SEZ PVT. LTD.**


Authorized Signatory

Encl: As above

CC:

1. Haryana State Pollution Control Board, C-11 Sec-6, Panchkula, Haryana.
2. SEIAA, Haryana Bays No. 55 - 58, Parytan Bhawan, 1st floor, Sector - 2, Panchkula, Haryana.
3. Regional Officer Gurgaon (North) Haryana State Pollution Control Board, Vikas Sadan, 1st floor Near DC Court Gurgaon, Pin code - 122001

ASF INSIGNIA SEZ PRIVATE LIMITED

Site Office : ASF Insignia SEZ (IT/ITes), Vatsal Valley (Gwal Pahari), off Gurugram-Faridabad Road, Gurugram-122003, Haryana

T: +91 124 2557100 F: +91 124 2557135 E: corporate@asfinfrastructure.com W: www.asfinfrastructure.com

Regd. Office : 11, Babar Lane, Bengali Market, New Delhi-110 001 T: +91 11 23355511 F: +91 1123739298

Corp. Office : ASF Centre, 362-363, Udyog Vihar, Phase-IV, Gurugram-122016 (India) T: +91 124 4777200 F: +91 124 4234110

CIN U45201DL2005PTC140408

Creating Intelligent Spaces®

HALF YEARLY ENVIRONMENT COMPLIANCE REPORT

FOR

IT/ITES SEZ PROJECT “ASF INSIGNIA”

LOCATED AT


Village Gwal Pahari, Tehsil Wazirabad,
District- Gurugram (Haryana)

Period: April 2024 September 2024

BY

M/S ASF INSIGNIA SEZ PVT.LTD.

For ASF INSIGNIA SEZ PVT. LTD.



Authorized Signatory

LIST OF ANNEXURES

S. No	Particulates	Annexure
1.	Environment Clearance Letter Nos <i>SEIAA/HR/2014/331 DATED 21.02.2014,(to be read with amendments granted vide memo nos. SEIAA/HR/2019/201 DATED 22.07.2019 and SEIAA (125)/HR/2021/254 Dated 04.03.2021).</i>	I
2.	Photograph of first aid room	II
3.	Form IV	III
4.	Ambient air test report	IV
5.	Photograph of RWH Pits	V
6.	Photograph of Fire equipment	VI
7.	Photograph of Fire Control Room	VII
8.	CTO of B2	VIII
9.	CTO of B3	IX
10.	CTO of Housing /Residential	X
11.	STP Test Report	XI
12.	Borewell outlet	XII
13.	Form V	XIII
14.	Audit report attached	XIV

For ASF INSIGNIA SEZ PVT. LTD.


Authorised Signatory

BRIEF DESCRIPTION OF THE PROJECT

The Environmental Clearance for the project was accorded by the SEIAA, Haryana vide letter no. *SEIAA/HR/2014/331 Dated 21.02.2014 (to be read with amendments granted vide memo nos. SEIAA/HR/2019/201 Dated 22.07.2019 and SEIAA (125)/HR/2021/254 Dated 04.03.2021)*. The project is partially under operation phase and partially under construction/ development / / phase.


OVERALL PROJECT

The IT/ITES – Special Economic Zone (SEZ) project is being developed by M/s ASF Insignia SEZ Pvt. Ltd. located in the Village- Gwal Pahari in Tehsil Wazirabad , District- Gurugram, Haryana on a land admeasuring 47.698 acre (1,92,994.58m²). The proposed project will consist of Processing Zone and Non-Processing zone having IT/ITES buildings B1, B2 and B3, Residential apartments, Commercial office, amenity spaces, Shopping spaces and Training Centre etc.

As the project will be completed and operationalized in stage wise manner, therefore the half yearly environment compliance report is prepared for both Construction/development/ and Operation phases. The key parameters of Environmental Clearance and it's amendments vide memos SEIAA/HR/2014/331 dated 21/02/2014 ,SEIAA/HR/2019/201 DATED 22.07.2019 & SEIAA(125)/HR/2021/254 Dated 04.03.2021 are as below

1. The total proposed built up area of the project is 7,92,209.65 m²
2. The total envisaged water requirement of the project is 2679 KLD which includes both fresh and treated water.
3. The total envisaged fresh water requirement of the project is 988.8 KLD.
4. The total envisaged waste water generation is 1901.56 KLD
5. The total STP capacity of the project is 2300 KLD
6. The proposed green belt development to be 35.15 % of the project area.
7. The total envisaged solid waste generation will be 8.3 TPD.
8. Total 40 numbers of Rain water harvesting pits for the project area are proposed for recharging the ground water level.
9. The total power requirement for the project will be 35 MVA approximately.
10. The source of the water supply during operation phase will be through the CGWA approved bore wells and HUDA water as and when provided
11. The construction/ development work to be undertaken with the treated water of the STPs.
12. The total proposed parking spaces are 10100 ECS.

For ASF INSIGNIA SEZ PVT. LTD.


Authorised Signatory

PART UNDER OPERATION PHASE

The IT/ITES Buildings (B2 & B3), Amenity Podium Building, Facility Management (BMS) Building and Energy Centre Building in Processing Zone and Residential Building (Tower A, B & C) and Club House in Non Processing Zone are under operation for which the necessary approvals from various authorities had already been obtained and the details of the key parameters are as under:


1. The total built up area of the Buildings under operation phase is approx. 3.59 Lacs Sq. Mtrs.
2. The green area comprising green belt, grass, peripheral green, developed is 20679 sq.m
3. The total envisaged water requirement of the operational phase of the project is 775 KLD.
 1. The fresh water requirement is 354.27 KLD.
 2. The waste water generated is 427.92 KLD.
 3. Total solid waste generation is 0.67 TPD. The source of the water supply is through Borewells for which CGWA approval has already been obtained; however, the proposed HUDA water is not available till date and once the HUDA water is available these bore wells shall be used for the standby or to meet the deficit.
 4. The waste water is being treated in the STP of 465 KLD installed for Building B2 and STP of 530 KLD installed for Building B3, the waste water is being treated in the STPs and the treated water is being used for the construction/ development, flushing, HVAC, Anti smog gun and landscape work of the project.
 5. So far, 21 Nos of Rain water harvesting pits have been made for recharging the ground water and are operational.
 6. The available power connection from DHVBN till date is 4800 KW for the operation and 500 KVA for the construction/ development phase
 7. The total parking provided is 1718 ECS

PART OF THE PROJECT UNDER DEVELOPMENT/ CONSTRUCTION PHASE

The IT/ITES Buildings (B1), Amenity Podium Building, and 66 KV Sub Station Building in Processing Zone and Residential Buildings, Commercial / Retail Buildings, Training Centre Building, Energy Centre Building and other Amenities Building etc in Non-Processing Zone are under development / construction phase. Proposed Built-up area for buildings under development / construction phase is approx. 4.33 Lacs Sq. Mtrs. Details of the key parameters are as under:


- The balance fresh water requirement of the project will be about 634.64 KLD. The balance solid waste generation will be about 7.63 TPD.

For ASF INSIGNIA SEZ PVT. LTD.



Authorised Signatory

- The source of the water supply during operation phase will be through the CGWA approved bore wells and HUDA water (HUDA water connection is yet to be provided by Authorities).
- The construction/ development work is being done with the treated water of the STPs.
- Another 19 nos. of Rain water harvesting pits are proposed for recharging the ground water level.
- The parking requirement as per the Haryana bye laws and as per MoEFCC is 8382 ECS.

For ASF INSIGNIA SEZ PVT. LTD.



Authorised Signatory

<p>Conditions of Environment Clearance No. SEIAA/HR/2014/331dtd 21.02.2014 (to be read with amendments granted vide memo nos. SEIAA/HR/2019/201 DATED 22.07.2019 read with SEIAA (125)/HR/2021/254 Dated 04.03.2021).</p>		Compliance Status
PART – A		
[1]	<p>“Consent To Establish” shall be obtained from Haryana State Pollution Control Board under air and water act and a copy shall be submitted to the SEIAA, Haryana before the start of any construction work at site.</p>	<p>Complied. The Consent To Establish for the Existing IT/ITES project had been obtained vide letter no. HSPCB/TAC/2011/663 dated 07.03.2011 from Haryana State Pollution Control Board which was submitted to SEIAA, Haryana.</p> <p>The Consent to Establish no. HSPCB/Consent/:2808615GUNOCTE1390645 dated 27.02.2015 was obtained.</p> <p>The Consent To Establish for the Expansion Phase had been obtained vide letter no. HSPCB/Consent/: 320303318GUNOCTE5008171 dated 07.03.2018 valid up to 20.02.2021</p> <p>The Consent To Establish for the Project obtained vide letter no. HSPCB/Consent/: 320303321GUNOCTE12599143 dated 23.06.2021 valid up to 20.02.2024</p> <p>The Consent To Establish for the Project obtained vide letter no. HSPCB/Consent/ : 329993524GUNOCTE50689148 dated 18.01.2024. Valid up to 20.08.2024 (upto validity of our EC referred in abov para. The same has been reapplied . Till new EC is received , we have stopped our construction activities)</p>
[2]	<p>A first aid room will be provided in the project both during construction and operation of the project.</p>	<p>Complied. For ASF INSIGNIA SEZ PVT. LTD. First Aid Facilities are attached as an Annexure II  Authorised Signatory</p>


[3]	Adequate drinking water and sanitary facilities should be provided for construction workers at the site. Provision should be made for mobile toilets. Open defecation is strictly prohibited. The safe disposal of waste water and solid wastes generated during the construction phase should be ensured.	Complied.
[4]	All the topsoil excavated during construction activities should be stored for use in horticulture/landscape development within the project site.	Ensured
[5]	The project proponent shall ensure that the building material required during construction phase is properly stored within the project area and disposal of construction waste should not create any adverse effect in the neighbouring communities and should be disposed of after taking necessary precautions for general health and safety aspects of people, only in approved sites with the approval of competent authority.	Complied. Building material is properly stored at the designated areas of the site and construction waste / Debris is mainly used in the internal fillings and surplus disposed-off at the approved sites of MCG
[6]	Construction spoils, including bituminous material and other hazardous materials, must not be allowed to contaminate watercourses and the dump sites for such materials must be secured so that they should not leach into the ground water and any Hazardous waste generated during the construction phase, should be disposed as per applicable rules and norms with necessary approval of the Haryana State Pollution Control Board	Complied.


For ASF INSIGNIA SEZ PVT. LTD.



Authorized Signatory

[7]	The diesel generator set to be used during construction phase should be of ultra-low sulphur diesel type and should conform to Environment (Protection) Rules prescribed for air and noise emissions standards.	Complied.
[8]	The Diesel required for operating DG set shall be stored in underground tanks and if required, clearance from chief controller of Explosive shall be taken.	Complied.
[9]	Ambient noise level should conform to residential standards both during day and night. Incremental pollution loads on the ambient air and noise quality should be closely monitored during construction phase. Adequate measures should be taken to reduce ambient air and noise level during construction phase, so as to conform to the stipulated standards.	Complied. Ambient air monitoring report for the month of JUNE 2024 is enclosed ref. Annexure – III
[10]	Fly ash should be used as building material in the construction as per the provision of Fly Ash Notification of September, 1999 and amended as on 27 th August, 2003.	Complied
[11]	Storm water control and its reuse as per CGWB and BIS standards for various applications should be ensured	Ensured. For complete project, 40 nos of RWH pits are envisaged. Out of which 21 nos of RWH pits are operational. Photographs of RWH Pits are attached in Annexure – V
[12]	Water demand during construction should be reduced by use of pre-mixed concrete, curing agents and other best practices referred.	Complied.
[13]	In view of the several constraints in water supply augmentation in the region and sustainability of water resources, the developer will submit the NOC from CGWA specifying water extraction quantities and assurance from HUDA/ utility	Complied. Fresh water requirement is being met through ground water for which NOC from CGWA had been obtained. For Construction activities, treated water from in house STP is available. In addition, surplus treated water if required is being provided from nearby CSTP for which assurance from HUDA has

	<p>provider indicating source of water supply and quantity of water with details of intended use of water – potable and non-potable. Assurance is required for both construction and operation stages separately. It shall be submitted to the SEIAA and RO, MoEF Chandigarh, before the start of construction</p>	<p>been obtained.</p>
[14]	<p>Roof should meet prescriptive requirements as per Energy Conservation Building Code by using appropriate thermal insulation material</p>	<p>Complied. Overdeck thermal insulation provided for all the buildings</p>
[15]	<p>Opaque wall should meet prescriptive requirements as per Energy Conservation Building Code which is proposed to be mandatory for all conditioned spaces while it is desirable for non air- conditioned spaces by use of appropriate thermal insulation material to fulfill requirement.</p>	<p>Ensured.</p>
[16]	<p>The approval of the competent authority shall be obtained for structural safety of the building due to earthquake, adequacy of firefighting equipment's, etc. as per National Building Code including protection measures from lightening etc. If any Forest Conservation Act shall be taken from Competent Authority.</p>	<p>Complied. Structure stability certificate has been obtained. Structure, firefighting are being constructed as per National Building Code and lightning protection measures are being provided</p>
[17]	<p>Overexploited ground water and impending severe shortage of water supply in the region requires the developer to redraw the water and energy conservation plan. Developer shall reduce the overall footprint of the proposed development. Project proponent shall incorporate water efficiency/ savings measures as well as water reuse/ recycling within 3 month and before start of construction to the SEIAA, Haryana and RO, MoEF, GOI,</p>	<p>Complied</p> <p style="text-align: right;">For ASF INSIGNIA SEZ PVT. LTD.  Authorised Signatory</p>


	Chandigarh	
[18]	The project proponent as stated in the proposal shall construct 40 rain water harvesting pits for recharging the ground water within the project premises. RWH pits shall be designed to make provisions for silting chamber and removal of floating matter before entering harvesting pit. Maintenance budget and persons responsible for Maintenance must be provided. Care shall also be taken that contaminated water do not enter any RWH pit.	Complied. 21 Nos of RWH pits has been designed and constructed in accordance with the approved plans.
[19]	The project proponent shall provide for adequate fire safety measure and equipment's as required by Haryana Fire Service Act, 2009 and instructions issued by the local Authority Directorate of fire from time to time. Further the project proponent shall take necessary permission regarding fire safety scheme/NOC form competent Authority as required.	Complied. Adequate fire safety measure and equipment's are provided as per the provision of Haryana Fire Service Act, 2009 and relevant norms. Necessary Fire NOC is being taken.
[20]	The project proponent shall obtain assurance from the DHBVN for supply of 40 MVA of power supply before the start of construction. In no case project will be operational solely on generators without any power supply from any external power utility.	Complied.
[21]	Detail calculation of power load and ultimate power load of the project shall be submitted to DHBVN under intimation to SELAA Haryana before the start of construction. Provisions shall be made for electrical	Complied. For ASF INSIGNIA SEZ PVT. LTD.  Authorised Signatory

	infrastructure in the project area.	
[22]	The project proponent shall not raise any construction in the natural land depression/Nallah/water course and shall ensure that the natural follow from the Nallah/water course is not obstructed.	Noted
[23]	The project proponent shall keep the plinth level of the building blocks sufficiently above the level of the approach road to the project as per prescribed by laws. Levels of the other areas in the projects shall also be kept suitably so as to avoid flooding.	Complied.
[24]	Construction shall be carried out so that density of population does not exceed norms approved by Director General Town and Country Department Haryana.	Complied. All Building plans are being approved by The Unit Approval Committee Chaired by Development Commissioner, NSEZ, Noida in consultation with Town and Country Department Haryana..
[25]	The project proponent shall submit an affidavit with the declaration that ground water will not be used for construction and only treated water should be used for construction	Complied. Affidavit copy of the same had been provided earlier.
[26]	The project proponent shall not cut any existing tree and project landscaping plan should be modified to include those trees in green area.	Complied
[27]	The project proponent shall ensure that EBC norms for composite climate zone are met. In particular building envelope, HVAC service, water heating, pumping, lighting and electrical infrastructure must meet ECBC norms.	Complied.

For ASF INSIGNIA SEZ PVT. LTD.



Authorized Signatory


[28]	The project proponent shall provide 3 meter high barricade around the project area, dust screen for every floor above the ground, proper sprinkling and covering of stored material to restrict dust and air pollution during construction.	Complied. Every listed measure and any further guidelines released on dust and air pollution controls applicable to construction activities are being adhered. Deployed Anti-smog gun immediately after the guidelines by HSPCB were issued.
[29]	The project proponent shall construct a sedimentation basin in the lower level of the project site to trap pollutant and other wastes during rains.	Complied
[30]	The project proponent shall provide proper Rasta of proper width and proper strength for each project before the start of construction.	Complied
[31]	The project proponent shall ensure that the U-value of the glass is less than 3.177 and Maximum solar heat gain coefficient is 0.25 for vertical fenestration.	Noted
[32]	The project proponent shall adequately control construction dusts like silica dust, non-silica dust, and wood dust. Such dusts shall not spread outside project premises project Proponent shall provide respiratory protective equipment to all construction workers.	Complied. Adequate control measures including protective equipment for construction workers are in place
[33]	The project proponent shall provide one refuse area till 24 meter, one till 39 meter and one after every 15 meter as per National Building Code. The project proponent shall not convert any refuse area in the habitable space and it should not be sold out/commercialized.	Complied The applicable refuse areas will be provided at designated heights of the building as per NBC.
[34]	The project proponent shall provide fire control room and fire officer for building above 30 meters as per National Building Code.	Complied. Photograph of fire control room is attached as an Annexure VII
[35]	The project proponent shall obtain permission of Mines and Geology Department for excavation of soil before the start	Complied. For ASF INSIGNIA SEZ PVT. LTD.  Authorised Signatory


	of construction	
[36]	The project proponent shall seek specific prior approval from concerned local Authority/HUDA regarding provision of storm drainage and sewerage system including their integration with external services of HUDA / Local authorities beside other required services before taking up any construction activity.	Noted
[37]	The site for solid waste management plan is earmarked on the layout plan and the detailed project for setting up the solid waste management plan shall be submitted of the Authority within one month.	Noted.
[38]	Vertical fenestration shall not exceed 40% of total wall area.	Noted.
[39]	The project proponent shall discharge excess of treated waste water/ storm water in the public drainage system and shall seek permission of HUDA before the start of construction.	Noted.
[40]	The project proponent shall seek NOC from Town and country department regarding height of the building allowed in the skyline of that area.	Complied.
[41]	The project proponent shall ensure that structural stability to withstand earthquake of magnitude 8.5 on richter scale.	Ensured. Ensured as per NBC Norms.
[42]	The project proponent shall ensure that no construction activity is undertaken either on surface or below or above surface of revenue rasta passing through the project area.	Ensured.

For ASF INSIGNIA SEZ PVT. LTD.



Authorized Signatory

[43]	The project proponent shall indicate the width and length of revenue Rasta passing through the project area on sign board and shall display the same at both the ends of revenue Rasta stretch, for awareness of public, sign board also display the message that the is public rasta / road and any citizen can use it. There shall not be any gate with or without guards on revenue rasta.	Noted.
[44]	The project proponent shall ensure that natural flow of existing nallah is never obstructed and shall seek NOC from Irrigation Department regarding this before the start of construction.	Noted
[45]	The project proponent shall ensure that in case of excessive flow of water in nallah, the structural integrity of buildings alongside the nallah is not breached in any circumstances.	Noted.
[46]	The project proponent shall ensure that there should not be any water logging on the bed of nallah even in case of excessive rain.	Noted.
[47]	The project proponent shall ensure that sewerage pipe line should not cross over the nallah and project proponent shall maintain separate STP in the plot area across the nallah.	Noted.
[48]	The project proponent shall ensure that sewerage system and storm drainage system shall be planned by taking into account the natural slope of original land and approval from HUDA and irrigation department shall be taken before the start of construction.	Ensured.
[49]	The project proponent shall ensure that bed of nallah is not encroached in any manner, while constructing the culvert over the nallah.	Noted. For ASF INSIGNIA SEZ PVT. LTD.  Authorised Signatory


[50]	The project proponent shall ensure plinth level of the building block is 1.5 meter above 100 years flood level.	Complied.
[51]	The project proponent shall provide pervious surface instead of impervious and hard surface in order to reduce overflow of water in nallah.	Noted.
[52]	The project proponent shall ensure proper drainage in the project area as the project area is uneven and undiluted.	Ensured.
B. Operational Phase		
[a]	“Consent to Operate” shall be obtained from Haryana State Pollution Control Board under Air and Water Act and a copy shall be submitted to the SEIAA, Haryana.	<p>Complied. The Consent to Operate has already been obtained and submitted.</p> <p>The consent to operate renewal for Building B2 has been obtained via HSPCB/Consent/: 320303322 GUNOCTO 25902144 dated 20.08.2022 valid up-to 30.09.2027 and attached as an Annexure VIII.</p> <p>The consent to operate renewal for Building B3 has been obtained via HSPCB/Consent/: 320303322 GUNOCTO 25902144 dated 20.08.2022 valid up to 30.09.2027 and attached as an Annexure IX.</p> <p>The consent to operate for Housing /Residential has been obtained via Certificate No. HSPCB/Consent/:329993522GUNOCTOW19397394 dated: 02/02/2022 Valid up to 31.03.2025 and attached as an Annexure X.</p>
[b]	The Sewage Treatment Plant (STP) shall be installed for the treatment of the sewage to prescribed including odor and treatment effluent shall be recycled. The installation of STP should be certified by an independent expert and a report in this regard should be submitted to the SEIAA, Haryana before the project is commissioned for operation. Tertiary treatment of waste	<p>Complied.</p> <p>The STP of 530, 465 KLD and 50 KLD capacities for B3 , B2 and Housing /Residential respectively has been installed. STP feasibility report and photographs of the same has already been submitted. Report of independent expert along with STP inlet and outlet test report are attached as an Annexure.-XI For ASF INSIGNIA SEZ PVT. LTD.</p> <p style="text-align: right;"> Authorised Signatory</p>

	<p>water is mandatory. Discharge of treated sewage shall conform to the norms and standards of HSPCB, Panchkula project proponent shall implement such STP Technology which does not required filter backwash</p>	
[c]	<p>Separation of the grey and black water should be done by use of dual plumbing line. Treatment of 100% grey water by decentralized treatment should be done ensuring that the re-circulate water should have BOD level less than 10mg/ litre. And the recycled water will be used for flushing, gardening and DG set cooling etc. to achieve zero exit discharge.</p>	<p>Complied: Dual plumbing lines have been provided. Tertiary treatment of grey water is being carried out. Treated water is being used for flushing, gardening and HVAC cooling. We have zero exit discharge.</p>
[d]	<p>For disinfection of the treated wastewater ultra-violet radiation or ozonization process should be used.</p>	<p>Ensured.</p>
[e]	<p>Diesel power generating sets proposed as source of back power for lifts, common area illumination and for domestic use should be of enclosed type and conform to rules made under the Environment (Protection) Act, 1986. The location of the DG sets should be in the basement as promised by the project proponent with appropriate stack heights as per the CPCB norms. The diesel used for the DG sets shall be ultra-low sulphur diesel(35ppm sulphur), instead of low sulphur diesel.</p>	<p>Complied. DG Sets used in the project site for various purposes are placed in a acoustic treated area which is as per CPCB norms. The stack heights are as per CPCB norms.</p>

For ASF INSIGNIA SEZ PVT. LTD.





Authorized Signatory

	of rain fall. Roof top of the building shall be without any toxic material or which can contaminate rain water. Wire mesh and filters should be used wherever required.	
[j]	The ground water level and its quality should monitor regularly in consultation with Central Ground Water Authority.	<p>Complied. Ground water level and its quality are being monitored at regular intervals. Reports on water level and quality are being sent to the competent authorities on regular basis.</p> <p>Test reports of Bore well Outlet are attached as an Annexure – XII</p>
[k]	A report on the energy conservation measure conforming to energy conservation norms finalized by Bureau of Energy Efficiency should be prepared incorporating details about building materials & Technology, R & U factors etc and submitted to the SEIAA, Haryana in three months' time.	<p>Ensured. Energy Audit report on Energy Conservation prepared as per the norms by Bureau of Energy Efficiency. The Copy of the same had been provided earlier</p>
[l]	Energy conservation measure like installation of LED for lighting the areas outside the building should be integral part of the project design and should be in place before project commission. Use of solar panels must be adapted to the maximum energy conservation	<p>Ensured. Energy conservation methods adopted like installation of LED lights, Solar Panels for heating of water, VFDs, Double Glass Units, Shadings etc.</p>
[m]	The project proponent shall use zero ozone depleting potential material in insulation, refrigeration, air- conditioning and adhesive; project	<p>Ensured.</p> <p>For ASF INSIGNIA SEZ PVT. LTD.</p> <p> Authorised Signatory</p>

	proponent shall also provide Halon free fire suppression system	
[n]	The solid waste generated should be properly collected and segregated as per the requirement of the MSW Rules, 2000 and as amended from time to time. The bio-degradable waste should be treated by appropriate technology at the site earmarked within the project area and dry/inert solid waste should be disposed off to the approved sites for land filling after recovering recyclable material.	Ensured.
[o]	The provision of the solar water heating system shall be as per norms specified by HAREDA and shall be made operational in each building block.	Complied.
[p]	The traffic plan and the parking plan proposed by the project proponent should be adhered to meticulously with further scope of additional parking for future requirement. There should be no traffic congestion near the entry and exit points from the roads adjoining the proposed project site. Parking should be fully internalized and no public space should be used	Ensured. Parking facility had been provided within the premises as per the norms. There is no traffic congestion on the site.
[q]	The project shall be operationalized only when HUDA / local authority will provide domestic water supply system in the area.	Complied. Currently, HUDA has no provision of water supply in this area or neighbourhood. NOC for the regularization of existing tube well has been obtained from the nominated agency of Central Ground Water Authority (CGWA). The copy of the same attached.

FOR ASF INSIGNIA SEZ PVT. LTD.



 Authorised Signatory

[r]	Operation and maintenance of STP, Solid waste management and electrical infrastructure, pollution control measure shall be ensured even after the completion of project.	Noted
[s]	Different type of wastes should be disposed off as per provisions of municipal solid waste, biomedical waste, hazardous waste, e-waste, batteries & plastic rules made under Environmental Protection Act, 1986, Particularly E-waste and battery waste shall be disposed of as per existing E-waste Management Rules 2011 and Batteries Management Rules 2001, The project proponent should maintain a collection centre for E-waste and it should be disposed of to only registered and authorized dismantler / recycler.	<p>Complied.</p> <p>All categories of wastes are handled and disposed-off as per applicable Rules.</p>
[t]	Standards for discharge of environmental pollutants as enshrined in various schedules of rules 3 of Environmental Protection Rules 1986 shall be strictly Complied with.	Complied
[u]	The project proponent shall make provision for guard pond and other provisions for safety against failure in the operation of wastewater treatment facilities. The project proponent shall also identify acceptable outfall for treated effluent.	<p>Noted</p> <p>STPs of B 2 and B 3 are interconnected so that in case of any breakdown in one STP, the sewerage of the same could be diverted to the other STP.</p>
[v]	The project proponent shall ensure that the stack height of DG sets is as per the CPCB guide lines and also ensure that the emission standards of noise and air are within the CPCB prescribed limits. Noise and Emission level of DG sets greater than 800KVA shall be as per CPCB latest standards for high capacity DG Sets.	<p>Ensured and made all provisions as per CPCB norms.</p> <p style="text-align: right;">For ASF INSIGNIA SEZ PVT. LTD.</p> <p style="text-align: right;"> Authorised Signatory</p>

[w]	All electric supply exceeding 100amp, 3 phases shall maintain the power factor between 0.98 lag to 1 at the point of connection.	Complied.
[x]	The project proponent shall minimize heat island effect through shading and reflective or pervious surface instead of hard surface.	Ensured.
[y]	The project proponent shall use only treated water instead of fresh water for HVAC and DG cooling. The project proponent shall also use evaporative cooling technology and double stage cooling system for HVAC in order to reduce water consumption. Further temperature, relative humidity during summer and winter seasons should be kept at optimal level. Variable speed drives, best Co-efficient of Performance (CoP), as well as optimal Integrated Point Load Value and minimum outside fresh air supply may be restored for conservation of power and water. Coil type cooling DG sets shall be used for saving cooling water consumption for water cooled DG sets.	Complied. Treated water of STP being used for cooling of HVAC equipment.
[z]	The project proponent shall ensure that the transformer is constructed with high quality grain oriented, low loss silicon steel and virgin electrolyte grade copper. The project proponent shall obtain manufacturer's certificate also for that.	Complied.
[aa]	Water supply shall be metered among different users and different utilities.	Ensured. Flow meters provided at various outlets.

For ASF INSIGNIA SEZ PVT. LTD.


 Authorised Signatory


[ab]	The project proponent shall ensure that exit velocity from stack should be sufficiently high. Stack shall be designed in such a way that there is no stack down –water under any meteorological conditions	Ensured.
[ac]	The project proponent shall provide water sprinkling system in the project area to suppress the dust in addition to the already suggested mitigation measures in the Air Environment chapter of EMP.	Ensured.
[ad]	The project proponent shall ensure proper Air Ventilation and light system in the basements area for comfortable living of human being and shall ensure that number of Air Changes per hour/(ACH) in basement never falls below 15. In case of emergency capacity for increasing ACH to the extent of 30 must be provided by the project proponent.	Ensured.
[ae]	The project proponent shall get the inspection of nallah before the onset of monsoon season every year from Irrigation department.	Noted.
[af]	The project proponent shall not discharge untreated water in the nallah and also shall not throw any solid waste in the nallah.	Ensured.
PART-B GENERAL CONDITIONS		
B [i]	The project proponent shall ensure the commitments made in Form-1, Form-1A, EIA/EMP and other documents submitted to the SEIAA for the protection of environment and proposed environmental safeguards are Complied with in letter and spirit. In case of contradiction between two or more	Complied. All the commitments made in the Form-1, Form-1A, EIA/EMP and other documents submitted to the SEIAA had been and are being complied strictly during the construction as well as the operation phase of the project. For ASF INSIGNIA SEZ PVT. LTD.  Authorised Signatory

	documents on any point, the most environmentally friendly commitment on the point shall be taken as commitment by project proponent.	
B [ii]	The project proponent shall also submit six monthly reports on the status of compliance of the stipulated EC conditions including results of monitored data(both in hard copies as well as e-mail) to the northern regional office of MoEF, the respective Zonal office of CPCB, HSPCB and SEIAA Haryana.	Complied. Six monthly compliance reports on the status of compliance of the stipulated EC conditions including results of monitored data is being submitted to the HSPCB, Northern Regional office-MoEF, SEIAA-Haryana and Regional office of CPCB as per the stipulated conditions.
B [iii]	STP outlet after stabilization and stack emission shall be monitored monthly. Other environmental parameters and green belt shall be monitored on quarterly basis. After every 3 months, the project proponent shall conduct environmental audit and shall take corrective measure, if required without delay.	Noted
B [iv]	The SEIAA, Haryana reserves the right to add additional safeguard measures subsequently, if found necessary, Environmental Clearance granted will be revoked if it is found the false information has been given for getting approval of this project. SEIAA reserves the right to revoke the clearance if conditions stipulated are not implemented to the satisfaction of SEIAA/MoEF.	Noted
B [v]	The project proponent shall not violate any judicial orders/pronouncements issued by any court/Tribunal.	Noted

For ASF INSIGNIA SEZ PVT. LTD.




Authorized Signatory

B [vi]	All other statutory clearance such as the approvals for storage of diesel from Chief Controller of Explosive, Fire Department, Civil Aviation Department, Forest Conservation Act , 1980 and Wildlife (Protection) Act, 1972 PLPA, 1900, Forest Act 1927 etc shall be obtained, as applicable by project proponent from the respective authorities prior to construction of the project	Ensured Obtained all the approvals required from the competent authorities.
B [vii]	The project proponent should inform the public that the project has been accorded Environment Clearance by the SEIAA and copies of the clearance letter are available with the state pollution control board & SEIAA. This should be advertised within 7 days from the date of issue of the clearance letter at least in two local newspapers that are widely circulated in the region and copy of the same should be forwarded to SEIAA Haryana. A copy of Environmental Clearance conditions shall also be put on project proponent's web site for public awareness.	Complied.
B [viii]	Under the provision of Environment (Protection) Act, 1986, legal action shall be initiated against the project proponent if it was found that construction of the project has been started before obtaining prior Environmental Clearance.	Noted.
B [ix]	Any appeal against the this Environmental Clearance shall lie with the National Green Tribunal, if preferred, within a period of 30 days as prescribed under section 16 of the National Green Tribunal Act,2010.	Noted. <div style="text-align: right;">For ASF INSIGNIA SEZ PVT. LTD.  Authorised Signatory</div>

B [x]	The project proponent shall put in place corporate Environment Policy as mentioned in MoEF, GOI OM No. J-11013/41/2006-IA II (I) dated 26.4.2012 within 3 months period. Latest corporate Environmentally Policy should be submitted to SEIAA within 3 months of issuance of this letter.	Complied
B [xi]	The fund ear-marked for environment protection measures should be kept in separate account and should not be diverted for other purposes and year wise expenditure shall be reported to the SEIAA/RO MoEF GOI under rules prescribed for Environment audit.	Noted.
B [xii]	The project proponent shall ensure the compliance of Forest Department, Haryana Notification no. S.O.121/PA2/1900/S.4/97 dated 28.11.1997	Complied. NOC from the deputy conservator of forest had been obtained vide letter No. 1627-G dated 05-03-2010. The copy of the same was submitted earlier.
B [xiii]	The project proponent shall ensure that no vehicle during construction/operation phase enter the project premises without valid "Pollution Under Control" certificate from competent authority.	Noted
B [xiv]	The project proponent is responsible for compliance of all conditions in Environmental Clearance letter and project proponent cannot absolve himself / herself for the responsibility by shifting it to any contractor engaged by project proponent.	Noted.
B [xv]	The project proponent shall seek fresh environmental clearance if at any stage there is change in the planning of the proposed project.	Noted.

FOR ASF INSIGNIA SEZ PVT. LTD.



Authorized Signatory

STATE ENVIRONMENT IMPACT ASSESSMENT AUTHORITY HARYANA
Bay No. 55-58, Prayatan Bhawan, Sector-2, PANCHKULA.

No. SEIAA/HR/2014/331

Dated: 21-02-2014

To

M/s ASF Insignia SEZ Pvt. Ltd.
(formally known as M/S Canton Buildwell Pvt. Ltd.)
Mr. P.K. Gupta, Senior Vice President,
11, Babar Lane, Bengali market,
New Delhi - 110 001

Subject: Environmental Clearance for Expansion of (phase-II) IT/ Information Technology Enable Services (SEZ) at Village- Gwal Pahari in Sohna Block, District-Gurgaon.

Dear Sir,

This letter is in reference to your application no. CBPL/01/09/001/520 dated 21.03.2011 addressed to M.S. SEIAA, Haryana received on 22.03.2011 and subsequent letters dated 17.08.2012, 22.08.2012, 30.08.2012, 18.09.2012, 23.04.2013 & 09.07.2013 seeking prior Environmental Clearance for the above project under the EIA Notification, 2006. The proposal has been appraised as per prescribed procedure in the light of provisions under the EIA Notification, 2006 on the basis of the mandatory documents enclosed with the application viz., Form-1, Form1-A & Conceptual Plan, EIA/EMP on the basis of approved TOR and additional clarifications furnished in response to the observations of the State Expert Appraisal Committee (SEAC) constituted by MOEF, GOI vide their Notification 23.3.2012, in its meetings held on 20.07.2012, 05.09.2012, 08.04.2013, 06.06.2013 and 26.08.2013 awarded "Gold" grading to the project.

[2] It is inter-alia, noted that the project involves the construction of expansion of (phase-II) IT/ ITES (SEZ) at Village- Gwal Pahari in Sohna Block, District- Gurgaon on a plot area of 192994.58 sqmt (47.698 Acres) Notified by Ministry of Industry and commerce Government of India. The Existing area of Phase-I is 101616.56 sqmt (25.11 Acres) and the proposed Phase-II plot area is 91378.02 sqmt (22.58 Acres). The total built up area after expansion shall be 489390 sqmt (Existing approved area of Phase-I 276249 sqmt + Expansion area of Phase-II 213141 sqmt). The total built up area for the processing zone after expansion shall be 354083 sqmt (Existing phase-I 201409 + proposed Phase-II under Expansion 152674 sqmt). The total built up area for the non-processing zone after expansion shall be 135307 sqmt (Existing phase-I 74840 + proposed Phase-II under Expansion 60467 sqmt). The proposed phase-II project shall have of IT/ITES buildings and commercial building in the processing zone and in the non-processing zone phase-II the project proponent has proposed housing and service

apartment, commercial office amenity and shopping spaces and training center. The maximum height of the building shall be approximately 90 meters. The total water requirement shall be 1843.2 M³/day (Phase-I 965.6 M³/day + 877.6 Phase-II). The fresh water requirement shall be 988.8 M³/day (Phase-I 531.7 M³/day + 457.1 Phase-II) which will be sourced from existing bore wells and permission of competent authority has been obtained. The total waste water generation shall be 949.4 M³/day (Phase-I 482.12 M³/day + 467.3 Phase-II), which will be treated in the 3 STPs of 350 M³/day capacity. The total power requirement shall be 40 MVA (phase-I 19.5 MVA + phase-II 20.5 MVA) which will be supplied by DHBVN through 66 KV grid line from sector-56 of Gurgaon for the connection load sanctioned of 50 MVA. The Project Proponent has proposed to develop 35.15% of project area for tree plantation (20.33%), landscape (9.81%) and water bodies (5.01%). The Project Proponent proposed to construct 40 rain water harvesting pits. The solid waste generation will be 8.3TPD (phase-I 4.3 TPD + phase-II 4TPD). The bio-degradable waste will be treated in the project area by adopting appropriate technology. The total parking spaces proposed are 10100 ECS.

[3] The State Expert Appraisal Committee, Haryana after due consideration of the relevant documents submitted by the project proponent and additional clarification furnished in response to its observations, have recommended the grant of environmental clearance for the project mentioned above, subject to compliance with the stipulated conditions. Accordingly, the State Environment Impact Assessment Authority in its meeting held on 24.01.2014 decided to agree with the recommendations of SEAC to accord necessary environmental clearance for the project under Category 8(b) of EIA Notification 2006 subject to the strict compliance with the specific and general conditions mentioned below:-

PART A-
SPECIFIC CONDITIONS:-
Construction Phase:-

- [1] "Consent for Establish" shall be obtained from Haryana State Pollution Control Board under Air and Water Act and a copy shall be submitted to the SEIAA, Haryana before the start of any construction work at site.
- [2] A first aid room as proposed in the project report shall be provided both during construction and operational phase of the project.
- [3] Adequate drinking water and sanitary facilities shall be provided for construction workers at the site. Provision should be made for mobile toilets. Open defecation by the laboures is strictly prohibited. The safe disposal of waste water and solid wastes generated during the construction phase should be ensured.
- [4] All the topsoil excavated during construction activities shall be stored for use in horticulture/landscape development within the project site.

- [5] The project proponent shall ensure that the building material required during construction phase is properly stored within the project area and disposal of construction waste should not create any adverse effect on the neighboring communities and should be disposed of after taking necessary precautions for general safety and health aspects of people, only in approved sites with the approval of competent authority.
- [6] Construction spoils, including bituminous material and other hazardous materials, must not be allowed to contaminate watercourses and the dump sites for such material must be secured so that they should not leach into the ground water and any hazardous waste generated during construction phase, should be disposed off as per applicable rules and norms with necessary approval of the Haryana State Pollution Control Board.
- [7] The diesel generator sets to be used during construction phase shall be of ultra low sulphur diesel type and should conform to Environment (Protection) Rules prescribed for air and noise emission standards.
- [8] The diesel required for operating DG sets shall be stored in underground tanks and if required, clearance from Chief Controller of Explosives shall be taken.
- [9] Ambient noise levels shall conform to the residential standards both during day and night. Incremental pollution loads on the ambient air and noise quality should be closely monitored during construction phase. Adequate measures should be taken to reduce ambient air pollution and noise level during construction phase, so as to conform to the stipulated residential standards of CPCB/MoEF.
- [10] Fly ash shall be used as building material in the construction as per the provisions of Fly Ash Notification of September 1999 and as amended on 27th August 2003.
- [11] Storm water control and its re-use as per CGWB and BIS standards for various applications should be ensured.
- [12] Water demand during construction shall be reduced by use of pre-mixed concrete, curing agents and other best practices.
- [13] In view of the severe constrains in water supply augmentation in the region and sustainability of water resources, the developer will submit the NOC from CGWA specifying water extraction quantities and assurance from HUDA/ utility provider indicating source of water supply and quantity of water with details of intended use of water – potable and non-potable. Assurance is required for both construction and operation stages separately. It shall be submitted to the SEIAA and RO, MOEF, Chandigarh before the start of construction.
- [14] Roof must meet prescriptive requirement as per Energy Conservation Building Code by using appropriate thermal insulation material.

- [15] Opaque wall must meet prescriptive requirement as per Energy Conservation Building Code which is proposed to be mandatory for all air conditioned spaces while it is desirable for non-air-conditioned spaces by use of appropriate thermal insulation material to fulfill requirement.
- [16] The approval of the competent authority shall be obtained for structural safety of the building on account of earthquake, adequacy of fire fighting equipments, etc. as per National Building Code including protection measures from lightening etc. If any forest land is involved in the proposed site, clearance under Forest Conservation Act shall be obtained from the competent Authority.
- [17] Overexploited groundwater and impending severe shortage of water supply in the region requires the developer to redraw the water and energy conservation plan. Developer shall reduce the overall footprint of the proposed development. Project proponent shall incorporate water efficiency /savings measures as well as water reuse/recycling within 3 months and before start of construction to the SEIAA, Haryana and RO, MOEF, GOI, Chandigarh.
- [18] The Project Proponent as stated in proposal shall construct 40 nos. rain water harvesting pits for recharging the ground water within the project premises. Rain water harvesting pits shall be designed to make provisions for silting chamber and removal of floating matter before entering harvesting pit. Maintenance budget and persons responsible for maintenance must be provided. Care shall also be taken that contaminated water do not enter any RWH pit.
- [19] The project proponent shall provide for adequate fire safety measures and equipments as required by Haryana Fire Service Act, 2009 and instructions issued by the local Authority/Directorate of fire from time to time. Further the project proponent shall take necessary permission regarding fire safety scheme/NOC from competent Authority as required.
- [20] The Project Proponent shall obtain assurance from the DHBVN for supply of 40 MVA of power supply before the start of construction. In no case project will be operational solely on generators without any power supply from any external power utility.
- [21] Detail calculation of power load and ultimate power load of the project shall be submitted to DHBVN under intimation to SEIAA Haryana before the start of construction. Provisions shall be made for electrical infrastructure in the project area.
- [22] The Project Proponent shall not raise any construction in the natural land depression / Nallah/water course and shall ensure that the natural flow from the Nallah/water course is not obstructed.

- [23] The Project Proponent shall keep the plinth level of the building blocks sufficiently above the level of the approach road to the Project. Levels of the other areas in the Projects shall also be kept suitably so as to avoid flooding.
- [24] Construction shall be carried out so that density of population does not exceed norms approved by Director General Town and Country Department Haryana.
- [25] The Project Proponent shall submit an affidavit with the declaration that ground water will not be used for construction and only treated water should be used for construction.
- [26] The project proponent shall not cut any existing tree and project landscaping plan should be modified to include those trees in green area.
- [27] The project proponent shall ensure that ECBC norms for composite climate zone are met. In particular building envelope, HVAC service, water heating, pumping, lighting and electrical infrastructure must meet ECBC norms.
- [28] The Project Proponent shall provide 3 meter high barricade around the project area, dust screen for every floor above the ground, proper sprinkling and covering of stored material to restrict dust and air pollution during construction.
- [29] The project proponent shall construct a sedimentation basin in the lower level of the project site to trap pollutant and other wastes during rains.
- [30] The project proponent shall provide proper rasta of proper width and proper strength for the project before the start of construction.
- [31] The project proponent shall ensure that the U-value of the glass is less than 3.177 and maximum solar heat gain co-efficient is 0.25 for vertical fenestration.
- [32] The project proponent shall adequately control construction dusts like silica dust, non-silica dust, wood dust. Such dusts shall not spread outside project premises. Project Proponent shall provide respiratory protective equipment to all construction workers.
- [33] The project proponent shall provide one refuse area till 24 meter, one till 39 meter and one each after 15 meter as per National Building Code. The project proponent shall not convert any refuse area in the habitable space and it should not be sold out/commercialized.
- [34] The project proponent shall provide fire control room and fire officer for building above 30 meter as per National Building Code.
- [35] The project proponent shall obtain permission of Mines and Geology Department for excavation of soil before the start of construction.
- [36] The project proponent shall seek specific prior approval from concerned local Authority/HUDA regarding provision of storm drainage and sewerage system including their integration with external services of HUDA/ Local authorities beside other required services before taking up any construction activity.

- [37] The site for solid waste management plant be earmarked on the layout plan and the detailed project for setting up the solid waste management plant shall be submitted to the Authority within one month.
- [38] Vertical fenestration shall not exceed 40% of total wall area.
- [39] The project proponent shall discharge excess of treated waste water/storm water in the public drainage system and shall seek permission of HUDA before the start of construction.
- [40] The project proponent shall seek NOC from Town and Country department regarding height of the building allowed in the skyline of that area.
- [41] The project proponent shall ensure that structural stability to withstand earthquake of magnitude 8.5 on Richter scale.
- [42] The project proponent shall ensure that no construction activity is undertaken either on surface or below or above surface of revenue rasta passing through the project area.
- [43] The project proponent shall indicate the width and length of revenue rasta passing through the project area on sign board and shall display the same at both the ends of revenue rasta stretch, for awareness of public. Sign board shall also display the message that this is public rasta/road and any citizen can use it. There shall not be any gate with or without guards on revenue rasta further project proponent shall not encroach revenue rasta and shall not cross internal roads over revenue rasta.
- [44] The project proponent shall ensure that natural flow of existing nallah is never obstructed and shall seek NOC from Irrigation Department regarding this before the start of the construction.
- [45] The project proponent shall ensure that in case of excessive flow of water in, nallah, the structural integrity of buildings along-side the nallah is not breached in any circumstances.
- [46] The project proponent shall ensure that there should not be any water logging on the bed of nallah even in case of excessive rain.
- [47] The project proponent shall ensure that sewerage pipe line should not cross over the nallah and project proponent shall maintain separate STP in the plot area across the nallah.
- [48] The project proponent shall ensure that sewerage system and storm drainage system shall be planned by taking into account the natural slope of original land and approval from HUDA and Irrigation department shall be taken before the start of construction.

- [49] The project proponent shall ensure that bed of nallah is not encroached in any manner, while constructing the culvert over the nallah.
- [50] The project proponent shall ensure plinth level of the building block is 1.5 meter above 100 years flood level.
- [51] The project proponent shall provide pervious surface instead of impervious and hard surface in order to reduce overflow of water in nallah.
- [52] The project proponent shall ensure proper drainage in the project area as the project area is uneven and undiluted.

Operational Phase:

- [a] "Consent to Operate" shall be obtained from Haryana State Pollution Control Board under Air and Water Act and a copy shall be submitted to the SEIAA, Haryana.
- [b] The Sewage Treatment Plant (STP) shall be installed for the treatment of the sewage to the prescribed standards including odour and treated effluent will be recycled to achieve zero exit discharge. The installation of STP shall be certified by an independent expert and a report in this regard shall be submitted to the SEIAA, Haryana before the project is commissioned for operation. Tertiary treatment of waste water is mandatory. The project proponent shall remove not only Ortho-Phosphorus but total Phosphorus to the extent of less than 2mg/liter. Similarly total Nitrogen level shall be less than 2mg/liter in tertiary treated waste water. Discharge of treated sewage shall conform to the norms and standards of CPCB/ HSPCB, whichever is environmentally better. Project Proponent shall implement such STP technology which does not require filter backwash.
- [c] Separation of the grey and black water should be done by the use of dual plumbing line. Treatment of 100% grey water by decentralized treatment should be done ensuring that the re-circulated water should have BOD level less than 5 mg/litre and the recycled water will be used for flushing, gardening and DG set cooling etc.
- [d] For disinfection of the treated wastewater ultra-violet radiation or ozonization process should be used.
- [e] Diesel power generating sets proposed as source of back-up power for lifts, common area illumination and for domestic use should be of enclosed type and conform to rules made under the Environment (Protection) Act, 1986. The location of the DG sets shall be in the basement as promised by the project proponent with appropriate stack height above the highest roof level of the project, as per the CPCB norms. The diesel used for DG sets shall be ultra low sulphur diesel (35ppm sulphur), instead of low sulphur diesel.

- [f] Ambient Noise level should be controlled to ensure that it does not exceed the prescribed standards both within and at the boundary of the Proposed IT/ITES Project.
- [g] The project proponent as stated in the proposal shall maintain at least 35.15% as green cover area for tree plantation especially all around the periphery of the project and on the road sides preferably with local species which can provide protection against noise and suspended particulate matter. The open spaces inside the project shall be preferably landscaped and covered with vegetation/grass, herbs & shrubs. Only locally available plant species shall be used.
- [h] The project proponent shall strive to minimize water in irrigation of landscape by minimizing grass area, using native variety, xeriscaping and mulching, utilizing efficient irrigation system, scheduling irrigation only after checking evapo-transpiration data.
- [i] Rain water harvesting for roof run-off and surface run-off, as per plan submitted should be implemented. Before recharging the surface run off, pre-treatment through sedimentation tanks must be done to remove suspended matter, oil and grease. The bore well for rainwater recharging shall be kept at least 5 mts. above the highest ground water table. Care shall be taken that contaminated water do not enter any RWH pit. The project proponent shall avoid Rain Water Harvesting of first 10 minutes of rain fall. Roof top of the building shall be without any toxic material or paint which can contaminate rain water. Wire mesh and filters should be used wherever required.
- [j] The ground water level and its quality should be monitored regularly in consultation with Central Ground Water Authority.
- [k] A report on the energy conservation measures conforming to energy conservation norms finalized by Bureau of Energy Efficiency should be prepared incorporating details about building materials & technology, R & U Factors etc and submitted to the SEIAA, Haryana in three months time.
- [l] Energy conservation measures like installation of LED only for lighting the areas outside the building and inside the building should be integral part of the project design and should be in place before project commissioning. Use of solar panels must be adapted to the maximum energy conservation.
- [m] The Project Proponent shall use zero ozone depleting potential material in insulation, refrigeration, air-conditioning and adhesive. Project Proponent shall also provide halon free fire suppression system.
- [n] The solid waste generated should be properly collected and segregated as per the requirement of the MSW Rules, 2000 and as amended from time to time. The bio-degradable waste should be treated by appropriate technology at the site ear-marked

within the project area and dry/inert solid waste should be disposed off to the approved sites for land filling after recovering recyclable material.

- [o] The provision of the solar water heating system shall be as per norms specified by HAREDA and shall be made operational in each building block.
- [p] The traffic plan and the parking plan proposed by the Project Proponent should be meticulously adhered to with further scope of additional parking for future requirement. There should be no traffic congestion near the entry and exit points from the roads adjoining the proposed project site. Parking should be fully internalized and no public space should be used.
- [q] The Project shall be operationalized only when HUDA/local authority will provide domestic water supply system in the area.
- [r] Operation and maintenance of STP, solid waste management and electrical Infrastructure, pollution control measures shall be ensured even after the completion of project.
- [s] Different type of wastes should be disposed off as per provisions of municipal solid waste, biomedical waste, hazardous waste, e-waste, batteries & plastic rules made under Environment Protection Act, 1986. Particularly E-waste and Battery waste shall be disposed of as per existing E-waste Management Rules 2011 and Batteries Management Rules 2001. The project proponent shall maintain a collection center for E-waste and it shall be disposed of to only registered and authorized dismantler / recycler as per existing E-waste Management Rules 2011.
- [t] Standards for discharge of environmental pollutants as enshrined in various schedules of rule 3 of Environment Protection Rule 1986 shall be strictly complied with.
- [u] The project proponent shall make provision for guard pond and other provisions for safety against failure in the operation of wastewater treatment facilities. The project proponent shall also identify acceptable outfall for treated effluent.
- [v] The project proponent shall ensure that the stack height of DG sets is as per the CPCB guide lines and also ensure that the emission standards of noise and air are within the CPCB latest prescribed limits. Noise and Emission level of DG sets greater than 800 KVA shall be as per CPCB latest standards for high capacity DG sets.
- [w] All electric supply exceeding 100 amp, 3 phase shall maintain the power factor between 0.98 lag to 1 at the point of connection.
- [x] The project proponent shall minimize heat island effect through shading and reflective or pervious surface instead of hard surface.
- [y] The project proponent shall use only treated water instead of fresh water for HVAC and DG cooling. The Project Proponent shall also use evaporative cooling

technology and double stage cooling system for HVAC in order to reduce water consumption. Further temperature, relative humidity during summer and winter seasons should be kept at optimal level. Variable speed drive, best Co-efficient of Performance (CoP), as well as optimal Integrated Point Load Value and minimum outside fresh air supply may be resorted for conservation of power and water. Coil type cooling DG Sets shall be used for saving cooling water consumption for water cooled DG Sets.

- [z] The project proponent shall ensure that the transformer is constructed with high quality grain oriented, low loss silicon steel and virgin electrolyte grade copper. The project proponent shall obtain manufacturer's certificate also for that.
- [aa] Water supply shall be metered among different users and different utilities.
- [ab] The project proponent shall ensure that exit velocity from the stack should be sufficiently high. Stack shall be designed in such a way that there is no stack down-wash under any meteorological conditions.
- [ac] The project proponent shall provide water sprinkling system in the project area to suppress the dust in addition to the already suggested mitigation measures in the Air Environment Chapter of EMP.
- [ad] The project proponent shall ensure proper Air Ventilation and light system in the basements area for comfortable living of human being and shall ensure that number of Air Changes per hour/(ACH) in basement never falls below 15. In case of emergency capacity for increasing ACH to the extent of 30 must be provided by the project proponent.
- [ae] The project proponent shall get the inspection of nallah before the onset of monsoon season every year from Irrigation Department.
- [af] The project proponent shall not discharge untreated water in the nallah and also shall not throw any solid waste in the nallah.

PART-B. GENERAL CONDITIONS:

- [i] The Project Proponent shall ensure the commitments made in Form-1, Form-1A, EIA/EMP and other documents submitted to the SEIAA for the protection of environment and proposed environmental safeguards are complied with in letter and spirit. In case of contradiction between two or more documents on any point, the most environmentally friendly commitment on the point shall be taken as commitment by project proponent.
- [ii] The project proponent shall also submit six monthly reports on the status of compliance of the stipulated EC conditions including results of monitored data (both in hard copies as well as by e-mail) to the northern Regional Office of MoEF, the respective Zonal Office of CPCB, HSPCB and SEIAA Haryana.

- [iii] STP outlet after-stabilization and stack emission shall be monitored monthly. Other environmental parameters and green belt shall be monitored on quarterly basis. After every 3 (three) months, the project proponent shall conduct environmental audit and shall take corrective measure, if required, without delay.
- [iv] The SEIAA, Haryana reserves the right to add additional safeguard measures subsequently, if found necessary. Environmental Clearance granted will be revoked if it is found that false information has been given for getting approval of this project. SEIAA reserves the right to revoke the clearance if conditions stipulated are not implemented to the satisfaction of SEIAA/MoEF.
- [v] The Project proponent shall not violate any judicial orders/pronouncements issued by any Court/Tribunal.
- [vi] All other statutory clearances such as the approvals for storage of diesel from Chief Controller of Explosives, Fire Department, Civil Aviation Department, Forest Conservation Act, 1980 and Wildlife (Protection) Act, 1972, Forest Act, 1927, PLPA 1900, etc. shall be obtained, as applicable by project proponents from the respective authorities prior to construction of the project.
- [vii] The Project proponent should inform the public that the project has been accorded Environment Clearance by the SEIAA and copies of the clearance letter are available with the Haryana State Pollution Control Board & SEIAA. This should be advertised within 7 days from the date of issue of the clearance letter at least in two local newspapers that are widely circulated in the region and the copy of the same should be forwarded to SEIAA Haryana. A copy of Environment Clearance conditions shall also be put on project proponent's web site for public awareness.
- [viii] Under the provisions of Environment (Protection) Act, 1986, legal action shall be initiated against the Project Proponent if it was found that construction of the project has been started before obtaining prior Environmental Clearance.
- [ix] Any appeal against the this Environmental Clearance shall lie with the National Green Tribunal, if preferred, within a period of 30 days as prescribed under Section 16 of the National Green Tribunal Act, 2010.
- [x] The project proponent shall put in place Corporate Environment Policy as mentioned in MoEF, GoI OM No. J-11013/41/2006-IA II (I) dated 26.4.2012 within 3 months period. Latest Corporate Environment Policy should be submitted to SEIAA within 3 months of issuance of this letter.
- [xi] The fund ear-marked for environment protection measures should be kept in separate account and should not be diverted for other purposes and year wise expenditure shall be reported to the SEIAA/RO MoEF, GoI under rules prescribed for Environment Audit.
- [xii] The project proponent shall ensure the compliance of Forest Department, Haryana Notification no. S.O.121/PA2/1900/S.4/97 dated 28.11.1997.

- [xiii] The Project Proponent shall ensure that no vehicle during construction/operation phase enter the project premises without valid 'Pollution Under Control' certificate from competent Authority.
- [xiv] The project proponent is responsible for compliance of all conditions in Environmental Clearance letter and project proponent can not absolve himself /herself of the responsibility by shifting it to any contractor engaged by project proponent.
- [xv] The project proponent shall seek fresh Environmental clearance if at any stage there is change in the planning of the proposed project.
- [xvi] The proponent shall upload the status of compliance of the stipulated EC conditions, including results of monitored data on their website and shall update the same periodically. It shall simultaneously be sent to the Regional Office of MoEF, the respective Zonal Office of CPCB and the SPCB. The criteria pollutant levels namely; PM_{2.5}, PM₁₀, SO_x NO_x, Ozone, Lead, CO, Benzene, Ammonia, Benzopyrine, arsenic and Nickel. (Ambient levels as well as stack emissions) or critical sectoral parameters, indicated for the project shall be monitored and displayed at a convenient location near the main gate of the company in the public domain.
- [xvii] The environmental statement for each financial year ending 31st March in Form-V as is mandated to be submitted by the project proponent to the HSPCB Panchkula as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company along with the status of compliance of the EC conditions and shall also be sent to the respective Regional Offices of MoEF by e-mail.
- [xviii] The project proponent shall conduct environment audit at every three months interval and thereafter corrected measures shall be taken without any delay. Details of environmental audit and corrective measures shall be submitted in the monitoring report.

rajiv rajan
Member Secretary,
State Level Environment Impact
Assessment Authority, Haryana, Panchkula.

Endst. No. SEIAA/HR/2013

Dated:.....
DB

A copy of the above is forwarded to the following:

1. The Additional Director (IA Division), MOEF, GOI, CGO Complex, Lodhi Road, New Delhi.
2. The Regional office, Ministry of Environment & Forests, Govt. of India, Sector 31, Chandigarh.
3. The Chairman, Haryana State Pollution Control Board, Pkl.

Member Secretary,
State Level Environment Impact
Assessment Authority, Haryana, Panchkula

State Environment Impact Assessment Authority, Haryana,
Bays No.55-58, Prayatan Bhawan, Sector-2 Panchkula.

Telephone No. 0172-2565232

Memo No: SEIAA/HR/2019/201

Date: 22.07.19

To


M/s ASF Insignia SEZ Pvt Ltd,
11, Babarlane, Bengali Market,
New Delhi- 110001

Subject:- Amendment in Environmental Clearance for expansion of (phase-II) IT/information Technology Enable Services(SEZ) at village-Gwal Pahari in Sohna block, District Gurgaon Haryana.

Please refer to your application dated,01.03.2019 submitted for seeking amendment in EC granted for expansion of (phase-II) IT/Information Technology Enable Services (SEZ) at village-Gwal Pahari in Sohna block, District Gurgaon Haryana vide SEIAA/HR/2014/331 dated 21.02.2014.

Your application was considered by SEAC in its 178th meeting held on 11.04.2019 and recommended to SEIAA for amendment with a total built up area of 792209.65 sq. mtrs in EC letter no. SEIAA/HR/2014/331 dated 21.02.2014 (including already approved area of 489390 sq. mtrs + an area of 302819.65 sq. mtrs pertaining to basements).

Recommendations of SEAC was considered in 118th meeting of SEIAA held on 12.06.2019 and Authority decided to agree with the recommendation of SEAC and allow the amendment of Environment Clearance letter subject to compliance of the conditions already imposed in the Environment Clearance letter dated 21.02.2014.


Chairman, SEIAA
Haryana

STATE ENVIRONMENT IMPACT ASSESSMENT AUTHORITY HARYANA
 Bay No. 55-58, Prayatan Bhawan, Sector-2, PANCHKULA.

Tel: 0172-2565232

E-mail Id: seiaa.hry@gmail.com

No. SELAA(125)/HR/2021/254

Dated: 04/03/2021

To

**M/s ASF Insignia SEZ Pvt. Ltd,
 # 11, Babar lane, Bengali Market,
 New Delhi- 110001**

Subject: Amendment in Environment Clearance for "ASF Insignia IT/ITES (SEZ)" project located at Village Gwal Pahari, Tehsil - Wazirabad, District Gurugram, Haryana.

[1] This letter is in reference to your application dated 09.07.2020 addressed to Member Secretary, SELAA, Haryana received on 14.07.2020 and subsequent letter dated 30.08.2020 seeking prior Amendment in Environmental Clearance for the above project under the EIA Notification, 2006. The proposal has been appraised as per prescribed procedure in the light of provisions under the EIA Notification, 2006 on the basis of the mandatory documents enclosed with the application viz., Form-4 and additional clarifications furnished in response to the observations of the State Expert Appraisal Committee (SEAC) constituted by MoEF & CC, GoI vide their Notification dated 30.01.2019, in its meetings held on 30.08.2020.

[2] It is inter-alia, noted that the project involves "ASF insignia IT/ITES (SEZ)" project located at Village Gwal Pahari, Tehsil-Wazirabad, District Gurugram, Haryana. The details of the project as given below:

Sr. No.	Particulars	Existing/ Phase I	Expansion/ Phase II	Total	Amended
Online Project Proposal Number		SIA/HR/MIS/162790/2020			
1.	Waste Water Generated (KLD)	482.12	467.3	949.42	1901.56 (80% of fresh water + 100 % of Flushing + Blow Down of Cooling Tower of HAVC + Filter Backwash Water)
2.	STP Capacity (KLD)	1050 (3 X 350)			2300

[3] The State Expert Appraisal Committee, Haryana after due consideration of the relevant documents submitted by the project proponent and additional clarification furnished in response to its observations, have recommended the grant of amendment in environmental clearance for the project mentioned above, subject to no pollution load shall be increased due to

the amendment. Accordingly, the State Environment Impact Assessment Authority in its 125th meeting held on 07.10.2020 decided to agree with the recommendations of SEAC to accord necessary amendment in earlier Environmental Clearance for the project under Category 8(a) of EIA Notification 2006 with strict compliance of the stipulations imposed in earlier granted Environment Clearance vide letter No. SEIAA/HR/2014/331 dated 21.02.2014 & amendment thereto vide letter no. SEIAA/HR/2019/201 dated 22.07.2019 along-with the following additional stipulations:-

1. No pollution load shall be increased due to the amendment.
2. "Zero Liquid Discharge" would be achieved and will install all the necessary equipment to treat the residual water".



Chairman,
State Level Environment Impact
Assessment Authority, Haryana, Panchkula.

Endst. No. SEIAA(125)/HR/2021/

Dated: ____/03/2021

A copy of the above is forwarded to the following:

1. Director (IA Division), MoEF & CC, GoI, Indra Paryavaran Bhavan, Zor bagh Road- New Delhi-110003.
2. Regional office, Ministry of Environment, Forests & Climate Change, Govt. of India, Bay's no. 24-25, Sector 31-A, Dakshin Marg, Chandigarh-160018.
3. Chairman, Haryana State Pollution Control Board, C-11, Sector-6, Panchkula.
4. Director General, Town & Country Planning Haryana, Plot No. 3, Sector - 18A, Madhya Marg, Chandigarh- 160018.
5. Concerned File/ Office Copy

- sd -
Chairman,

State Level Environment Impact
Assessment Authority, Haryana, Panchkula.

State Environment Impact Assessment Authority, Haryana,
Bays No.55-58, Prayatan Bhawan, Sector-2 Panchkula.

Telephone No. 0172-2565232
E-mail ID: seiaa.hry@gmail.com

Memo No: SEIAA/HR/2021/465

Date: 11/05/2021

To

M/s ASF Insignia SEZ Private Limited,
11, Babar Lane, Bengali Market,
New Delhi-110001

Subject: Extension of validity of Environment Clearance for "ASF Insignia IT/ITES (SEZ)" project located at Village Gwali Pahari, Tehsil-Wazirabad, District Gurugram, Haryana.


With reference to your application No. Nil dated 18.03.2021 received in this office on 26.03.2021 for seeking Extension of Validity of Environment Clearance granted for "ASF Insignia IT/ITES (SEZ)" project located at Village Gwali Pahari, Tehsil-Wazirabad, District Gurugram, Haryana vide letter dated 21.02.2014. The Validity of your Environment Clearance was up to 20.02.2021 as per MoEF & CC, GoI dated 14.09.2006 & its subsequent Amendment dated 29.04.2015 & 14.09.2016. whereas, due to COVID-19 pandemic the validity of EC was automatically extended for six month from the date of expiry of validity i.e. 20.08.2021 vide MOEF & CC, GOI Notification No. S.O.4254 (E) dated 27.11.2020.

The case was examined in the light of MoEF & CC, GoI Amended Notification dated 14.09.2016 & its subsequent amendment Notification dated 27.11.2020.

Keeping in view of above, the Authority decided to grant Extension for Validity of Environment Clearance for further 3 years from the date of expiry of validity of earlier EC subject to compliance of the conditions already imposed in the Environmental Clearance letter dated 21.02.2014 granted by SEIAA, Haryana.

Chairman,
SEIAA, Haryana.

First Aid Room at Construction site

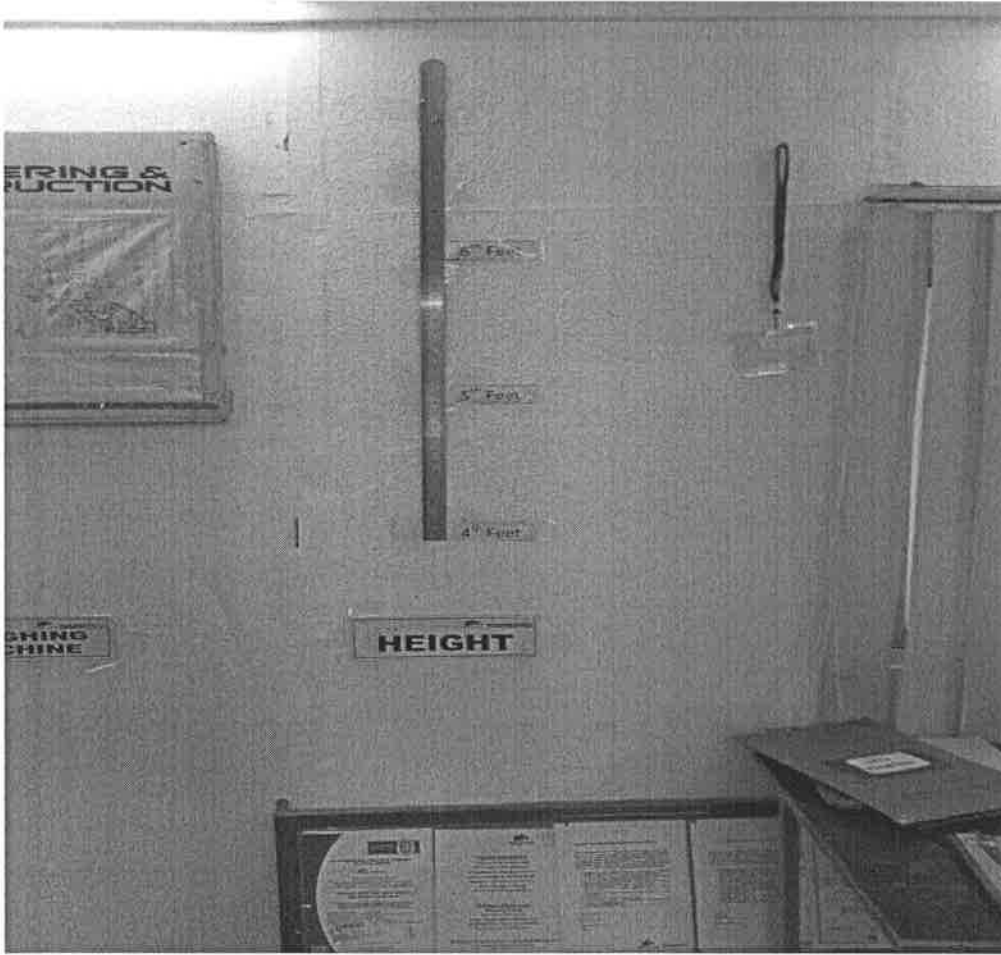

First Aid Room at Construction site





o/c

ANNEXURE - III

03.04.2024

To,

The Regional Officer,
Haryana State Pollution Control Board
Gurgaon

Sub.: Submission of Form - IV for the period 01.04.2023 to 31.03.2024 -
Annual Return.

Dear Sir,

We are enclosing herewith Form – IV for the period from 01.04.2023 to 31.03.2024 i.e. Annual Return for Hazardous Wastes for the financial year 2023 to 2024 for our site at Village Gwal Pahari, Tehsil Wazirabad Distt. Gurgaon (Haryana).

Thanking you,
Yours faithfully,

For ASF INSIGNIA SEZ PVT. LTD.

Authorized Signatory

Encl: AS Above

CC: The Chairman
Haryana State Pollution Control Board,
C-11, Sector-6, Panchkula

ED638501483IN IVR:6968638501483
SP PATPARGANJ 60 (110091)
Counter No:1, 19/04/2024, 09:38
To: REGIONAL OFFICER,
PIN:122001, Gurgaon HD
From: ASF INSIGNIA SEZ CENTRE (GWD)
Wt: 75gms
Art: 29.50 (Cash/Tax): 4.50
(Track on www.indiapost.gov.in)
(Dial: 18002666666) Clear Marks, Stay Safe!

ED638501483IN IVR:6968638501483
SP PATPARGANJ 60 (110091)
Counter No:1, 19/04/2024, 09:38
To: HARYANA STATE, D-11
PIN:134109, Panchkula Sector B 5, D
From: ASF INSIGNIA SEZ CENTRE (GWD)
Wt: 75gms
Art: 47.20 (Cash/Tax): 7.20
(Track on www.indiapost.gov.in)
(Dial: 18002666666) Clear Marks, Stay Safe!

ASF INSIGNIA SEZ PRIVATE LIMITED

Site Office: ASF Insignia SEZ (IT/ITES), Vatsal Valley (Gwal Pahari), off Gurugram-Faridabad Road, Gurugram-122003, Haryana

E: +91 124 4777200 | +91 124 4234110 | corporate@asfinfrastructure.com | www.asfinfrastructure.com

Regd. Office: 11, Beber Lane, Bengali Market, New Delhi-110001 | +91 11 23355511 | +91 1123739298

Corp. Office: ASF Centre, 362-363, Udyog Vihar, Phase-IV, Gurugram-122016 (India)

CIN U45201DL2005PTC140408


Creating Intelligent Spaces®



FORM 4*[See rules 5(6) and 22 (2)]***FORM FOR FILING ANNUAL RETURNS
BY THE OCCUPIER OR OPERATOR OF FACILITY
For the period from 1st April, 2023 to 31st March, 2024**

[To be submitted by occupier/operator of disposal facility to State Pollution Control Board/
Pollution Control Committee by 30th June of every year for the preceding period April to March]

1.	Name and address of the generator/ operator of facility	:	ASF Insignia SEZ Private Limited Village Gwal Pahari, Sub-Tehsil Wazirabad Distt. Gurgaon, Haryana				
2.	Name of the authorized person and full address with telephone and fax number	:	Shri Anil Sharma ASF Center Plot No.362-363, Gate No.4, Udyog Vihar , Phase IV, Gurgaon, Haryana. Tel. No. : 0124-4777205 Fax. No. : 0124-4234110				
3.	Description of hazardous waste	of	:	Physical form with description	Chemical form		
				Used Lube Oil generated from Generator Sets			
4.	Quantity of hazardous (in MTA)	:	Type of hazardous waste	Quantity (in Tonnes/KL)			
			Used Oil (Haz. Waste Category: 5.1)	3.080			
5.	Description of Storage	:	Stored in closed labeled PVC drums in designated area with concrete flooring				
6.	Description of Treatment	of	:	None			
7.	Details of transportation	:	Name & address of consignee	Mode of packing	Mode of transportation	Date of transportation	
			M/s. Shiv Shakti Oil & Lubricants F-557; RIICO Ind. Area Chopanki , Post Tapukara, Tehsil- Tizara, Distt- Alwar-301017, Rajasthan	Closed Drums	RJ40GA2066	02.11.2023	
8.	Details of disposal of hazardous waste	:	Name & address of consignee	Mode of packing	Mode of transportation	Date of transportation	



		Given to approved vendor/recycler (M/s. Shiv Shakti Oil & Lubricants)			
9.	Quantity of useful materials sent back to the manufacturers* and others#	:	Name and type of Quantity in Tonnes/KL material sent back to		
			Manufacturers*	Nil	
			Others# (Used Oil)	3.080 KL (M/s Shiv Shakti Oil & Lubricants)	

* delete whichever is not applicable# enclose list of other agencies



Signature
 Designation : Anil Sharma -Vice President (Projects)
 Date.. : 1st April 2024
 Place : Gurgaon, Haryana



Date: 06.11.2023

The Regional Office
Haryana State Pollution Control Board
Gurgaon, Haryana

Sub.: Disposal of used Oil with Drum (Hazardous Waste) M/S Shiv Shakti Oil Lubricants - F 557; RIICO Ind, Area Chopanki P.O. Tapokara, Tehsil Tizara, Distt. Alwar (Rajasthan) PIN. 301017

Dear Sir,

We have sent 3080 liters of Used lube oil with Drum (Hazardous Liquid Waste) to M/S Shiv Shakti Oil Lubricants - F 557; RIICO Ind, Area Chopanki P.O. Tapokara, Tehsil Tizara, Distt. Alwar (Rajasthan) PIN. 301017 and enclosing herewith copies of the following relevant documents for your records:-

- 1) Invoice No. 001023500002 Dated. 02.11.2023
- 2) Bill of Entry No. 2000030 Dated. 04.10.2023
- 3) Form-10 [See Rule 19 (1)]
- 4) E-way bill No. 3916 8121 5046 Dated. 02.11.2023 01:51 PM
- 5) Registration certificate-cum-Pass Book
- 6) Gate Pass No. 34 Dated. 02.11.2023

Thanking you,
Yours faithfully,

For ASF INSIGNIA SEZ PVT. LTD.



AUTHORISED SIGNATORY

Encl. As above

Su
21/11/23
Encl: Sande-p

ASF INSIGNIA SEZ PRIVATE LIMITED

Site Office : ASF Insignia SEZ (IT/ITES), Vatsal Valley (Gwal Pahari), off Gurugram-Faridabad Road, Gurugram-122003, Haryana

T: +91 124 4777200 F: +91 124 4234110 E: corporate@asfinfrastructure.com W: www.asfinfrastructure.com

Regd. Office : 11, Beber Lane, Bengali Market, New Delhi-110001 U: +91 11 23355511 F: +91 1123739298

Corp. Office : ASF Centre, 352-353, Udyog Vihar, Phase-IV, Gurugram-122016 (India)

CIN U45201DL2005PTC140408

Creating the intelligent Spaces



GOODS/MATERIAL GATE PASS



ASF INSIGNIA SEZ PRIVATE LIMITED

VILL. GWAL PAHARI, SUB TEHSIL WAZIRABAD, DISTT. GURUGRAM-122003 (HR.)

GST No. : 06AACCC7148L1ZG

231

GATE PASS NO. : 34

DATE 02/11/2023

TIME

TO

M/s. Shiv Stechiol & Lubricants,
F-57, KMO Ind. Area,
Rohtak

RETURNABLE

NON RETURNABLE

MODE OF TRANSPORT

VEHICLE NO.

RJ4067A/2066

Sl. No.	DESCRIPTION OF GOODS/MATERIAL	UNIT	QTY	REMARKS
01	Disposal of Used oil with Drum (14 Drum X 220 Ltr)	Ltr	3080	/
	Bo No → 200030 dt 04/10/22			
	Inv No → 00/023500002 dt. 02/11/2023			
	Rs. 80098.36/-			
	eway → 391681215046, 02/11/23			
		Ltr	3080	

PREPARED BY (SIGN & NAME)

AUTHORISED SIGNATORY



Tax Invoice

Supplier Company ASF INSIGNIA SEZ PRIVATE LIMITED ASF INSIGNIA SEZ ITeS,Village GwalPahariGurgaon Faridabad Road District - SubTeh Wazirabad, Gurgaon PinCode - 122003 GSTIN - 06AACCC7148L1ZG Place of Supply,Haryana Name of State (State Code):Haryana(07)		Invoice No:001023500002 SAP Document Number.91300250 Date of Issue: 02.11.2023 Vehicle No: RJ40GA-2066				
Recipient: SHIV SHAKTI OIL & LUBRICANTS F-557, RIICO Ind. Area Chopanki, post Tapokara, TizaraAlwar 301017 GSTIN - 08ABFFS4464G1ZZ Whether TAX is Payable on Reverse Charge - No		Order No. Date Permission No.91600159 Dated 30.10.2023 Delivery: 91700281 Buyer (if other than consignee) Same As Consignee				
Mark/Nos./Kind of packages	Description of goods	HSN / SAC	Quantity	UOM	Rate Rs.	Amount Rs.
1	Disposal of Used Oil with Drum	27109900	3,080.000	L	20.89	64,341.20
N. Wt:	0.000 KG					
G. Wt:	0.000 KG					
TOTAL			3,080.000			64,341.20
	BCD			5.00 %		3,217.06
	SWS			10.00 %		321.71
	CGST					
	SGST					
	IGST			18.00 %		12,218.39
	Net Invoice Value					80,098.36
Total: RUPEES EIGHTY THOUSAND NINETY EIGHT Rupees THIRTY SIX Paise ONLY.						
We certify that the above particulars are true & correct.				For ASF INSIGNIA SEZ PVT LTD For ASF Insignia SEZ Pvt. Ltd. Signature / DSC Authorised Signatory		

ASF Insignia SEZ Pvt. Ltd.
INWARD/ OUTWARD ENTRY

SI No.....237.....

Time In.....

Time Out.....14:30.....

Date.....02.11.2023.....

Sign. /Security).....[Signature].....



FORM 10

[See Rule 19 (1)]

MANIFEST FOR HAZARDOUS AND OTHER WASTE

273

1	Sender's name and mailing address (including Phone no. and e-mail)	ASF Insignia SEZ Pvt. Ltd Gurgaon-Faridabad Road, Vill. Gwal Pahari, Teh-Sohna District Gurgaon (Haryana)			
2	Sender's Authorisation No.				
3	Manifest Documents No.	SSOL / HW / 01 / 2023.24 / ASE..... / Dt. 02.11.23			
4	Transporter's name and address: (including Phone No. and e-mail)	M/s. Shiv Shakti Oil & Lubricants,			
5	Type of vehicle	(Truck/Tankers/Special Vehicle) ✓			
6	Transporter's registration No.	Self			
7	Vehicle registration No.	RJ.40 GA - 2066			
8	Receiver's name and mailing address (including Phone No. and e-mail)	SHIV SHAKTI OIL & LUBRICANTS F-557 & F-693 (Unit 3), RIICO Industrial Area Chopanki, Post: Tapukara Teh. Tijara, Distt. Alwar - 301707 (Rajasthan) INDIA Ph.: +91-9310003339, 9350003339 E: shivshakti_lub07@yahoo.co.in			
9	Receiver's Authorisation No.	RSPCB / HWM / 20 23-20 24 / HSW / HSW / 08 RSPCB / HWM / 20 19-20 20 / HSW / HSW / 106 (Unit 3)			
10	Waste description	<input checked="" type="checkbox"/> Used Lube Oil, Used Cutting Coolant Oil (Cat. 5.1) ✓ <input checked="" type="checkbox"/> Used Hydraulic Oil, Used Transformer Oil (Cat. 5.2) X <input checked="" type="checkbox"/> Waste or Residues Containing Oil (Cat. 33.1) (Unit-3) ✓ <input checked="" type="checkbox"/> Containers/ Barrels/ Drums Contaminated with Hazardous Wastes/ Chemicals			
11	Total quantity No. of Containers 3020 LTR m ³ or MT 54 Nos.			
12	Physical form	<input checked="" type="checkbox"/> Solid/Semi-Solid/Sludge) <input checked="" type="checkbox"/> OILY / Tarry / Slurry / Liquid			
13	Special handling instructions and additional information	Disposed/ sale as per Precautions/ Rules of Central Pollution Control Board/ MOEF/ SPCB to the Authorized Reg. Re-recycler/ Re-reprocessor (Handle with Care)			
14	Sender's Certificate	I hereby declare that the contents of the consignment are fully and accurately described above by proper shipping name and are categorised, packed, marked, and labelled and are in all respects in proper condition for transport by road according to applicable national government regulations.			
	Name & stamp:	Signature	Month	Day	Year
			11	02	2023
15	Transporter acknowledgement of receipt of Wastes				
	Name & stamp:	Signature	Month	Day	Year
			11	02	2023
16	Receiver's certification for receipt of hazardous and other waste				
	Name & stamp:	Signature	Month	Day	Year
			11	02	2023

COPY 1 of 7

White Copy To be forwarded by the sender to the State Pollution Control Board





e-Way Bill

1 E-WAY BILL Details

eWay Bill No: 3916 8121 5046

Generated Date: 02/11/2023 01:51 PM

Generated By: 06AAC CC714 8L1ZG

Valid Upto: 03/11/2023

Mode: Road

Approx Distance: 42km

Type: Outward - Supply

Document Details: Tax Invoice - 1023500002 - 02/11/2023

Transaction type: Regular

2. Address Details

From

GSTIN: 06AAC CC714 8L1ZG
ASF INSIGNIA SEZ PVT LTD
OTHER COUNTRIES

:: Dispatch From ::

GAWALPAHARI
FARIDABAD ROAD GURGRAM
Gurugram, HARYANA-122001

To

GSTIN: 08ABF FS446 4G1ZZ
SHIV SHAKTI OIL & LUBRICANTS
RAJASTHAN

:: Ship To ::

F.357
CHOPANKI INDUSTRIAL AREA
CHOPANKI, BHIWADI, RAJASTHAN-301019

3. Goods Details

HSN Code	Product Name & Desc.	Quantity	Taxable Amount Rs.	Tax Rate (C+B+H+Cess+Cess Non.Advol)
27109900	DISPOSAL OF USED OIL WITH DRUM & LTR	3080.00	67879.97	NE+NE+18.000+0.000+0.00

Tot. Tax'ble Amt	CGST Amt	SGST Amt	IGST Amt	CESS Amt	CESS Non.Advol Amt	Other Amt	Total Inv.Amt
67879.97	0.00	0.00	12218.39	0.00	0.00	0.00	80098.36

4. Transportation Details

Transporter ID & Name : 08ABFF34464G1ZZ & SHIV SHAKTI OIL LUBRICANTS

Transporter Doc. No & Date : & 02/11/2023

5. Vehicle Details

Mode	Vehicle / Trans Doc No & Dt.	From	Entered Date	Entered By	CEWB No. (If any)	Multi Veh.Info (If any)
Road	RJ40GA2066	Gurugram	02-11-2023 01:51 PM	06AACCC7148L1ZG		



301001215046



BOE Form

BOE Form

Sl. No.	Particulars	Quantity	Unit	Value	Remarks
1
2
3
4
5
6
7
8
9
10
11
12
13
14
15
16
17
18
19
20
21
22
23
24
25
26
27
28
29
30
31
32
33
34
35
36
37
38
39
40
41
42
43
44
45
46
47
48
49
50
51
52
53
54
55
56
57
58
59
60
61
62
63
64
65
66
67
68
69
70
71
72
73
74
75
76
77
78
79
80
81
82
83
84
85
86
87
88
89
90
91
92
93
94
95
96
97
98
99
100



23/10/23
 Pankaj Negi
 PANKAJ NEGI
 Auth. Officer & Supdt. of Customs
 ASF Insignia SEZ Pvt. Ltd.
 Gurgaon, (Haryana)

Performa Invoice

M/s ASF Insignia SEZ Pvt. Ltd.
 15/1, Gwal Pahari, Jhansi Road,
 Daman Gurgaon (Haryana)
 GSTIN # 06AA00007148L1Z0

Invoice No: ASF/SL-D/AVD/23/34
 Date: 31/07/2023

Buyer: M/S NETA SHAKTI OIL & LUBRICANTS
 15/1, Gwal Pahari, Jhansi Road, Daman Gurgaon,
 Dist: Gurgaon, Rajasthan-302017,
 GST No: 06ABFFS4464G1ZZ
 PAN No: ABFFS4464G

Delivery At SEZ Site
 Invoice Type: Advance
 Nature of Goods: Same as consignee

Quantity of Goods	Description of Goods	Quantity (Ltrs)	Rate (Rs)	Amount (Rs)
14 Drums (220 Ltrs each)	Used Lubricating Oil (Waste Oil with drum) H.S. Code: 27109900	3080.00	20.89	64341.20
3080 Ltrs				
TOTAL		3080		64341.20

IGST	12.00%	7720.94	12.00%
SGST	10.00%	6434.12	10.00%
		0.00	
Customs Duty		3538.77	
IGST	12.00%	12210.39	12.00%
Add: TOTAL Duty		16757.16	

Handwritten: PANKAJ NEGI
 Add: 15/1, Gwal Pahari, Jhansi Road, Daman Gurgaon, Rajasthan-302017
 GSTIN: 06ABFFS4464G1ZZ
 PAN: ABFFS4464G
 Net Invoice Value

	15,757.16
	80098.36
R/o	18.36
	80080.00

Total: Rupees Eighty Thousand Eighty Only.

I hereby declare that the above particulars are true & correct
 and I further declare that the goods are to be used only for the
 purpose for which they are intended.

For ASF Insignia SEZ Pvt. Ltd.

Authorized Signatory



Authorisation Cum-Passbook for
Re-refining/Recycling of Hazardous Waste

43

Name and Address of the Industry : M/s Shiv Shakti Oil & Lubricants
F-557, RIA Chopanki, Bhiwadi,
Tehsil - Tijara, District - Alwar

Telephone/Fax No. : 9818408248

E-Mail Address : shivshakti_lub07@yahoo.co.in

Authorisation No. : RPCB/HWM/2023-2024/HSW/HSW/E.

Date of issue : 11/05/2023

Validity period : 01/04/2023 To 31/03/2028

Type & quantity of the Hazardous Waste (S) permitted for procurement and recycling.

S. No.	Hazardous Waste (Used/Waste Oil) Type	Quantity (Kilolitres/Metric ton per annum)
1.	Used or spent oil (Schedule - I, code - S.1)	2000 KLA (Two Thousand KLA)
2.	Wastes or residues containing oil (Schedule - IV, code - S.2)	1600 KLA (Sixteen hundred KLA)




11.05.2023
श्री पी. गुप्ता
Authorized Signatory & Seal
आर. गुप्ता

Endorsement by the Auctioneer/Seller (except column no. 6 & 7)

(Condition No.3 of the Authorisation)

Authorisation No. KPCB/MHCH/2023-2024/1 HSW/MSW/8
Date: 11/05/2023

Waste(s) Type: Used or spent oil Permitted Quantity: 2000 KLA
Waste as Cardless Containers All - 16,000 KLA

S. No.	Date	Address of the Auctioneer/Seller	Type & Quantity of HW sold /Auctioned	Signature & Seal of the Auctioneer/Seller with date	Date of arrival in Recyclers premises & Challan No.	Balance Quantity (Registered - procured till date)
(1)	(2)	(3)	(4)	(5)	(6)	(7)
55						
56						
57	02/05/23	ASF Insignia SEZ Pvt Ltd 14, Gurgaon	51 3080 L		02/11/23 No. 0010215 02002	
58						
59						
60						

*to be filled by the Recycler





EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Contact : +91 - 9810243870

We Build Relations

Competence | Quality | Service

TEST REPORT

Ambient Air Quality Monitoring

Test Report No. : EKO/E-010/050624

Issue Date : 10/06/2024

Issued To

: ASF INSIGNIA SEZ PVT. LTD.
Village - Gwal Pahari,
Gurgaon Faridabad Road
Gurugram Haryana- 122003

Sample Description

: Ambient Air

Sample Drawn on

: 04/06/2024 To 05/06/2024

Sample Drawn by

: EPEPL (Mr. Mohd. Shakir)

Sample Received on

: 05/06/2024

Sampling Location

: Near Konark Area

Sampling Time

: 24.0 Hrs.

Sampling Plan & Procedure

: SOP-AAQ/15

Analysis Duration

: 05/06/2024 To 10/06/2024

Ambient Temperature (°C)

: 39.0

Average Flow Rate of SPM (m³/min.)

: 1.1

Average Flow Rate of Gases (lpm)

: 1.0

Weather Conditions

: Clear

Remark (if any)

: NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB Notification, 18th Nov 2009
1	Particulate Matter (PM10)	IS: 5182 (P-23)	254.2	µg/m ³	100.0
2	Particulate Matter (PM2.5)	IS:5182 (P-22)	128.4	µg/m ³	60.0
3	Sulphur Dioxide (as SO ₂)	IS: 5182 (P-2)	12.7	µg/m ³	80.0
4	Nitrogen Dioxide (as NO ₂)	IS: 5182 (P-6)	28.5	µg/m ³	80.0
5	Carbon Monoxide (as CO)	IS: 5182 (P-10)	1.24	mg/m ³	4.0

Notes :



- The results given above are related to the tested sample, for various parameters, as observed at the time of Sampling. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report.
Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

**** End of Report ****



For EKO PRO ENGINEERS PVT. LTD.
EKO PRO ENGINEERS PVT. LTD.
★ PURNIMA CHAUHAN ★
TECHNICAL MANAGER
Authorised Signatory
SAVE THE ENVIRONMENT






PHOTOGRAPH OF RAIN WATER HARVESTING PITS AT ASF INSIGNIA SEZ PVT. LTD

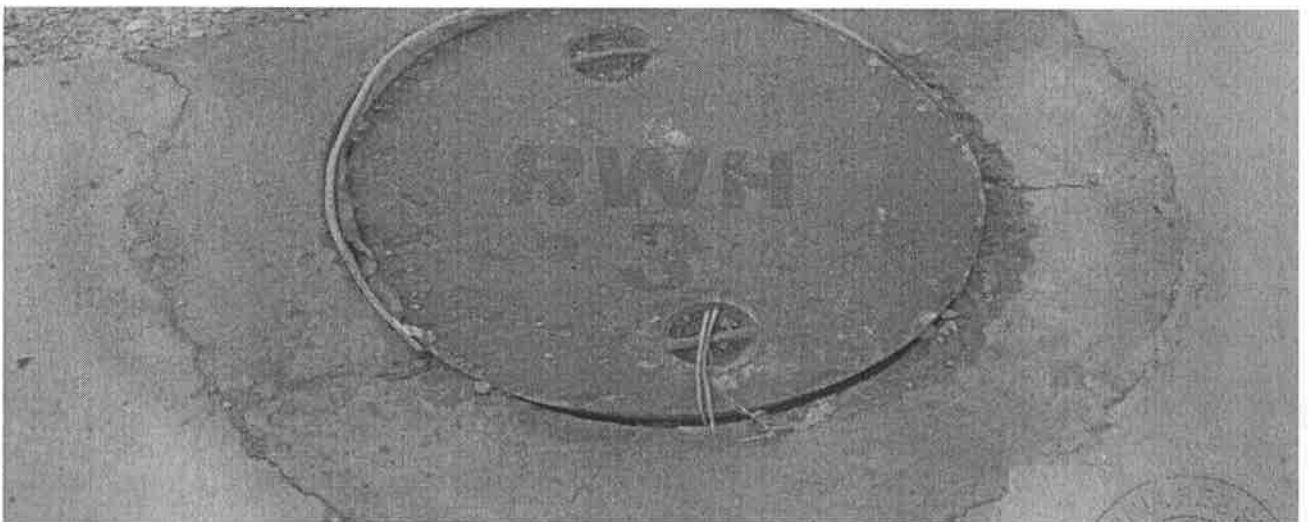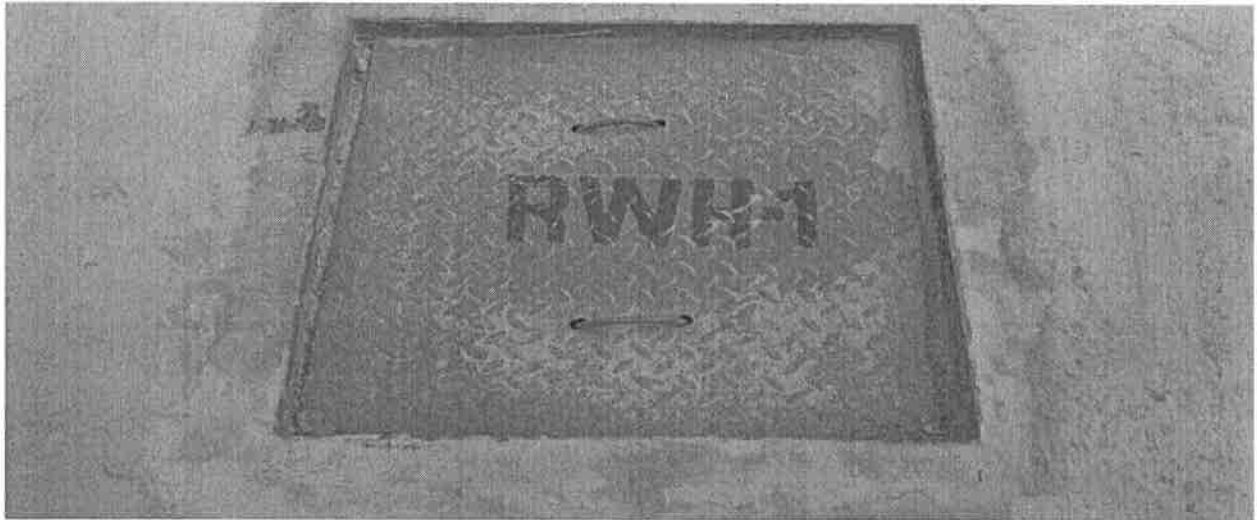






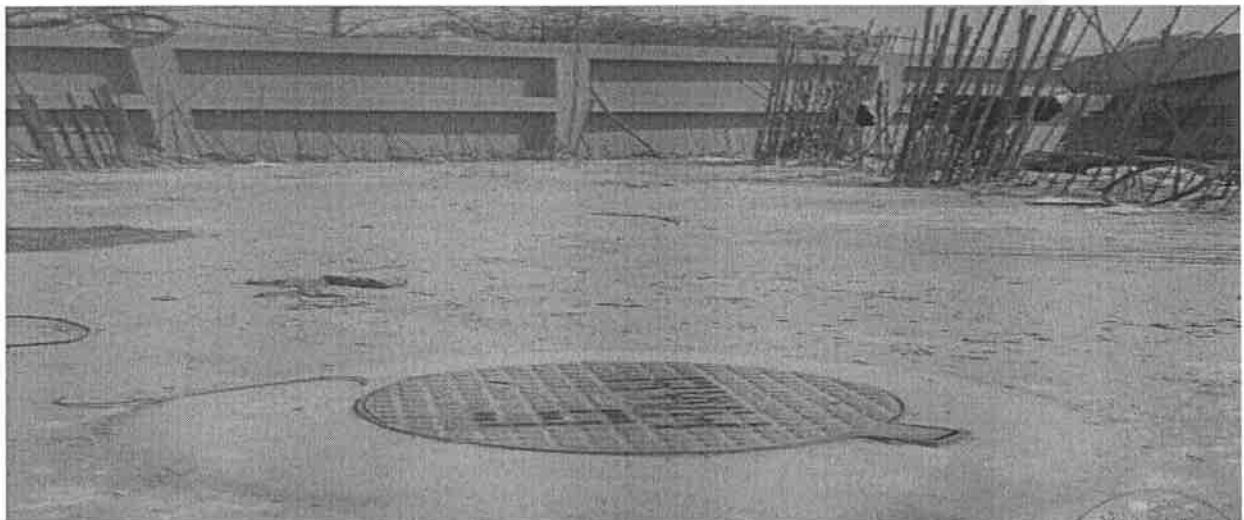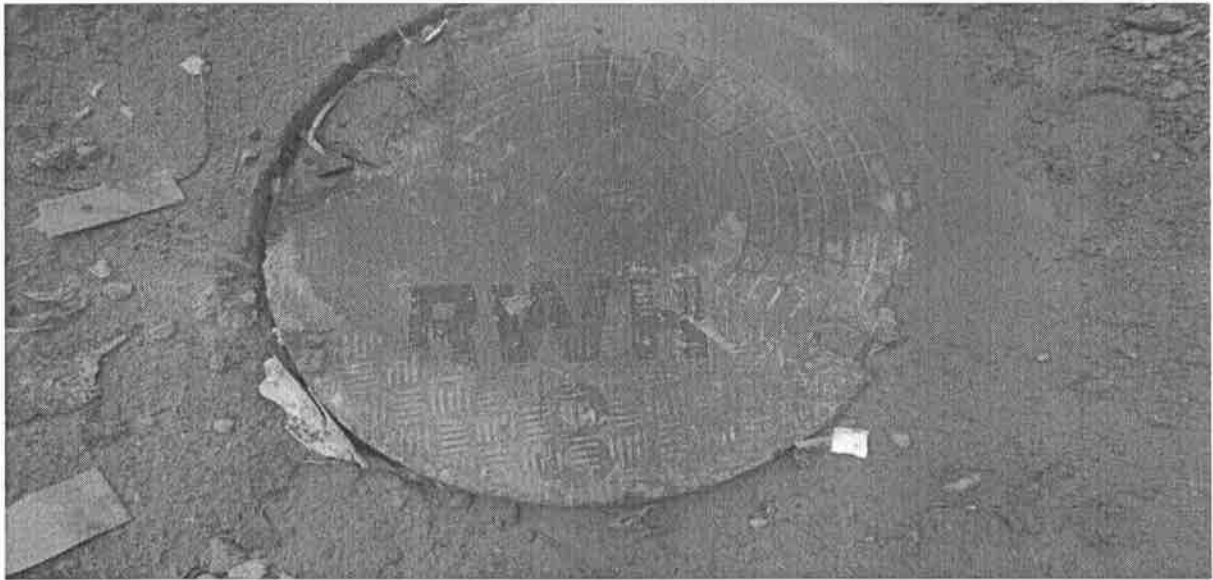


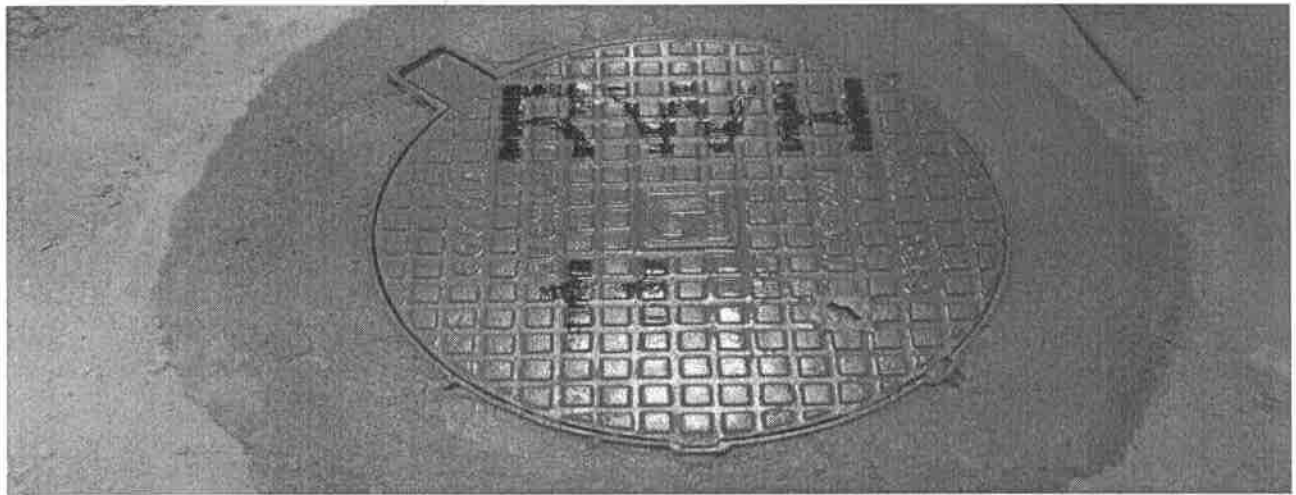

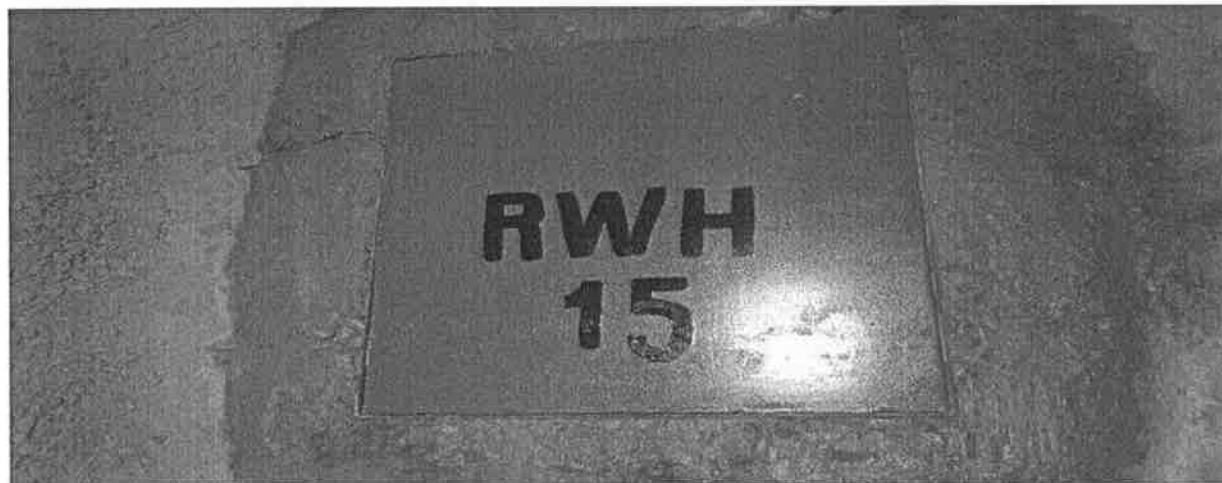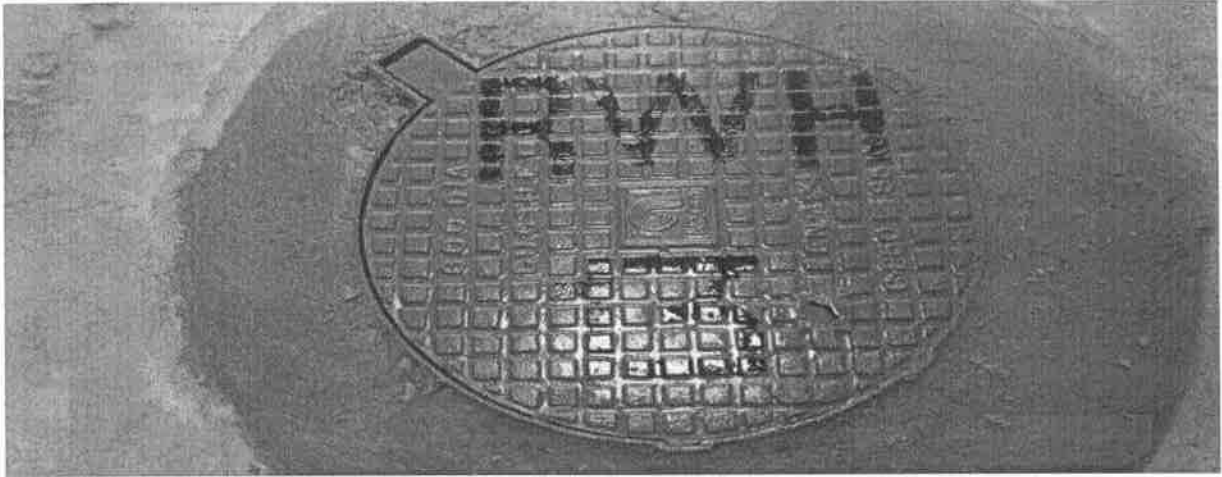

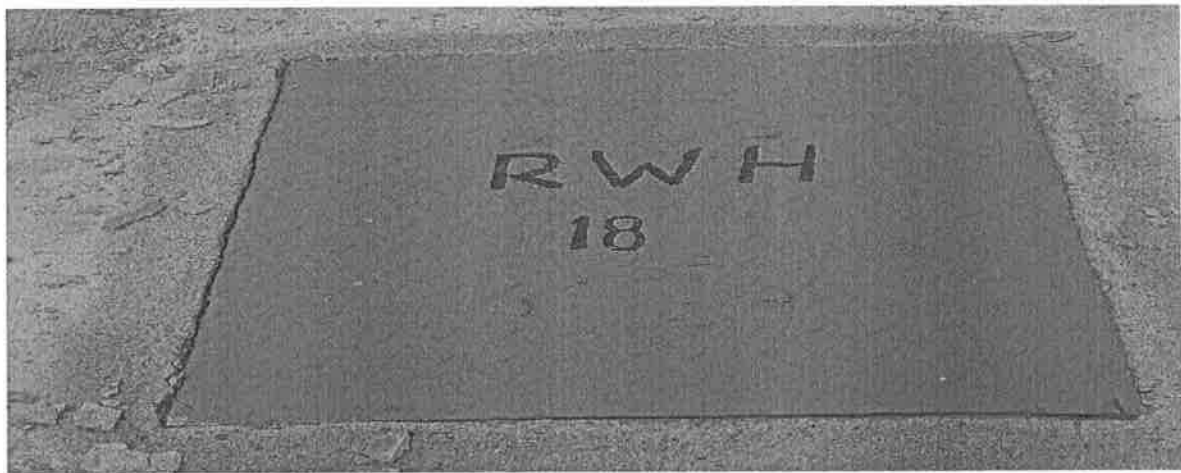

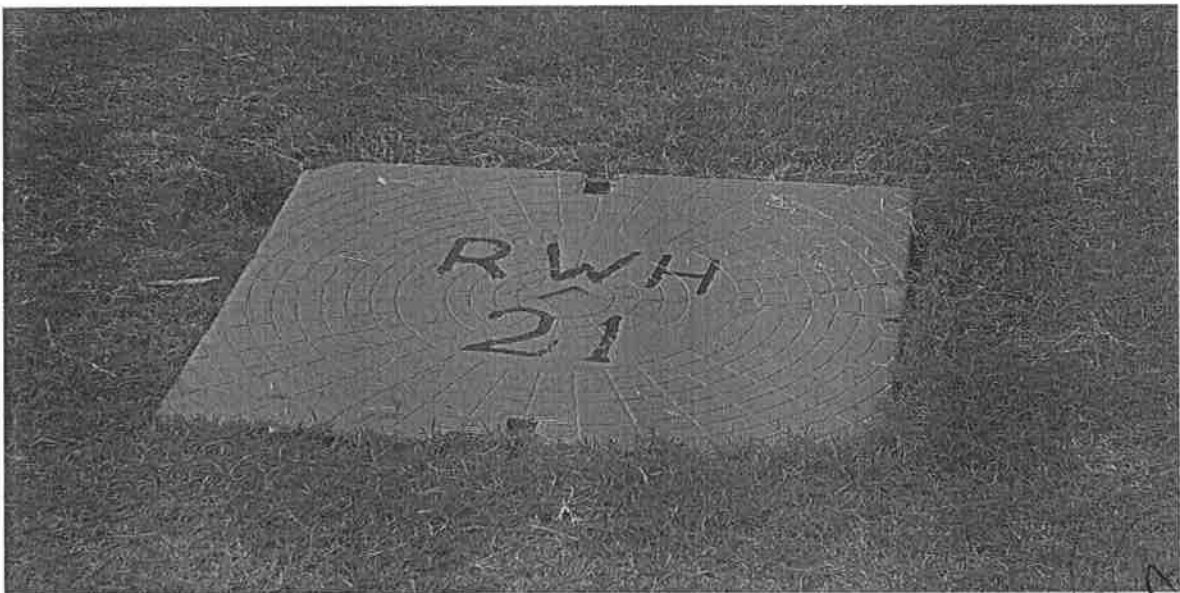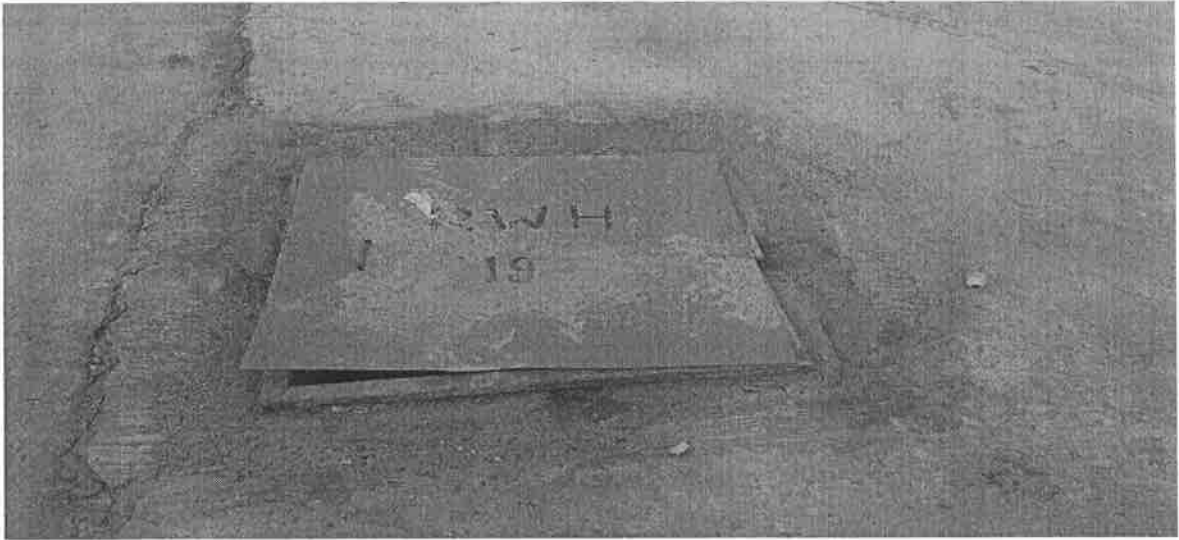

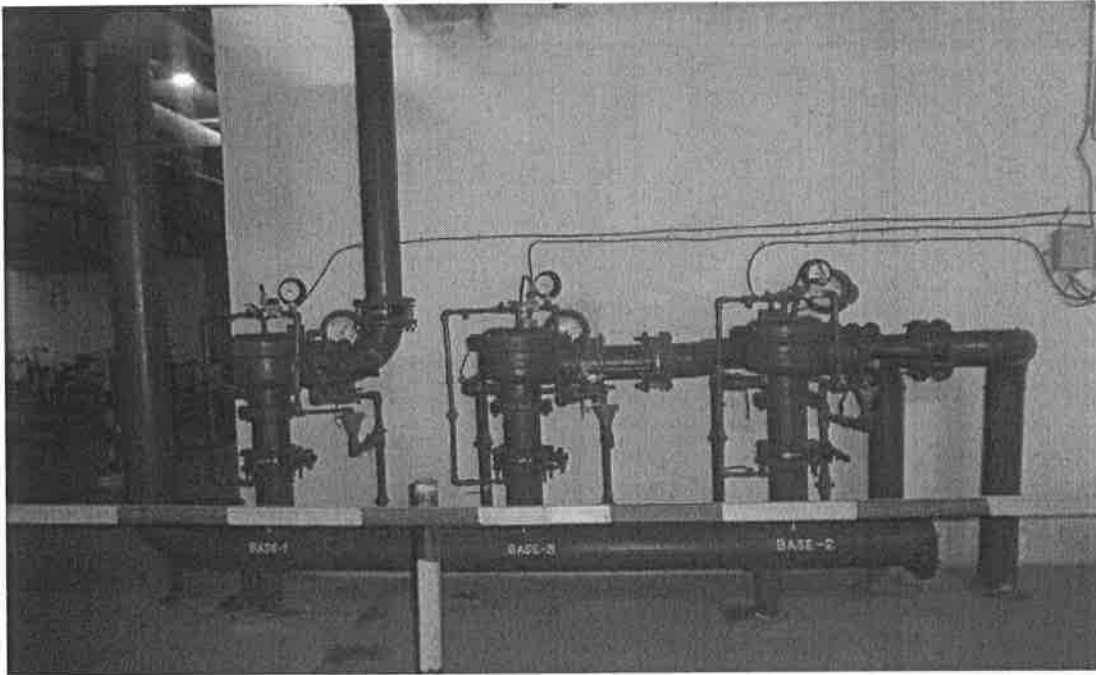

DELUGE SYSTEM FOR AUTOMATED WATER CURTAIN



PORTABLE EXTINGUISHERS ON TROLLEY





SAND BUCKET WITH FIRE EXTINGUISHER




FIRE TENDER AND AMBULANCE





FIRE TENDER

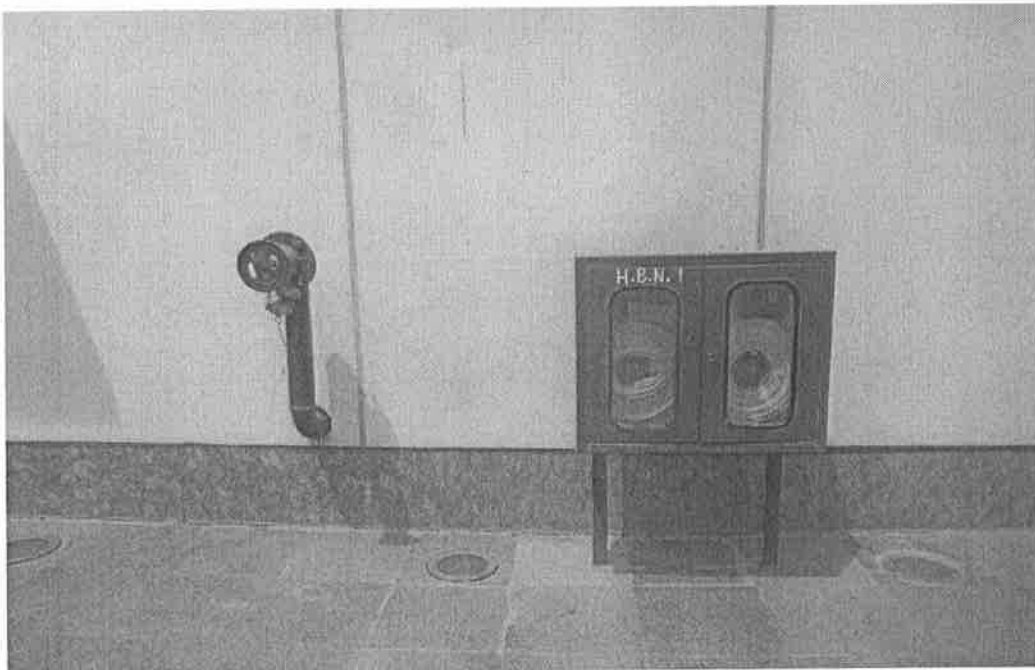

EXTERNAL FIRE HYDRANT






DRAW IN – DRAW OUT CONNECTION




FHC



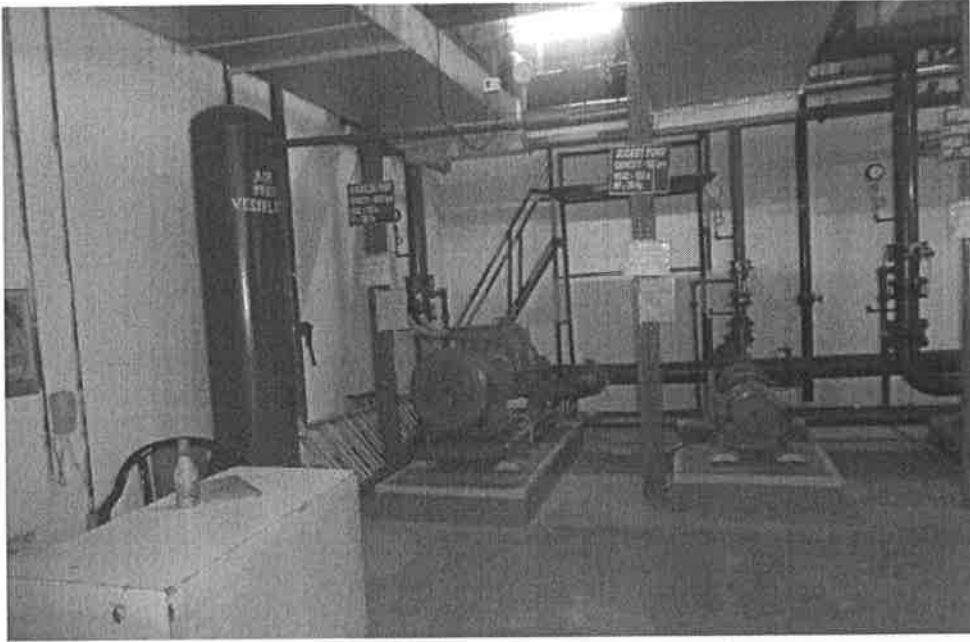


FIRE PUMP ROOM

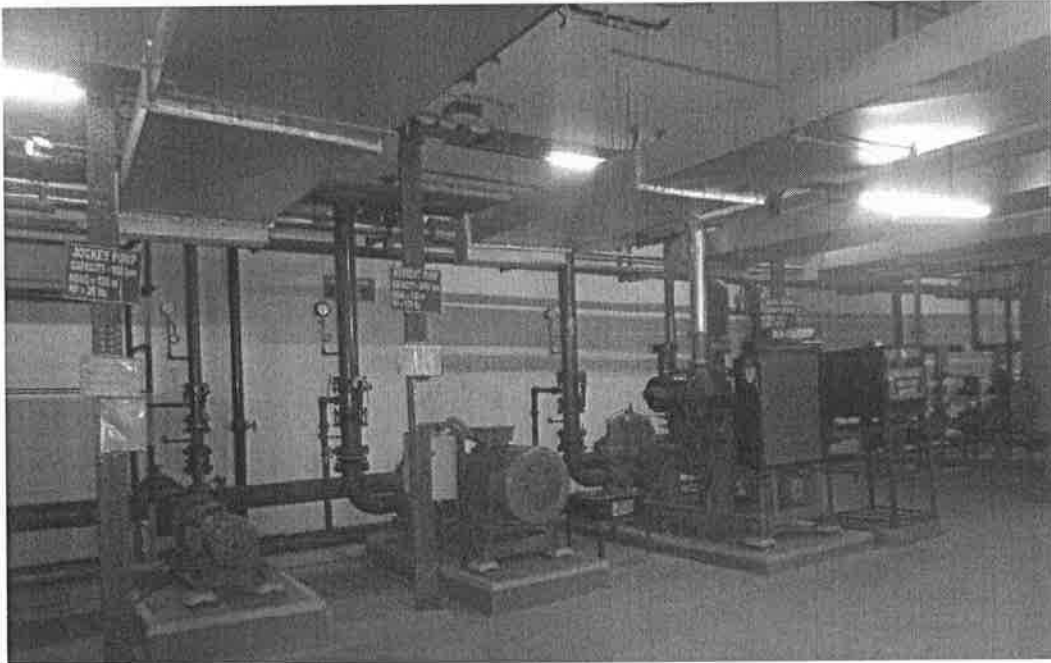

FIRE PUMP ROOM WITH DG BACK-UP



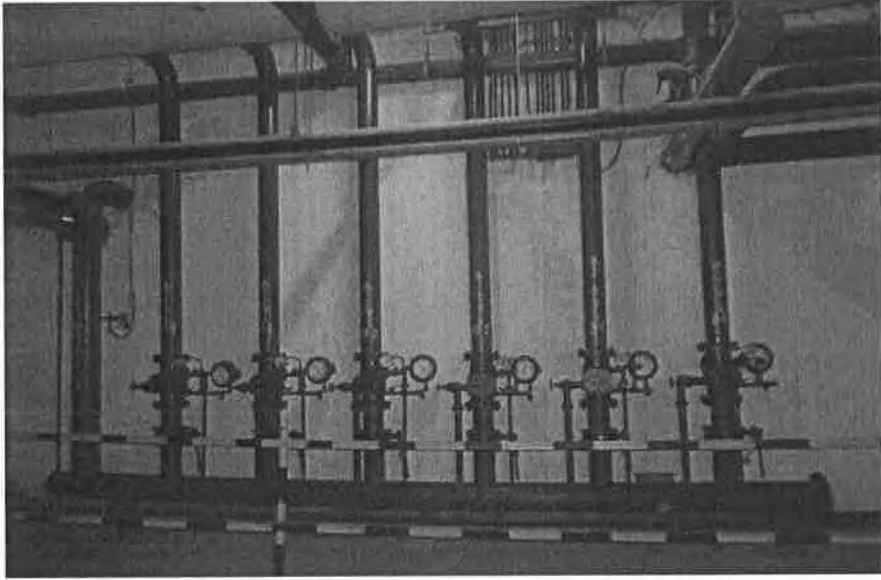

ACV FOR AUTOMATED SPRINKLER





FIRE CONTROL ROOM



AMINATURE-UTTIK
Tx



HARYANA STATE POLLUTION CONTROL BOARD

Gurgaon North Vikas Sadan, 1st Floor, Near DC Court, Gurgaon Ph.0124-2332775 Email:-

hspcbrogarn@gmail.com

E-mail: hspcb@hry.nic.in



No. HSPCB/Consent/ : 320303322GUNOCTO25902144

Dated:20/08/2022

To.

M/s :ASF INSIGNIA SEZ PVT. LTD. Building B2 (KCSPL) and Building B3(GCSPL)

Village Gwal Pahari, Gurgaon - Faridabad Road, Tehsil Wazirabad, District. Gurgaon

Subject: Grant of consent to operate to M/s ASF INSIGNIA SEZ PVT. LTD. Building B2 (KCSPL) and Building B3(GCSPL).

Please refer to your application no. 25902144 received on dated 2022-06-30 in regional office Gurgaon North. With reference to your above application for consent to operate, M/s ASF INSIGNIA SEZ PVT. LTD. Building B2 (KCSPL) and Building B3(GCSPL) is here by granted consent as per following specification/Terms and conditions.

Consent Under	BOTH
Period of consent	01/10/2022 - 30/09/2027
Industry Type	Industrial estates/ parks / complexes/ areas/ export processing zones/ SEZs/ Biotech parks/ leather complex
Category	RED
Investment(In Lakh)	82702.0
Total Land Area(Sq. meter)	26272.5
Total Builtup Area(Sq. meter)	161268.9
Quantity of effluent	
1. Trade	0.0 KL/Day
2. Domestic	371.0 KL/Day
Number of outlets	1.0
Mode of discharge	
1. Domestic	Recycling/ reuse
2. Trade	
Domestic Effluent Parameters	
1. BOD	30 mg/l
2. COD	250 mg/l
3. TSS	100 mg/l
4. O&G	10 mg/l
5. pH	5.5-9.0
Trade Effluent Parameters	




1. NA	
Number of stacks	1
Height of stack	
1. Stack to DG set 2000 KVA x 10	6 Meter (Above roof level)
Emission parameters	
1. NA	
Product Details	
1. NA	Metric Tonnes/day
Capacity of boiler	
1. NA	Ton/hr
Type of Furnace	
1. NA	
Type of Fuel	
1. Diesel	2.41 KL/day
Raw Material Details	
NA	Metric Tonnes/Day

HARYANA STATE

*Regional Officer, Gurgaon North
Haryana State Pollution Control Board.*

Terms and conditions


1. The applicants shall maintain good house keeping both within factory and in the premises. All hose pipelines valves, storage tanks etc. shall be leak proof. In plant allowable pollutants levels, if specified by State Board should be met strictly.
2. The applicant/company shall comply with and carry out directive/orders issued by the Board in this consent order at all subsequent times without negligence of his /its part. The applicant/company shall be liable for such legal action against him as per provision of the law/act in case of violation of any order/directives. Issued at any time and or non compliance of the terms and conditions of his consent order.
3. The applicant shall make an application for grant of consent at least 90 days before the date of expiry of this consent.
4. Necessary fee as prescribed for obtaining renewal consent shall be paid by the applicant alongwith the consent application.
5. If due to any technological improvement or otherwise this Board is of opinion that all or any of the conditions referred to above required variation (including the change of any control equipment either in whole or in part) this Board shall after giving the applicant an opportunity of being heard vary all or such condition and there upon the applicant shall be bound to comply with the conditions so varied.
6. The industry shall provide adequate arrangement for fighting the accidental leakages, discharge of any pollutants gas/liquids from the vessels, mechanical equipment etc. which are likely to cause environment pollution.
7. The industry shall comply noise pollution (Regulation and control) Rules, 2000.
8. The industry shall comply all the direction/Rules/Instructions as may be issued by the MOEF/CPCB/HSPCB from time to time.



9. The industry shall ensure that various characteristics of the effluents remain within the tolerance limits as specified in EPA Standard and as amended from time to time and at no time the concentration of any characteristics should exceed these limits for discharge.
10. The industry would immediately submit the revised application to the Board in the event of any change in the raw material in process, mode of treatment/discharge of effluent. In case of change of process at any stage during the consent period, the industry shall submit fresh consent application alongwith the consent to operate fee, if found due, which may be on any account and that shall be paid by the industry and the industry would immediately submit the consent application to the Board in the event of any change during the year in the raw material, quantity, quality of the effluent, mode of discharge, treatment facilities etc.
11. The officer/official of the Board shall reserve the right to access for the inspection of the industry in connection with the various process and the treatment facilities. The consent to operate is subject to review by the Board at any time.
12. Permissible limits for any pollutants mentioned in the consent to operate order should not exceed the concentration permitted in the effluent by the Board.
13. The industry shall pay the balance fee, in case it is found due from the industry at any time later on.
14. If the industry fails to adhere to any of the conditions of this consent to operate order, the consent to operate so granted shall automatically lapse.
15. If the industry is closed temporarily at its own, they shall inform the Board and obtain permission before restart of the unit.
16. The industry shall comply all the Directions/ Rules/Instructions issued from time to time by the Board.

Specific Conditions :

1. Unit will run and maintain it's STP/ETP/APCM regularly and properly, will provide separate energy meter on their STP/ETP/APCM and maintain the Log Book for energy consumption of STP/ETP/APCM and chemicals used daily for the STP/ETP.
2. That the unit shall keep all the parameters within the prescribed limits and shall comply with all the Norms and Rules as prescribed in the Act
3. That the unit will adopt cleaner technology thereby reducing pollution load.
4. That the unit will provide inter locking arrangement of DG set with STP/ETP/APCM and shall have separate D.G. set to ensure regular and effective running of pollution control devices.
5. That the unit will not discharge any untreated effluent inside and outside its premises.
6. Unit will provide separate flow meter at Inlet/ Outlet of STP/ETP for which separate log book will be maintained if required.
7. That the unit will not add any air polluting process/ machinery and also not to add any process which increases the water pollution load.
8. That the unit will comply with all the provisions of Hazardous Waste Rules and submit return under HWM Rules on yearly basis.
9. That the CTO so granted shall become invalid in case of violation of any of the above / any law of the land.
10. Unit will apply for consent to operate for further period 90 days before expiry of this consent otherwise penalty will be imposed as per policy.
11. Unit will submit compliance report of general & specific conditions mentioned in CTO alongwith fresh analysis report within 03 months.
12. Unit will install Emission control measures on DG set of capacity more than 500 KVA having minimum specified PM capturing efficiency of atleast 70% approved by CPCB recognized labs or shift to gas based generator in compliance of HSPCB office order no. 4230-44 dated 25.06.2020.
13. Unit will deposit any balance CTE/CTO fee, if found at any stage and time.





Haryana State Pollution Control Board
Gurgaon North Vikas Sadan, 1st Floor, Near DC Court, Gurgaon Ph.0124-
2332775 Email:- hspcbrogrn@gmail.com



No. :HWM/GUNO/2022/16670070

DT: 20/08/2022

To

M/s ASF INSIGNIA SEZ PVT. LTD. Building B2 (KCSPL) and Building B3(GCSPL)
Village Gwal Pahari, Gurgaon - Faridabad Road, Tehsil Wazirabad, District. Gurgaon
Gurgaon north

Sub: Grant of Authorization under Hazardous and Other Wastes(Management & Transboundary Movement) Rules, 2016

1. Reference of application:16670070 dated: 20/08/2022
2. Anil Sharma of ASF INSIGNIA SEZ PVT. LTD. Building B2 (KCSPL) and Building B3(GCSPL) is hereby granted an authorization for generation, storage on the premises situated at Village Gwal Pahari, Gurgaon - Faridabad Road, Tehsil Wazirabad, District. Gurgaon

Details of Authorization

S.No.	Name of process and Category of Hazardous Waste as per the Schedules I, II and III of these rules	Authorised mode of disposal or recycling or utilisation or co-processing, etc.	Quantity
1	Industrial operations using mineral/synthetic oil as lubricant in hydraulic systems or other applications, Used/spent oil	Authorized recyclers	2.86 KL/Annu m

1. The authorization shall be valid for a period of 01/10/2022 to 30/09/2027
2. The authorization is subject to the following general and specific conditions :-

- (i) **1. The unit will submit the Annual Report under HWM Rules by 30th June and Environment Statement by 30th September every year. 2. Unit will apply for renewal of consent/Authorization at least 90 days before expiry date of the consent/Authorization. 3. The hazardous waste generated by the unit will be disposed off through authorized TSDF/recyclers / Refiners of hazardous waste. 4. Unit will comply all the applicable Law/Acts/CPCB directions under the HOWM, Rules 2016 time to time, Unit will submit Annual Return under HWM, Rules timely. 5. Unit will maintain the record of storage and sold out the waste/spent oil of dg sets and same will submit in board on yearly basis. 6. That the authorization under HWM rules so granted shall become invalid in case of violation of any of the above / any law of the land. 7. Unit will generate online manifest regarding lifting of Hazardous Waste. 8) Unit is directed to comply with all the conditions invoked in authorization granted, failing which authorization granted will be suspended /revoked.**



AMMESHURE - X



HARYANA STATE POLLUTION CONTROL BOARD

Gurgaon North Vikas Sadan, 1st Floor, Near DC Court, Gurgaon Ph.0124-2332775 Email:-

hspcbrogrn@gmail.com

E-mail: hspcb@hry.nic.in



No. HSPCB/Consent/ : 329993522GUNOCTOW19397394

Dated:02/02/2022

To.

M/s :ASF Insignia SEZ Pvt. Ltd. IDR Residential

Village Gwal Pahari, Gurgaon-Faridabad Road Tehsil Wazirabad Gurugram

Subject: Grant of consent to operate to M/s ASF Insignia SEZ Pvt. Ltd. IDR Residential.

Please refer to your application no. 19397394 received on dated 2021-12-28 in regional office Gurgaon North. With reference to your above application for consent to operate, M/s ASF Insignia SEZ Pvt. Ltd. IDR Residential is here by granted consent as per following specification/Terms and conditions.

Consent Under	WATER
Period of consent	01/04/2022 - 31/03/2025
Industry Type	Sewage treatment plant having capacity 10 KLD or more but less than 100 KLD
Category	ORANGE
Investment(In Lakh)	15825.0
Total Land Area(Sq. meter)	8558.696
Total Builtup Area(Sq. meter)	25411.62
Quantity of effluent	
1. Trade	0.0 KL/Day
2. Domestic	42.0 KL/Day
Number of outlets	1.0
Mode of discharge	
1. Domestic	Reuse/Recycle
2. Trade	
Domestic Effluent Parameters	
1. BOD	30 mg/l
2. COD	250 mg/l
3. TSS	100 mg/l
4. O&G	10 mg/l
5. pH	5.5-9.0
Trade Effluent Parameters	
1. NA	
Number of stacks	1
Height of stack	




1. NA	
Emission parameters	
1. NA	
Product Details	
1. NA	Metric Tonnes/day
Capacity of boiler	
1. NA	Ton/hr
Type of Furnace	
1. NA	
Type of Fuel	
1. NA	
Raw Material Details	
NA	Metric Tonnes/Day

*Regional Officer, Gurgaon North
Haryana State Pollution Control Board.*

Terms and conditions

1. The applicants shall maintain good house keeping both within factory and in the premises. All hose pipelines valves, storage tanks etc. shall be leak proof. In plant allowable pollutants levels, if specified by State Board should be met strictly.
2. The applicant/company shall comply with and carry out directive/orders issued by the Board in this consent order at all subsequent times without negligence of his /its part. The applicant/company shall be liable for such legal action against him as per provision of the law/act in case of violation of any order/directives. Issued at any time and or non compliance of the terms and conditions of his consent order.
3. The applicant shall make an application for grant of consent at least 90 days before the date of expiry of this consent.
4. Necessary fee as prescribed for obtaining renewal consent shall be paid by the applicant alongwith the consent application.
5. If due to any technological improvement or otherwise this Board is of opinion that all or any of the conditions referred to above required variation (including the change of any control equipment either in whole or in part) this Board shall after giving the applicant an opportunity of being heard vary all or such condition and there upon the applicant shall be bound to comply with the conditions so varied.
6. The industry shall provide adequate arrangement for fighting the accidental leakages, discharge of any pollutants gas/liquids from the vessels, mechanical equipment etc. which are likely to cause environment pollution.
7. The industry shall comply noise pollution (Regulation and control) Rules, 2000.
8. The industry shall comply all the direction/Rules/Instructions as may be issued by the MOEF/CPCB/HSPCB from time to time.
9. The industry shall ensure that various characteristics of the effluents remain within the tolerance limits as specified in EPA Standard and as amended from time to time and at no time the concentration of any characteristics should exceed these limits for discharge.





We Build Relations



TC-5063

EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Contact : +91 - 9810243870

Competence | Quality | Service

TEST REPORT

Sewage Sample Analysis

Test Report No. : EKO/E-574/010424

Issue Date : 05/04/2024

Issued To

: ASF INSIGNIA SEZ ITES,
Village- Gwal Pahari,
Gurgaon Faridabad Road,
Sub Teh Wazirabad, Gurugan-122003

Sample Description : STP Inlet
Sample Drawn on : 01/04/2024
Sample Drawn by : EPEPL (Mr. Kishan Kumar)
Sample Received on : 01/04/2024
Sampling Location : From STP Plant B2 (465 KLD)
Sampling Plan & Procedure : SOP-W/66
Sample Quantity : 2.0 Litre
Environmental Condition : Normal
Analysis Duration : 01/04/2024 To 05/04/2024
Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11)	7.28	-
2	Total Suspended Solids	IS: 3025 (P-17)	139.0	mg/L
3	Oil & Grease	IS: 3025 (P-39)	16.0	mg/L
4	COD (as O ₂)	IS: 3025 (P-58)	348.7	mg/L
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	112.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

EKO PRO ENGINEERS PVT. LTD.
For EKO PRO ENGINEERS PVT. LTD.
POORNIMA GUHAN
TECHNICAL MANAGER
(Authorized Signatory)

Page 1 of 1



EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Contact : +91 - 9810243870

We Build Relations

TC-5063

Competence | Quality | Service

TEST REPORT

Sewage Sample Analysis

Test Report No. : EKO/E-572/010424

Issue Date : 05/04/2024

Issued To

: ASF INSIGNIA SEZ ITES,
Village- Gwal Pahari,
Gurgaon Faridabad Road,
Sub Teh Wazirabad, Gurugaon-122003

Sample Description : STP Outlet
 Sample Drawn on : 01/04/2024
 Sample Drawn by : EPEPL (Mr.Kishan Kumar)
 Sample Received on : 01/04/2024
 Sampling Location : From STP Plant B2 (465 KLD)
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 2.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 01/04/2024 To 05/04/2024
 Remark (if any) : NA


RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB Guidelines
1	pH	IS: 3025 (P-11)	7.18	-	5.5-9.0
2	Total Suspended Solids	IS: 3025 (P-17)	21.0	mg/L	100.0
3	Oil & Grease	IS: 3025 (P-39)	<4.0	mg/L	10.0
4	COD (as O ₂)	IS: 3025 (P-58)	41.6	mg/L	250.0
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	8.8	mg/L	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****





EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Contact : +91 - 9810243870

We Build Relations

TC-5063

Competence | Quality | Service

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/E-576/010424

Issue Date : 05/04/2024

Issued To

: ASF INSIGNIA SEZ ITES,
Village- Gwal Pahari,
Gurgaon Faridabad Road,
Sub Teh Wazirabad, Gurgaon-122003

Sample Description : STP Inlet
 Sample Drawn on : 01/04/2024
 Sample Drawn by : EPEPL (Mr. Kishan Kumar)
 Sample Received on : 01/04/2024
 Sampling Location : From STP Plant (IDR Building) - 50KLD
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 1.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 01/04/2023 To 05/04/2024
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units
1	pH	IS: 3025 (P-11) 2.0: 2022	7.18	-
2	Total Suspended Solids	IS:3025(Part-17): 2022	325.0	mg/L
3	Oil & Grease	IS:3025 (Part-39)-F : 2021	15.0	mg/L
4	COD (as O ₂)	IS 3025 (Part 58): 2006	460.5	mg/L
5	BOD (@27°C for 3 days)	IS 3025 (Part 44): 1993	185.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.
PURNIMA BANSAL
TECHNICAL MANAGER
(AUTHORISED SIGNATURE)



Page 1 of 1



We Build Relations

EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Contact : +91 - 9810243870

Competence | Quality | Service

TEST REPORT

Sewage Sample Analysis

Test Report No. : EKO/E-516/020524

Issue Date : 06/05/2024

Issued To

: ASF INSIGNIA SEZ ITES,
Village- Gwal Pahari,
Gurgaon Faridabad Road,
Sub Teh Wazirabad, Gurugaon-122003

Sample Description : STP Inlet
Sample Drawn on : 02/05/2024
Sample Drawn by : EPEPL (Mr. Pradeep Pandey)
Sample Received on : 02/05/2024
Sampling Location : From STP Plant B2 (465 KLD)
Sampling Plan & Procedure : SOP-W/66
Sample Quantity : 2.0 Litre
Environmental Condition : Normal
Analysis Duration : 02/05/2024 To 06/05/2024
Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11)	7.25	-
2	Total Suspended Solids	IS: 3025 (P-17)	136.0	mg/L
3	Oil & Grease	IS: 3025 (P-39)	15.0	mg/L
4	COD (as O ₂)	IS: 3025 (P-58)	350.5	mg/L
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	115.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.
PURNIMA CHAUHAN
TECHNICAL MANAGER
Authorized Signatory
SAVE THE ENVIRONMENT

Page 1 of 1



EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Contact : +91 - 9810243870

We Build Relations

Competence | Quality | Service

TEST REPORT

Sewage Sample Analysis

Test Report No. : EKO/E-515/020524

Issue Date : 06/05/2024

Issued To

: ASF INSIGNIA SEZ ITES,
Village- Gwal Pahari,
Gurgaon Faridabad Road,
Sub Teh Wazirabad, Gurugaon-122003

Sample Description : STP Outlet
 Sample Drawn on : 02/05/2024
 Sample Drawn by : EPEPL (Mr. Pradeep Pandey)
 Sample Received on : 02/05/2024
 Sampling Location : From STP Plant B3 (530 KLD)
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 2.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 02/05/2024 To 06/05/2024
 Remark (if any) : NA


RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB Guidelines
1	pH	IS: 3025 (P-11)	7.31	-	5.5-9.0
2	Total Suspended Solids	IS: 3025 (P-17)	18.0	mg/L	100.0
3	Oil & Grease	IS: 3025 (P-39)	<4.0	mg/L	10.0
4	COD (as O ₂)	IS: 3025 (P-58)	39.2	mg/L	250.0
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	8.8	mg/L	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****





We Build Relations

EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Contact : +91 - 9810243870

Competence | Quality | Service

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/E-520/020524

Issue Date : 06/05/2024

Issued To

: ASF INSIGNIA SEZ ITES,
Village- Gwal Pahari,
Gurgaon Faridabad Road,
Sub Teh Wazirabad, Gurgaon-122003

Sample Description : STP Inlet
 Sample Drawn on : 02/05/2024
 Sample Drawn by : EPEPL (Mr. Pradeep Pandey)
 Sample Received on : 02/05/2024
 Sampling Location : From STP Plant (IDR Building) - 50KLD
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 1.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 02/05/2023 To 06/05/2024
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units
1	pH	IS: 3025 (P-11) 2.0: 2022	7.21	-
2	Total Suspended Solids	IS:3025(Part-17): 2022	340.0	mg/L
3	Oil & Grease	IS:3025 (Part-39)-F : 2021	14.0	mg/L
4	COD (as O ₂)	IS 3025 (Part 58): 2006	450.9	mg/L
5	BOD (@27°C for 3 days)	IS 3025 (Part 44): 1993	183.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****



Page 1 of 1



We Build Relations

EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Contact : +91 - 9810240870

Competence | Quality | Service

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/E-521/020524

Issue Date : 06/05/2024

Issued To

: ASF INSIGNIA SEZ ITES,
Village- Gwal Pahari,
Gurgaon Faridabad Road,
Sub Teh Wazirabad, Gurgaon-122003

Sample Description : STP Outlet
Sample Drawn on : 02/05/2024
Sample Drawn by : EPEPL (Mr. Pradeep Pandey)
Sample Received on : 02/05/2024
Sampling Location : From STP Plant (IDR Building) - 50KLD
Sampling Plan & Procedure : SOP-W/66
Sample Quantity : 1.0 Litre
Environmental Condition : Normal
Analysis Duration : 02/05/2023 To 06/05/2024
Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB Guidelines
1	pH	IS: 3025 (P-11) 2.0: 2022	7.18	-	5.5-9.0
2	Total Suspended Solids	IS:3025(Part-17): 2022	47.0	mg/L	100.0
3	Oil & Grease	IS:3025 (Part-39)-F : 2021	<4.0	mg/L	10.0
4	COD (as O ₂)	IS 3025 (Part 58): 2006	41.8	mg/L	250.0
5	BOD (@27°C for 3 days)	IS 3025 (Part 44): 1993	9.2	mg/L	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****





EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Contact : +91 - 9810243870

We Build Relations

Competence | Quality | Service

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/E-515/010624

Issue Date : 05/06/2024

Issued To

: ASF INSIGNIA SEZ ITES,
Village- Gwal Pahari,
Gurgaon Faridabad Road,
Sub Teh Wazirabad, Gurgaon-122003

Sample Description : STP Outlet
 Sample Drawn on : 01/06/2024
 Sample Drawn by : EPEPL (Mr. Anuj Gupta)
 Sample Received on : 01/06/2024
 Sampling Location : From STP Plant (IDR Building) - 50KLD
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 1.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 01/06/2024 To 05/06/2024
 Remark (if any) : NA


RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB Guidelines
1	pH	IS: 3025 (P-11) 2.0: 2022	7.13	-	5.5-9.0
2	Total Suspended Solids	IS:3025(Part-17): 2022	45.0	mg/L	100.0
3	Oil & Grease	IS:3025 (Part-39)-F : 2021	<4.0	mg/L	10.0
4	COD (as O ₂)	IS 3025 (Part 56): 2006	39.4	mg/L	250.0
5	BOD (@27°C for 3 days)	IS 3025 (Part 44): 1993	8.9	mg/L	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****





We Build Relations

EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Contact : +91 - 9810243870

Competence | Quality | Service

TEST REPORT

Sewage Sample Analysis

Test Report No. : EKO/E-520/020724

Issue Date : 06/07/2024

Issued To

: ASF INSIGNIA SEZ ITES,
Village- Gwal Pahari,
Gurgaon Faridabad Road,
Sub Teh Wazirabad, Gurugaon-122003

Sample Description : STP Outlet
 Sample Drawn on : 02/07/2024
 Sample Drawn by : EPEPL (Mr. Rajeev Sharma)
 Sample Received on : 02/07/2024
 Sampling Location : From STP Plant B2 (465 KLD)
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 2.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 02/07/2024 To 06/07/2024
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB Guidelines
1	pH	IS: 3025 (P-11)	7.15	-	5.5-9.0
2	Total Suspended Solids	IS: 3025 (P-17)	25.0	mg/L	100.0
3	Oil & Grease	IS: 3025 (P-39)	<4.0	mg/L	10.0
4	COD (as O ₂)	IS: 3025 (P-58)	42.9	mg/L	250.0
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	9.3	mg/L	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.
 PURNIMA CHAUHAN
 TECHNICAL MANAGER
 Authorised Signatory
 SAVE THE ENVIRONMENT





We Build Relations

EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Contact : +91 - 9810243870

Competence | Quality | Service

TEST REPORT

Sewage Sample Analysis

Test Report No. : EKO/E-509/020724

Issue Date : 06/07/2024

Issued To

: ASF INSIGNIA SEZ ITES,
Village- Gwal Pahari,
Gurgaon Faridabad Road,
Sub Teh Wazirabad, Gurugaon-122003

Sample Description : STP Outlet
 Sample Drawn on : 02/07/2024
 Sample Drawn by : EPEPL (Mr. Rajeev Sharma)
 Sample Received on : 02/07/2024
 Sampling Location : From STP Plant B3 (530 KLD)
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 2.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 02/07/2024 To 06/07/2024
 Remark (if any) : NA


RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB Guidelines
1	pH	IS: 3025 (P-11)	7.32	-	5.5-9.0
2	Total Suspended Solids	IS: 3025 (P-17)	18.0	mg/L	100.0
3	Oil & Grease	IS: 3025 (P-39)	<4.0	mg/L	10.0
4	COD (as O ₂)	IS: 3025 (P-58)	37.9	mg/L	250.0
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	8.7	mg/L	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****





We Build Relations

EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Contact : +91 - 9810243870

Competence | Quality | Service

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/E-507/020724

Issue Date : 06/07/2024

Issued To

: ASF INSIGNIA SEZ ITES,
Village- Gwal Pahari,
Gurgaon Faridabad Road,
Sub Teh Wazirabad, Gurgaon-122003

Sample Description

: STP Inlet

Sample Drawn on

: 02/07/2024

Sample Drawn by

: EPEPL (Mr. Rajeev Sharma)

Sample Received on

: 02/07/2024

Sampling Location

: From STP Plant (IDR Building) - 50KLD

Sampling Plan & Procedure

: SOP-W/66

Sample Quantity

: 1.0 Litre

Environmental Condition

: Normal

Analysis Duration

: 02/07/2024 To 06/07/2024

Remark (if any)

: NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units
1	pH	IS: 3025 (P-11) 2.0: 2022	7.21	-
2	Total Suspended Solids	IS:3025(Part-17): 2022	358.0	mg/L
3	Oil & Grease	IS:3025 (Part-39)-F : 2021	14.0	mg/L
4	COD (as O ₂)	IS 3025 (Part 58): 2006	454.9	mg/L
5	BOD (@27°C for 3 days)	IS 3025 (Part 44): 1993	183.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.
★ PURNIMA SHUKLA ★
TECHNICAL MANAGER
Authorised Signatory

Page 1 of 1



We Build Relations

EKO TESTING LABS® Eko Pro Engineers Pvt. Ltd.

Contact : +91 - 9810243870

Competence | Quality | Service

TEST REPORT

Sewage Sample Analysis

Test Report No. : EKO/E-509/010824

Issue Date : 05/08/2024

Issued To

: ASF INSIGNIA SEZ ITES
Village- Gwal Pahari,
Gurgaon Faridabad Road,
Sub Teh Wazirabad, Gurugaon-122003

Sample Description

: STP Inlet

Sample Drawn on

: 01/08/2024

Sample Drawn by

: EPEPL (Mr. Harish Kumar)

Sample Received on

: 01/08/2024

Sampling Location

: From STP Plant B2 (465 KLD)

Sampling Plan & Procedure

: SOP-W/66

Sample Quantity

: 2.0 Litre

Environmental Condition

: Normal

Analysis Duration

: 01/08/2024 To 05/08/2024

Remark (if any)

: NA


RESULTS

S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11) 2.0: 2022	7.31	-
2	Total Suspended Solids	IS:3025(Part-17): 2022	142.0	mg/L
3	Oil & Grease	IS:3025 (Part-39)-F : 2021	15.0	mg/L
4	COD (as O ₂)	IS 3025 (Part 58): 2006	350.2	mg/L
5	BOD (@27°C for 3 days)	IS 3025 (Part 44): 1993	119.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.

 PURNIM CHAUHAN
 TECHNICAL MANAGER
 SAVE THE ENVIRONMENT

Page 1 of 1



We Build Relations

EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Competence | Quality | Service

Contact : +91 9810240837



TEST REPORT

Sewage Sample Analysis

Test Report No. : EKO/E-508/010824

Issue Date : 05/08/2024

Issued To

: ASF INSIGNIA SEZ ITES,
Village- Gwal Pahari,
Gurgaon Faridabad Road,
Sub Teh Wazirabad, Gurugaoon-122003

Sample Description : STP Outlet
 Sample Drawn on : 01/08/2024
 Sample Drawn by : EPEPL (Mr. Harish Kumar)
 Sample Received on : 01/08/2024
 Sampling Location : From STP Plant B3 (530 KLD)
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 2.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 01/08/2024 To 05/08/2024
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB Guidelines
1	pH	IS: 3025 (P-11) 2.0: 2022	7.31	-	5.5-9.0
2	Total Suspended Solids	IS:3025(Part-17): 2022	17.0	mg/L	100.0
3	Oil & Grease	IS:3025 (Part-39)-F : 2021	BLQ (LOQ-4.0)	mg/L	10.0
4	COD (as O ₂)	IS 3025 (Part 58): 2006	38.5	mg/L	250.0
5	BOD (@27°C for 3 days)	IS 3025 (Part 44): 1993	9.6	mg/L	30.0
6	Total Phosphate (as P)	IS 3025(Part 31)Se -1 B: 2022	0.81	mg/L	5.0
7	Total Nitrogen (as N)	S 3025 (Part 34)-A: 1988	5.22	mg/L	100.0
8	Faecal Coliform	IS:1622 :1981	60	MPN/100ml	1000.0

BLQ=Below Limits of Quantification, LOQ= Limits of Quantification

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.
 SHIVANG SHARMA
 SECTION INCHARGE MICROBIOLOGY
 (Authorized Signatory)

For EKO PRO ENGINEERS PVT. LTD.
 PURNIMA CHAUHAN
 TECHNICAL MANAGER
 (Authorized Signatory)

Page 1 of 1



We Build Relations

EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Competence | Quality | Service

Contact : +91 9810240370



TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/E-002/010824

Issue Date : 06/08/2024

Issued To

: ASF INSIGNIA SEZ ITES,
Village- Gwal Pahari,
Gurgaon Faridabad Road,
Sub Teh Wazirabad, Gurgaon-122003

Sample Description : STP Inlet
 Sample Drawn on : 01/08/2024
 Sample Drawn by : EPEPL (Mr. Harish Kumar)
 Sample Received on : 01/08/2024
 Sampling Location : From STP Plant (IDR Building) - 50KLD
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 1.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 01/08/2024 To 06/08/2024
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units
1	pH	IS: 3025 (P-11) 2.0: 2022	7.18	-
2	Total Suspended Solids	IS:3025(Part-17): 2022	365.0	mg/L
3	Oil & Grease	IS:3025 (Part-39)-F : 2021	15.0	mg/L
4	COD (as O ₂)	IS 3025 (Part 58): 2006	449.6	mg/L
5	BOD (@27°C for 3 days)	IS 3025 (Part 44): 1993	185.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA CHAUHAN
 TECHNICAL MANAGER
 Ghaziabad
 Authorised Signatory
 SAVE THE ENVIRONMENT





We Build Relations

EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Competence | Quality | Service

Contact : +91-9810240837



TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/E-003/010824

Issue Date : 06/08/2024

Issued To

: ASF INSIGNIA SEZ ITES,
Village- Gwal Pahari,
Gurgaon Faridabad Road,
Sub Teh Wazirabad, Gurgaon-122003

Sample Description : STP Outlet
 Sample Drawn on : 01/08/2024
 Sample Drawn by : EPEPL (Mr. Harish Kumar)
 Sample Received on : 01/08/2024
 Sampling Location : From STP Plant (IDR Building) - 50KLD
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 1.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 01/08/2024 To 06/08/2024
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB Guidelines
1	pH	IS: 3025 (P-11) 2.0: 2022	7.17	-	5.5-9.0
2	Total Suspended Solids	IS:3025(Part-17): 2022	48.0	mg/L	100.0
3	Oil & Grease	IS:3025 (Part-39)-F : 2021	<4.0	mg/L	10.0
4	COD (as O ₂)	IS 3025 (Part 58): 2006	39.6	mg/L	250.0
5	BOD (@27°C for 3 days)	IS 3025 (Part 44): 1993	8.8	mg/L	30.0
6	Total Phosphate (as P)	IS 3025(Part 31)Se -1 B: 2022	0.78	mg/L	5.0
7	Total Nitrogen (as N)	S 3025 (Part 34)-A: 1988	5.16	mg/L	100.0
8	Faecal Coliform	IS:1622 :1981	50	MPN/100ml	1000.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.
 ESHIVANGI SINGH RAZADA
 SECTION INCHARGE MICROBIOLOGY
 GHAZIABAD
 Authorised Signatory
 SAVE THE ENVIRONMENT

For EKO PRO ENGINEERS PVT. LTD.
 PURNIMA CHAUHAN
 TECHNICAL MANAGER
 GHAZIABAD
 Authorised Signatory
 SAVE THE ENVIRONMENT





TEST REPORT

Sewage Sample Analysis

Test Report No. : EKO/E-014/020924

Issue Date : 06/09/2024

Issued To

: ASF INSIGNIA SEZ ITES
 : Village- Gwal Pahari,
 : Gurgaon Faridabad Road,
 : Sub Teh Wazirabad, Gurugaon-122003

Sample Description

: STP Inlet

Sample Drawn on

: 02/09/2024

Sample Drawn by

: EPEPL (Mr. Amit Kumar)

Sample Received on

: 02/09/2024

Sampling Location

: From STP Plant B2 (465 KLD)

Sampling Plan & Procedure

: SOP-W/66

Sample Quantity

: 2.0 Litre

Environmental Condition

: Normal

Analysis Duration

: 02/09/2024 To 06/09/2024

Remark (if any)

: NA

RESULTS

S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11) 2.0: 2022	7.26	-
2	Total Suspended Solids	IS:3025(Part-17): 2022	144.0	mg/L
3	Oil & Grease	IS:3025 (Part-39)-F : 2021	16.0	mg/L
4	COD (as O ₂)	IS 3025 (Part 58): 2006	342.8	mg/L
5	BOD (@27°C for 3 days)	IS 3025 (Part 44): 1993	120.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.
 PURNIMA CHAUHAN
 TECHNICAL MANAGER
 (Authorised Signatory)





TEST REPORT

Sewage Sample Analysis

Test Report No. : EKO/E-015/020924

Issue Date : 06/09/2024

Issued To

: ASF INSIGNIA SEZ ITES
 : Village- Gwal Pahari,
 : Gurgaon Faridabad Road,
 : Sub Teh Wazirabad, Gurugaon-122003

Sample Description

: STP Inlet

Sample Drawn on

: 02/09/2024

Sample Drawn by

: EPEPL (Mr. Amit Kumar)

Sample Received on

: 02/09/2024

Sampling Location

: From STP Plant B3 (530 KLD)

Sampling Plan & Procedure

: SOP-W/66

Sample Quantity

: 2.0 Litre

Environmental Condition

: Normal

Analysis Duration

: 02/09/2024 To 06/09/2024

Remark (if any)

: NA

RESULTS

S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11) 2.0: 2022	7.23	-
2	Total Suspended Solids	IS:3025(Part-17): 2022	130.0	mg/L
3	Oil & Grease	IS:3025 (Part-39)-F : 2021	14.0	mg/L
4	COD (as O ₂)	IS 3025 (Part 58): 2006	308.4	mg/L
5	BOD (@27°C for 3 days)	IS 3025 (Part 44): 1993	103.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.
 PURNIMA SHAHAN
 TECHNICAL MANAGER
 (Authorised Signatory)

Page 1 of 1



TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/E-010/020924

Issue Date : 06/09/2024

Issued To

: ASF INSIGNIA SEZ ITES,
 : Village- Gwal Pahari,
 : Gurgaon Faridabad Road,
 : Sub Teh Wazirabad, Gurgaon-122003

Sample Description

: STP Inlet

Sample Drawn on

: 02/09/2024

Sample Drawn by

: EPEPL (Mr. Amit Kumar)

Sample Received on

: 02/09/2024

Sampling Location

: From STP Plant (IDR Building) - 50KLD

Sampling Plan & Procedure

: SOP-W/66

Sample Quantity

: 1.0 Litre

Environmental Condition

: Normal

Analysis Duration

: 02/09/2024 To 06/09/2024

Remark (if any)

: NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units
1	pH	IS: 3025 (P-11) 2.0: 2022	7.23	-
2	Total Suspended Solids	IS:3025(Part-17): 2022	360.0	mg/L
3	Oil & Grease	IS:3025 (Part-39)-F : 2021	14.0	mg/L
4	COD (as O ₂)	IS 3025 (Part 58): 2006	440.5	mg/L
5	BOD (@27°C for 3 days)	IS 3025 (Part 44): 1993	183.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.
 PURNIMA CHAUHAN
 TECHNICAL MANAGER
 Authorised Signatory
 SAVE THE ENVIRONMENT

ASF INSGNIA SEZ ITES PVT. LTD.
 Page 1 of 1



TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/E-011/020924

Issue Date : 06/09/2024

Issued To : ASF INSIGNIA SEZ ITES,
 : Village- Gwal Pahari,
 : Gurgaon Faridabad Road,
 : Sub Teh Wazirabad, Gurgaon-122003

Sample Description : STP Outlet
 Sample Drawn on : 02/09/2024
 Sample Drawn by : EPEPL (Mr. Amit Kumar)
 Sample Received on : 02/09/2024
 Sampling Location : From STP Plant (IDR Building) - 50KLD
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 1.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 02/09/2024 To 06/09/2024
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB Guidelines
1	pH	IS: 3025 (P-11) 2.0: 2022	7.19	-	5.5-9.0
2	Total Suspended Solids	IS:3025(Part-17): 2022	46.0	mg/L	100.0
3	Oil & Grease	IS:3025 (Part-39)-F : 2021	<4.0	mg/L	10.0
4	COD (as O ₂)	IS 3025 (Part 58): 2006	35.8	mg/L	250.0
5	BOD (@27°C for 3 days)	IS 3025 (Part 44): 1993	8.6	mg/L	30.0
6	Total Phosphate (as P)	IS 3025(Part 31)Se -1 B: 2022	0.72	mg/L	5.0
7	Total Nitrogen (as N)	S 3025 (Part 34)-A: 1988	5.11	mg/L	100.0
8	Faecal Coliform	IS:1622 :1981	40	MPN/100ml	1000.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.


****End of Report****

For EKO PRO ENGINEERS PVT. LTD.
 SHIVANGI SINGH RAIZADA
 SECTION INCHARGE MICROBIOLOGY
 (Authorised Signatory)
 SAVE THE ENVIRONMENT




For EKO PRO ENGINEERS PVT. LTD.
 PURNIMA GHAIHAN
 TECHNICAL MANAGER
 (Authorised Signatory)
 SAVE THE ENVIRONMENT




Borewell No.1

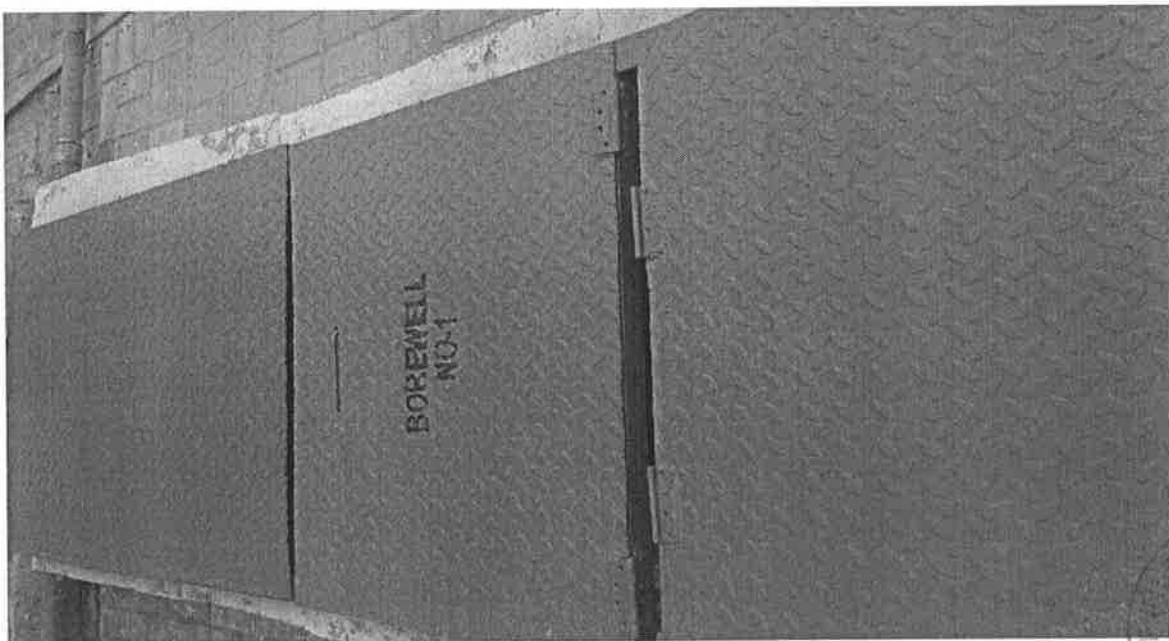



Borewell No.2

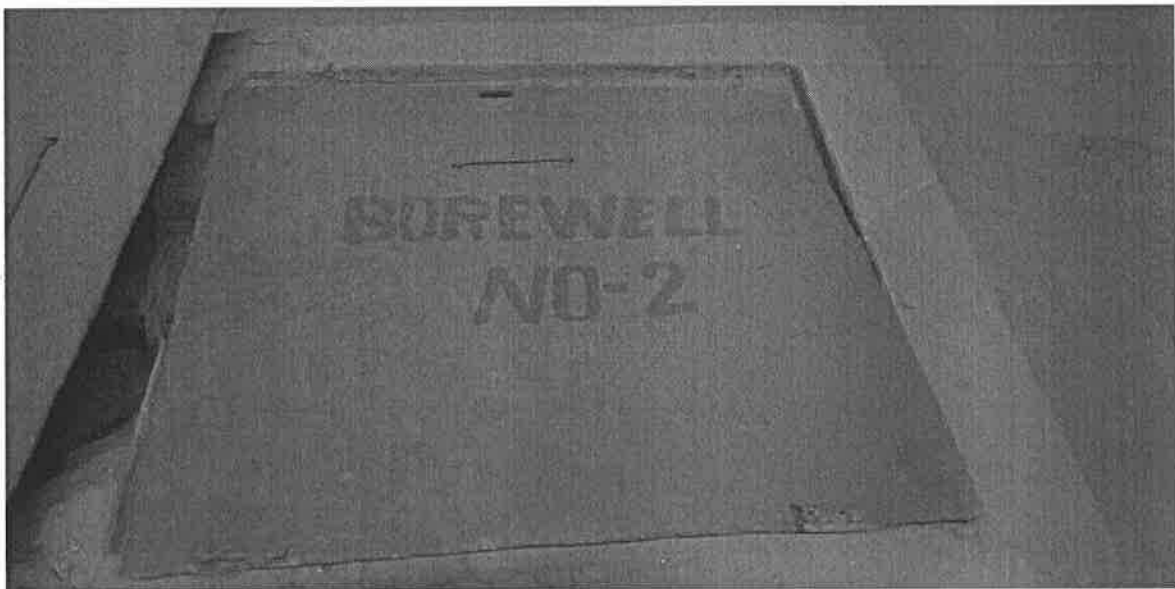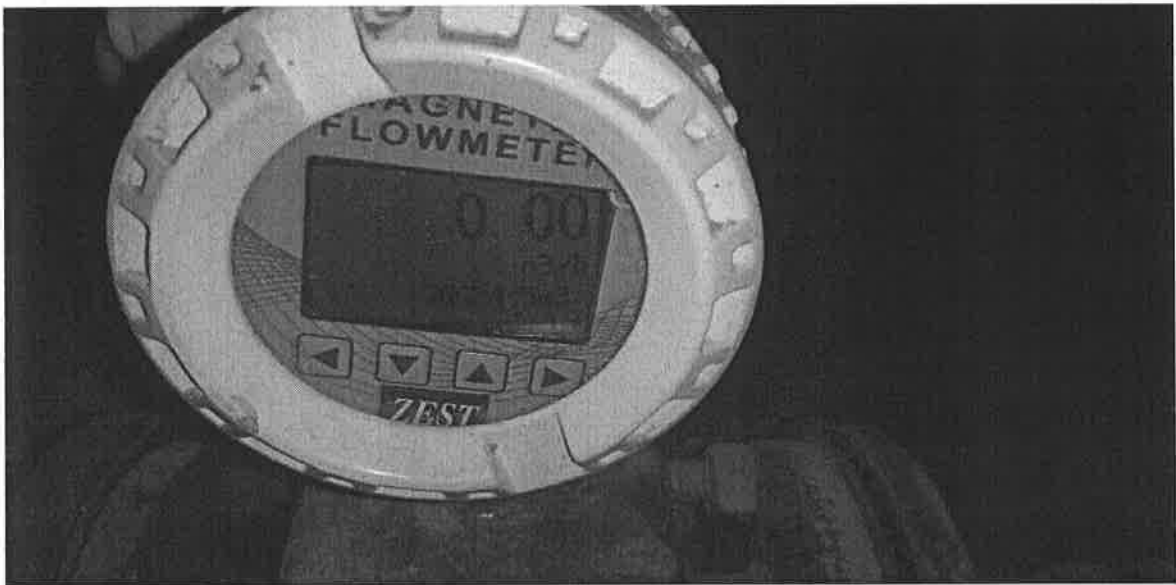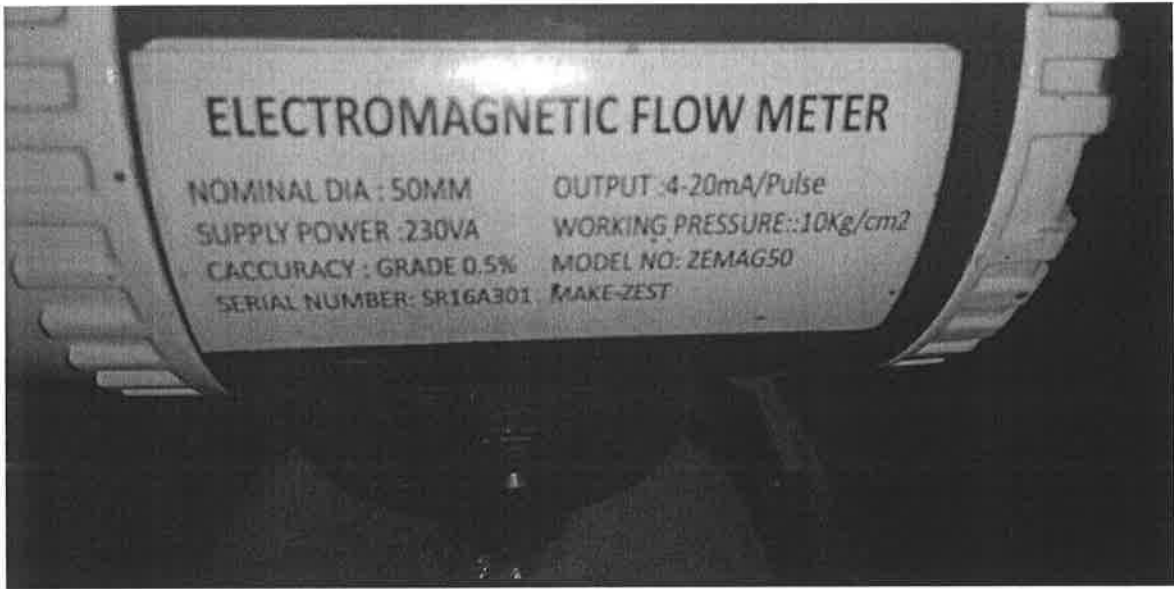

Borewell No.3

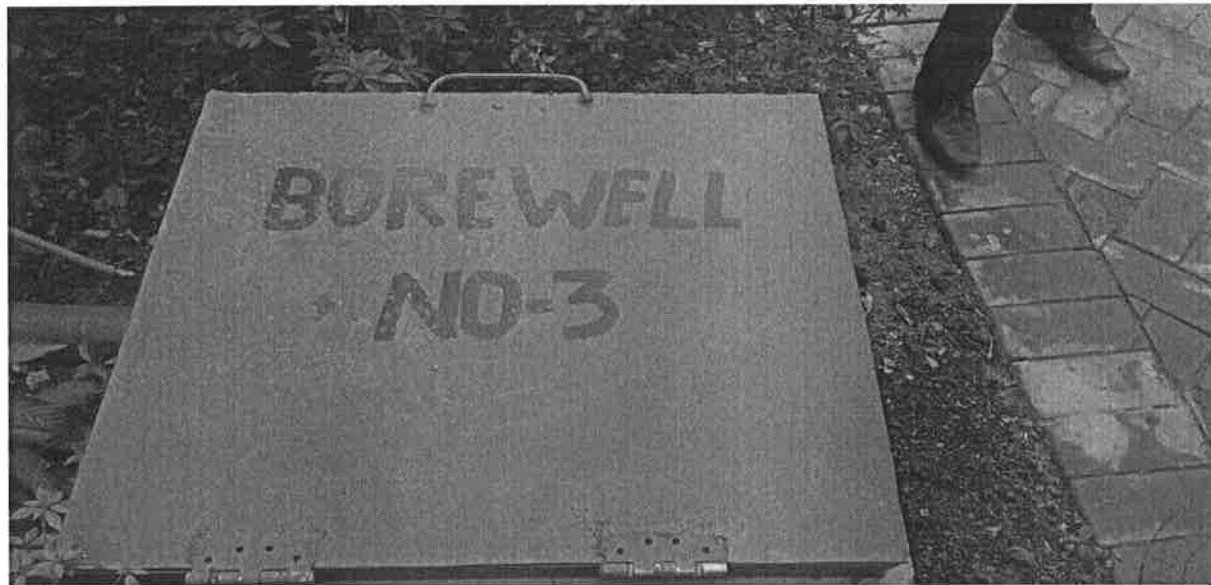

Borewell No. 4

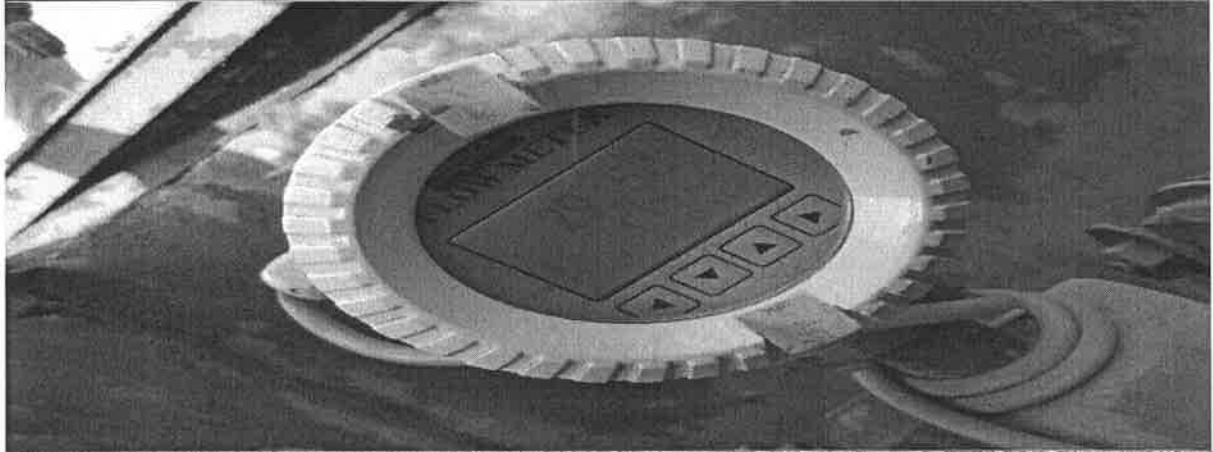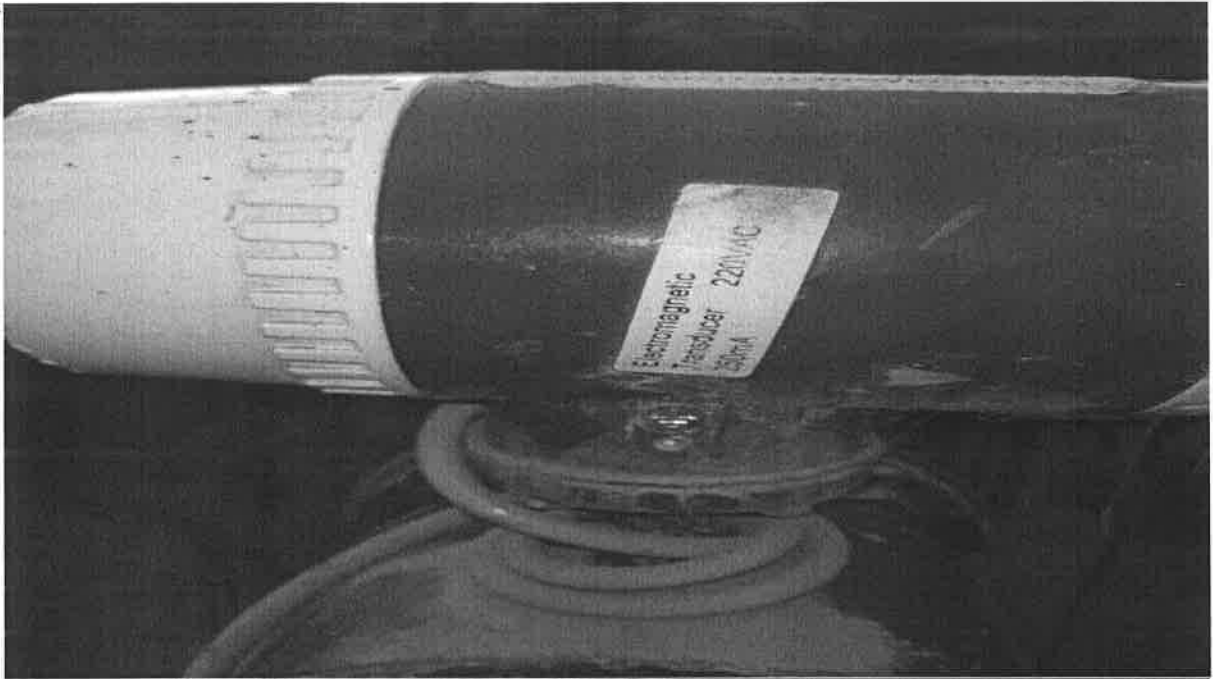

ED6415449751N INR:69686415449751N
SP NEW DELHI 6PO <110001>
Counter No:4,22/03/2024,18:2
To:MEMBER SECRET, CENTRAL GROUND W
PIN:110066, R K Puram Main SO
From:ASF INSGI, PAHARI
Wt:65gms
Amt:29.50 (Cash) Tax:4.50
<Track on www.indiapost.gov.in>
<Dial 18002666868> <Wear Masks, Stay Safe>

ASF
INSIGNIA

Office Copy.

Date: 02.08.2024

To,
Chairman, T.C.C
Cum Additional Deputy Commissioner, Gurgaon

Subject: Submission of CGWA compliance for IT/ Information Technology Enable Services (SEZ) project at Village- Gwal Pahari, Gurgaon – Faridabad road, Tehsil Wazirabad, District Gurgram, Haryana by M/s ASF Insignia SEZ Pvt. Ltd.

Reference No: Chairman, T.C.C cum Additional Deputy Commissioner, Gurgaon letter no. 1011 dated 23.11.2010

Dear Sir,

This is with reference to the above captioned subject; we are here with submitting quarterly compliance report for the period **April 2024 to June 2024** and The Ground Water Level monitoring report dated 08.07.2024 at 8 (eight) different locations at IT/ITES Project ASF Insignia SEZ Pvt. Ltd.

Thanking you,

For ASF INSGNIA SEZ PVT. LTD.



FOR. RECEIVED
FOR. ADC
22/08/2024

Authorised Signatory

Encl: As above

CC:

1. Member Secretary, CGWA, New Delhi.

2. Hydrologist Office, Ground Water Cell, Gurgaon, Haryana. →

Hydrologist = 8826011700 - Sunita majum.
(TA)

Received
Alok Kumar
22/08/2024

ASF INSGNIA SEZ PRIVATE LIMITED

Site Office : ASF Insignia SEZ (IT/ITES), Vatsal Valley (Gwal Pahari), off Gurugram-Faridabad Road, Gurugram-122003, Haryana

t: +91 124 4777200 f: +91 124 4234110 e: corporate@asfinfrastructure.com w: www.asfinfrastructure.com

Regd. Office : 11, Baber Lane, Bengali Market, New Delhi-110001 t: +91 11 23355511 f: +91 1123739288

Corp. Office : ASF Centre, 382-363, Udyog Vihar, Phase-IV, Gurugram-122016 (India)

CIN U45201DL2005PTC140408

Creating Intelligent Spaces®



COMPLIANCE OF THE CONDITIONS AS PER THE NO OBJECTION CERTIFICATE OBTAINED FROM CHAIRMAN, T.C.C CUM ADDITIONAL DEPUTY COMMISSIONER, GURGAON VIDE LETTER NO: 1011 DATED 23.11.2010 (ANNEXURE-I). PERIOD April 2024 – June 2024

CONDITIONS

S.NO.	CONDITIONS	COMPLIANCE
1	The ground water from the tube well shall be exclusively used for drinking purpose only and not for construction or any other purpose. The applicant will have to submit the undertaking on affidavit for the same.	Being Complied. The ground water from the tube well is being exclusively used for drinking purpose only. The affidavit stating the same has already been submitted.
2	The applicant shall take up Rain Water Harvesting system in project area.	Complied. Total 21. nos of Rain Water Harvesting Pits are operational at the site.
3	Treated waste water shall be utilized for gardening and flushing purposes by dual water supply system	Complied. Treated waste water is being utilized for gardening and flushing purposes by dual water supply system.
4	Photograph of the recharge structure is to be submitted immediately after completion to Chairman T.C.C. Gurgaon.	Complied. Photograph of the recharge structure has been submitted to the office of Chairman T.C.C. Cum Additional Deputy Commissioner Gurgaon.
5	After getting the drinking water supply from concerned Private/Govt. agency, applicant would not to be allowed abstraction of ground water through this tube well.	Noted.



6	The applicant will have to submit the depth, diameter, H.P. of primemover and exact location (Khasra no., Killa no.) as per revenue record of permitted tube well along with photograph within 15 days after getting permission letter. Otherwise the permission will be withdrawn. No further drilling or deeping of the tube well should be carried out.	Being Complied. Details already submitted
7	The ground water level in the tube wells is to be monitored at least quarterly (January, May, August & November) in a year on regular basis and ground water quality is to be monitored twice in a year during pre and post monsoon period and data to be submitted Hydrologist office, Ground Water Cell Gurgaon on regular basis.	Complied. We are regularly submitting the required data to your esteemed office. latest Ground Water Level report & Ground Water Test Report is attached as an <i>Annexure II & II-A</i> .
8	Violation of the above mentioned conditions, T.C.C. Gurgaon reserves its rights to withdraw/cancel the permission of the said tube well at any time without assigning any reason, if the contingency so demand	Noted.





RAJ BOREWELLS & PROJECTS

Specialists in : Rain Water Harversting, Tubewell Drilling, Dewatering,
Turnkey Projects, Re-development of Old Borewells

Office : Amichand Market, First Floor, Opp. Indian Oil Corp., Sector -13, By Pass Road, Faridabad-121007
E-mail:rajborewells2010@rediffmail.com / Phones : +91-98111-41355, 8585904007

Ref. No.

08.07.2024

M/s ASF INSIGNIA SEZ PVT. LTD.,
Village - Gwal Pahari,
Gurgaon, Haryana.

Sub: Checking of Water Level of the Existing Bores at site M/s ASF Insignia SEZ Pvt. Ltd., Village - Gwal Pahari, Tehsil - Sohna, Distt. - Gurgaon, Haryana (April - June 2024)

Dear Sir,

As per our findings, following are the water level of different bores for the period April - June 2024 at the subject site :

- | | | |
|------------------------|---|---|
| 1. Marked B.W No. I | - | Colling Tower WL at 145 ft. |
| 2. Marked B.W. No. II | - | Ground Floor, Tower 1 South WL at 140 ft. |
| 3. Marked B.W. No.III | - | Basement -3, Tower 3, WL at 92 ft. |
| 4. Marked B.W. No.IV | - | Housing Northwest WL at 142 ft. |
| 5. Marked B.W. No.V | - | Housing East WL at 146 ft. |
| 6. Marked B.W. No.VI | - | Behind residential building WL at 144 ft. |
| 7. Marked B.W. No. VII | - | North of B3 building 1 WL at 134 ft. |
| 8. Marked B.W. No.VIII | - | North of B3 Building 2 WL at 138 ft. |

Thanking you,

Yours truly,

For RAJ BOREWELLS & PROJECTS,





We Build Relations

EKO TESTING LABS[®]

Eko Pro Engineers Pvt. Ltd.

Contact : +91 - 9610243670

Competence | Quality | Service

TEST REPORT

Water Sample Analysis

Test Report No. : EKO/E-020/050624


Issue Date : 10/06/2024

Issued To : ASF INSIGNIA SEZ PVT. LTD.
Village -Gwal Pahari
Gurgaon Faridabad Road
Gurgaon (Haryana) -122003

Sample Description : Ground Water
Sample Drawn on : 05/06/2024
Sample Drawn by : EPEPL (Mr. Mohd. Shakir)
Sample Received on : 05/06/2024
Sampling Location : From Building No.-2
Sampling Plan & Procedure : SOP-W/66
Sample Quantity : 1.0 Litre
Environmental Conditions : Normal
Analysis Duration : 05/06/2024 To 10/06/2024
Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per IS:10500-2012 (Amd.No.3 Feb-2021)	
					Acceptable	Permissible
1	Colour	IS: 3025 (P-4)	<1.0	Hazen	5.0	15.0
2	Odour	IS: 3025 (P-5)	Agreeable	-	Agreeable	Agreeable
3	Taste	IS: 3025 (P-7)	Agreeable	-	Agreeable	Agreeable
4	Turbidity	IS: 3025 (P-10)	<1.0	NTU	1.0	5.0
5	pH	IS: 3025 (P-11)	7.21	-	6.5-8.5	No relaxation
6	Total Hardness (as CaCO ₃)	IS: 3025 (P-21)	268.0	mg/L	200.0	600.0
7	Iron (as Fe)	IS: 3025 (P-53)	<0.1	mg/L	1.0	No relaxation
8	Chloride (as Cl)	IS: 3025 (P-32)	84.5	mg/L	250.0	1000.0
9	Residual Free Chlorine	IS: 3025 (P-26)	<0.1	mg/L	0.2	1.0
10	Fluoride (as F)	IS: 3025 (P-60)	<1.0	mg/L	1.0	1.5
11	Total Dissolved Solids	IS: 3025 (P-16)	398.0	mg/L	500.0	2000.0
12	Total Alkalinity (as CaCO ₃)	IS: 3025 (P-23)	185.0	mg/L	200.0	600.0
13	Phenolic Compounds (as C ₆ H ₅ OH)	IS: 3025 (P-43)	<0.001	mg/L	0.001	0.002
14	Cyanide (as CN)	APHA 4500 CN-K	Absent	mg/L	0.05	No relaxation
15	Total Coliform	IS: 15185	Not Detected	Per 100mL	Absent	No relaxation
16	E.coli	IS: 15185	Not Detected	Per 100mL	Absent	No relaxation



Page 1 of 2



EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Contact : +91 - 9810243870

We Build Relations

Competence | Quality | Service

TEST REPORT

Water Sample Analysis

Test Report No. : EKO/E-022/050624

Issue Date : 10/06/2024


Issued To : ASF INSIGNIA SEZ PVT. LTD.
Village -Gwal Pahari
Gurgaon Faridabad Road
Gurgaon (Haryana) -122003

Sample Description : Ground Water
Sample Drawn on : 05/06/2024
Sample Drawn by : EPEPL (Mr. Mohd. Shakir)
Sample Received on : 05/06/2024
Sampling Location : From Building No.-3
Sampling Plan & Procedure : SOP-W/66
Sample Quantity : 1.0 Litre
Environmental Conditions : Normal
Analysis Duration : 05/06/2024 To 10/06/2024
Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per IS:10500-2012 (Amd.No.3 Feb-2021)	
					Acceptable	Permissible
1	Colour	IS: 3025 (P-4)	<1.0	Hazen	5.0	15.0
2	Odour	IS: 3025 (P-5)	Agreeable	-	Agreeable	Agreeable
3	Taste	IS: 3025 (P-7)	Agreeable	-	Agreeable	Agreeable
4	Turbidity	IS: 3025 (P-10)	<1.0	NTU	1.0	5.0
5	pH	IS: 3025 (P-11)	7.15	-	6.5-8.5	No relaxation
6	Total Hardness (as CaCO ₃)	IS: 3025 (P-21)	230.0	mg/L	200.0	600.0
7	Iron (as Fe)	IS: 3025 (P-53)	<0.1	mg/L	1.0	No relaxation
8	Chloride (as Cl)	IS: 3025 (P-32)	61.8	mg/L	250.0	1000.0
9	Residual Free Chlorine	IS: 3025 (P-26)	<0.1	mg/L	0.2	1.0
10	Fluoride (as F)	IS: 3025 (P-60)	<1.0	mg/L	1.0	1.5
11	Total Dissolved Solids	IS: 3025 (P-16)	324.0	mg/L	500.0	2000.0
12	Total Alkalinity (as CaCO ₃)	IS: 3025 (P-23)	174.0	mg/L	200.0	600.0
13	Phenolic Compounds (as C ₆ H ₅ OH)	IS: 3025 (P-43)	<0.001	mg/L	0.001	0.002
14	Cyanide (as CN)	APHA 4500 CN-K	Absent	mg/L	0.05	No relaxation
15	Total Coliform	IS: 15185	Not Detected	Per 100mL	Absent	No relaxation
16	E. coli	IS: 15185	Not Detected	Per 100mL	Absent	No relaxation

Remark:- Standard Applicable only for Drinking Water.



Page 1 of 2



EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Contact : +91 - 9810240870

We Build Relations

Competence | Quality | Service

TEST REPORT

Water Sample Analysis

Test Report No. : EKO/E-021/050624

Issue Date : 10/06/2024

Issued To : ASF INSIGNIA SEZ PVT. LTD.
 Village -Gwal Pahari
 Gurgaon Faridabad Road
 Gurgaon (Haryana) -122003


Sample Description : Ground Water
 Sample Drawn on : 05/06/2024
 Sample Drawn by : EPEPL (Mr. Mohd. Shakir)
 Sample Received on : 05/06/2024
 Sampling Location : Borewell (IDR)
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 1.0 Litre
 Environmental Conditions : Normal
 Analysis Duration : 05/06/2024 To 10/06/2024
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per IS:10500-2012 (Amd.No.3 Feb-2021)	
					Acceptable	Permissible
1	Colour	IS: 3025 (P-4)	<1.0	Hazen	5.0	15.0
2	Odour	IS: 3025 (P-5)	Agreeable	-	Agreeable	Agreeable
3	Taste	IS: 3025 (P-7)	Agreeable	-	Agreeable	Agreeable
4	Turbidity	IS: 3025 (P-10)	<1.0	NTU	1.0	5.0
5	pH	IS: 3025 (P-11)	7.18	-	6.5-8.5	No relaxation
6	Total Hardness (as CaCO ₃)	IS: 3025 (P-21)	230.0	mg/L	200.0	600.0
7	Iron (as Fe)	IS: 3025 (P-53)	<0.1	mg/L	1.0	No relaxation
8	Chloride (as Cl)	IS: 3025 (P-32)	60.5	mg/L	250.0	1000.0
9	Residual Free Chlorine	IS: 3025 (P-26)	<0.1	mg/L	0.2	1.0
10	Fluoride (as F)	IS: 3025 (P-60)	<1.0	mg/L	1.0	1.5
11	Total Dissolved Solids	IS: 3025 (P-16)	348.0	mg/L	500.0	2000.0
12	Total Alkalinity (as CaCO ₃)	IS: 3025 (P-23)	177.0	mg/L	200.0	600.0
13	Phenolic Compounds (as C ₆ H ₅ OH)	IS: 3025 (P-43)	<0.001	mg/L	0.001	0.002
14	Cyanide (as CN)	APHA 4500 CN-K	Absent	mg/L	0.05	No relaxation
15	Total Coliform	IS: 15185	Not Detected	Per 100mL	Absent	No relaxation
16	E.coli	IS: 15185	Not Detected	Per 100mL	Absent	No relaxation



Page 1 of 2





We Build Relations

EKO TESTING LABS[®]

Eko Pro Engineers Pvt. Ltd.

Contact : +91 - 9810243670

Competence | Quality | Service

TEST REPORT

Water Sample Analysis

Test Report No. : EKO/E-547/050624


Issue Date : 10/06/2024

Issued To : ASF INSIGNIA SEZ PVT. LTD.
Village -Gwal Pahari
Gurgaon Faridabad Road
Gurgaon (Haryana) -122003

Sample Description : Ground Water
Sample Drawn on : 05/06/2024
Sample Drawn by : EPEPL (Mr. Mohd. Shakir)
Sample Received on : 05/06/2024
Sampling Location : From Stand By Borewell
Sampling Plan & Procedure : SOP-W/66
Sample Quantity : 1.0 Litre
Environmental Conditions : Normal
Analysis Duration : 05/06/2024 To 10/06/2024
Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per IS:10500-2012 (Amd.No.3 Feb-2021)	
					Acceptable	Permissible
1	Colour	IS: 3025 (P-4)	<1.0	Hazen	5.0	15.0
2	Odour	IS: 3025 (P-5)	Agreeable	-	Agreeable	Agreeable
3	Taste	IS: 3025 (P-7)	Agreeable	-	Agreeable	Agreeable
4	Turbidity	IS: 3025 (P-10)	<1.0	NTU	1.0	5.0
5	pH	IS: 3025 (P-11)	7.32	-	6.5-8.5	No relaxation
6	Total Hardness (as CaCO ₃)	IS: 3025 (P-21)	275.0	mg/L	200.0	600.0
7	Iron (as Fe)	IS: 3025 (P-53)	<0.1	mg/L	1.0	No relaxation
8	Chloride (as Cl)	IS: 3025 (P-32)	90.5	mg/L	250.0	1000.0
9	Residual Free Chlorine	IS: 3025 (P-26)	<0.1	mg/L	0.2	1.0
10	Fluoride (as F)	IS: 3025 (P-60)	<1.0	mg/L	1.0	1.5
11	Total Dissolved Solids	IS: 3025 (P-16)	410.0	mg/L	500.0	2000.0
12	Total Alkalinity (as CaCO ₃)	IS: 3025 (P-23)	186.0	mg/L	200.0	600.0
13	Phenolic Compounds (as C ₆ H ₅ OH)	IS: 3025 (P-43)	<0.001	mg/L	0.001	0.002
14	Cyanide (as CN)	APHA 4500 CN-K	Absent	mg/L	0.05	No relaxation
15	Total Coliform	IS: 15185	Not Detected	Per 100mL	Absent	No relaxation
16	E.coli	IS: 15185	Not Detected	Per 100mL	Absent	No relaxation



Page 1 of 2

B-1

From

Chairman, T.C.C.
Cum Additional Deputy Commissioner, Gurgaon.

To

Canton Buildwell Pvt Ltd, 3623/3 ASF Centre Vidyog Vihar

No. 1011 dated

IV
Gurgaon

Sub:
Memo.

N.O.C. for regularization of existing tubewells for drinking & domestic purpose.

With reference to your application no _____ dated 2-8-2010 on the above cited subject the Technical Core Committee has no objection for withdrawal of ground water from existing Eight tubewell located at Village Gawal Puhali.

The N.O.C. is subject to the following terms & conditions :-

- 1 The ground water from the tubewell shall be exclusively used for drinking & domestic purpose only and not for construction or any other purposes. The applicant will have to submit the undertaking on affidavit for the same.
- 2 The applicant shall take up Rain Water Harvesting scheme in the project area.
- 3 Treated waste water shall be utilized for gardening and flushing purposes by providing dual water supply system.
- 4 Photograph of the recharge structure is to be submitted immediately after completion to the chairman T.C.C. Gurgaon.
- 5 After getting the drinking water supply from concerned Private/Govt agency, the applicant would not be allowed abstraction of ground water through this tubewell.
- 6 The applicant will have to submit the depth, diameter, H.P. of primemover and exact location (Khasra no., Killa no.) as per revenue record of the permitted tubewell alongwith photograph within 15 days after getting permission letter, otherwise the permission will be withdrawn. No further drilling or deeping of the tubewell should be carried out.
- 7 The ground water level in the tubewells is to be monitored atleast quarterly (January, May, August & November) in a year on regular basis and ground water quality is to be monitored twice in a year during pre & post monsoon period and data to be submitted to Hydrologist office, Ground Water Cell Gurgaon on regular basis.
- 8 Violation of the above mentioned conditions, T.C.C. Gurgaon reserves its rights to withdraw/cancel the permission of the said tubewell at any time without assigning any reason, if the contingency so demand.

Chairman, T.C.C.

Cum Additional Deputy Commissioner, Gurgaon.

No. 1012 dated

A copy is forwarded to Member Secretary, C.G.W.A. New Delhi for favour of information & necessary action please.

Chairman, T.C.C.

Cum Additional Deputy Commissioner, Gurgaon.

Handwritten signatures and dates:
28/11
28/3/16

B. S. YADAV HAS-II
Asst. Geologist
Ground Water Cell, Gurgaon



Handwritten notes:
o/c
As per record available the copy has been compared with the original office copy and found correct.

Handwritten signature and date:
28/3/16

Date: 25.03.2016



To,

de

The Chairman-TCC
Cum Addl. Dy. Commissioner,
Vikas Sadan
Gurgaon

Sub.: Request for providing original copy/ certified copy of the NOC dated 23.11.2010 granted to Canton Buildwell Pvt. Ltd.(Now) ASF Insignia SEZ Pvt. Ltd.) for 8 tubewells for drinking and domestic purposes.

Ref.: Your NOC vide Memo No. 1011 dated 23.11.2010

Dear Sir,

This has reference to the above referred NOC dated 23.11.2010 issued to Canton Buildwell Pvt. Ltd. (now known as ASF Insignia SEZ Pvt Ltd.). This is to bring to your kind notice that the original copy of the above mentioned NOC is somehow not traceable in our records, and perhaps it was never received by us, and we are having only a copy of the office copy of the Deptt. in our records.

It is therefore requested that we may kindly be provided with the original copy of the said NOC issued in our favour vide Memo No. 1011 dated 23.11.2010.

In the alternate, we may be provided with a duly authenticated /certified copy of the said NOC at the earliest.

Thanking you,

Yours faithfully,
For ASF INSIGNIA SEZ PVT.LTD.
(formerly known as Canton Buildwell Pvt. Ltd.)

AUTHORIZED SIGNATORY

Encl. Photocopy of NOC vide Memo No. 1011 dated 23.11.2010.

Hydrologist To supply
URGENT certified copy
Put up on.....
.....urgently.
ADC

ASF INSIGNIA SEZ PRIVATE LIMITED
Corp Office: ASF Centre, 362-363, Udyog Vihar, Phase-IV, Gurgaon-122016 (India)
T: +91 124 4777200 F: +91 124 4234110 e: corporate@asfinfrastructure.com w: www.asfinfrastructure.com
Regd. Office - 11, Bahar Lane, Bengali Market, New Delhi-110001 T: +91 11 23353511 F: +91 1123739296
CIN U45201DL2006PTC140408

Creating Intelligent Spaces®





Office COPY

Date: 06.11.2024

To,
Chairman, T.C.C
Cum Additional Deputy Commissioner, Gurgaon

Subject: Submission of CGWA compliance for IT/ Information Technology Enable Services (SEZ) project at Village- Gwal Pahari, Gurgaon – Faridabad road, Tehsil Wazirabad, District Gurugram, Haryana by M/s ASF Insignia SEZ Pvt. Ltd.

Reference No: Chairman, T.C.C cum Additional Deputy Commissioner, Gurgaon letter no. 1011 dated 23.11.2010

Dear Sir,

This is with reference to the above captioned subject; we are here with submitting quarterly compliance report for the period **July 2024 to September 2024** and The Ground Water Level monitoring report dated 08.10.2024 at 8 (eight) different locations at IT/ITES Project ASF Insignia SEZ Pvt. Ltd.

Thanking you,

For ASF INSIGNIA SEZ PVT. LTD.

Authorised Signatory

Encl: As above

CC:

1. Member Secretary, CGWA, New Delhi.
2. Hydrologist Office, Ground Water Cell, Gurgaon, Haryana.

EDB09530104IM TVR24956309530104
SF MARKET ROAD INPL SF HUB (110001)
Counter No:1,06/11/2024,17:00
To: NUMBER SEFTY, CENTRAL GURAM
PIN:110016, R. K. Puram Main St
From:ASF INSIGNIA SEZ, 362
Wt:52gms
Amt:29.50, Tax:4.50, Amt.Paid:30.00(Cash)
Track on www.indiapost.gov.in

Handwritten signature and date 06/11/24

Handwritten signature and date 06/11/24

ASF INSIGNIA SEZ PRIVATE LIMITED

Site Office : ASF Insignia SEZ (IT/ITes), Vatsal Valley (Gwal Pahari), off Gurugram-Faridabad Road, Gurugram-122003, Haryana

T: +91 124 2557100 F: +91 124 2557135 E: corporate@asfinfrastructure.com W: www.asfinfrastructure.com

Regd. Office : 11, Babar Lane, Bengali Market, New Delhi-110 001 T: +91 11 23355511 F: +91 1123739298

Corp. Office : ASF Centre, 362-363, Udyog Viher, Phase-IV, Gurugram-122016 (India) T: +91 124 4777200 F: +91 124 4234110

CIN U45201DL2005PTC140408

Creating Intelligent Spaces®

COMPLIANCE OF THE CONDITIONS AS PER THE NO OBJECTION CERTIFICATE OBTAINED FROM CHAIRMAN, T.C.C CUM ADDITIONAL DEPUTY COMMISSIONER, GURGAON VIDE LETTER NO: 1011 DATED 23.11.2010 (ANNEXURE-I). PERIOD July 2024 – September 2024

CONDITIONS

S.NO.	CONDITIONS	COMPLIANCE
1	The ground water from the tube well shall be exclusively used for drinking purpose only and not for construction or any other purpose. The applicant will have to submit the undertaking on affidavit for the same.	Being Complied. The ground water from the tube well is being exclusively used for drinking purpose only. The affidavit stating the same has already been submitted.
2	The applicant shall take up Rain Water Harvesting system in project area.	Complied. Total 21. nos of Rain Water Harvesting Pits are operational at the site.
3	Treated waste water shall be utilized for gardening and flushing purposes by dual water supply system	Complied. Treated waste water is being utilized for gardening and flushing purposes by dual water supply system.
4	Photograph of the recharge structure is to be submitted immediately after completion to Chairman T.C.C. Gurgaon.	Complied. Photograph of the recharge structure has been submitted to the office of Chairman T.C.C. Cum Additional Deputy Commissioner Gurgaon.
5	After getting the drinking water supply from concerned Private/Govt. agency, applicant would not to be allowed abstraction of ground water through this tube well.	Noted.



6	The applicant will have to submit the depth, diameter, H.P. of primemover and exact location (Khasra no., Killa no.) as per revenue record of permitted tube well along with photograph within 15 days after getting permission letter. Otherwise the permission will be withdrawn. No further drilling or deeping of the tube well should be carried out.	Being Complied. Details already submitted
7	The ground water level in the tube wells is to be monitored at least quarterly (January, May, August & November) in a year on regular basis and ground water quality is to be monitored twice in a year during pre and post monsoon period and data to be submitted Hydrologist office, Ground Water Cell Gurgaon on regular basis.	Complied. We are regularly submitting the required data to your esteemed office. latest Ground Water Level report & Ground Water Test Report is attached as an <i>Annexure II & II-A</i> .
8	Violation of the above mentioned conditions, T.C.C. Gurgaon reserves its rights to withdraw/cancel the permission of the said tube well at any time without assigning any reason, if the contingency so demand	Noted.





RAJ BOREWELLS & PROJECTS

Specialists in : Rain Water Harvesting, Tubewell Drilling, Dewatering,
Turnkey Projects, Re-development of Old Borewells

Office : Amichand Market, First Floor, Opp. Indian Oil Corp., Sector -13, By Pass Road, Faridabad-121007
E-mail: rajborewells2010@rediffmail.com / Phones : +91-98111-41355, 8585904007

Ref. No. _____

Date: 08.10.2024

M/s ASF INSIGNIA SEZ PVT. LTD.,
Village - Gwal Pahari,
Gurgaon, Haryana.

Sub: Checking of Water Level of the Existing Bores at site M/s ASF Insignia SEZ Pvt. Ltd., Village - Gwal Pahari, Tehsil - Sohna, Distt. - Gurgaon, Haryana (July - September 2024)

Dear Sir,

As per our findings, following are the water level of different bores for the period July - September 2024 at the subject site :

- | | | |
|-------------------------|---|---|
| 1. Marked B.W. No. I | - | Colling Tower WL at 144 ft. |
| 2. Marked B.W. No. II | - | Ground Floor, Tower 1 South WL at 142 ft. |
| 3. Marked B.W. No. III | - | Basement -3, Tower 3, WL at 97 ft. |
| 4. Marked B.W. No. IV | - | Housing Northwest WL at 158 ft. |
| 5. Marked B.W. No. V | - | Housing East WL at 142 ft. |
| 6. Marked B.W. No. VI | - | Behind residential building WL at 144 ft. |
| 7. Marked B.W. No. VII | - | North of B3 building 1 WL at 137 ft. |
| 8. Marked B.W. No. VIII | - | North of B3 Building 2 WL at 143 ft. |

Thanking you,

Yours truly

For RAJ BOREWELLS & PROJECTS,

(Auth. Signatory)







We Build Relations

EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Contact : +91 - 9810243570

Competence | Quality | Service

TEST REPORT

Water Sample Analysis

Test Report No. : EKO/E-020/050624

Issue Date : 10/06/2024

Issued To

: ASF INSIGNIA SEZ PVT. LTD.
Village -Gwal Pahari
Gurgaon Faridabad Road
Gurgaon (Haryana) -122003

Sample Description : Ground Water
Sample Drawn on : 05/06/2024
Sample Drawn by : EPEPL (Mr. Mohd. Shakir)
Sample Received on : 05/06/2024
Sampling Location : From Building No.-2
Sampling Plan & Procedure : SOP-W/66
Sample Quantity : 1.0 Litre
Environmental Conditions : Normal
Analysis Duration : 05/06/2024 To 10/06/2024
Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per IS:10500-2012 (Amd.No.3 Feb-2021)	
					Acceptable	Permissible
1	Colour	IS: 3025 (P-4)	<1.0	Hazen	5.0	15.0
2	Odour	IS: 3025 (P-5)	Agreeable	—	Agreeable	Agreeable
3	Taste	IS: 3025 (P-7)	Agreeable	—	Agreeable	Agreeable
4	Turbidity	IS: 3025 (P-10)	<1.0	NTU	1.0	5.0
5	pH	IS: 3025 (P-11)	7.21	—	6.5-8.5	No relaxation
6	Total Hardness (as CaCO ₃)	IS: 3025 (P-21)	268.0	mg/L	200.0	600.0
7	Iron (as Fe)	IS: 3025 (P-53)	<0.1	mg/L	1.0	No relaxation
8	Chloride (as Cl)	IS: 3025 (P-32)	84.5	mg/L	250.0	1000.0
9	Residual Free Chlorine	IS: 3025 (P-26)	<0.1	mg/L	0.2	1.0
10	Fluoride (as F)	IS: 3025 (P-60)	<1.0	mg/L	1.0	1.5
11	Total Dissolved Solids	IS: 3025 (P-16)	398.0	mg/L	500.0	2000.0
12	Total Alkalinity (as CaCO ₃)	IS: 3025 (P-23)	185.0	mg/L	200.0	600.0
13	Phenolic Compounds (as C ₆ H ₅ OH)	IS: 3025 (P-43)	<0.001	mg/L	0.001	0.002
14	Cyanide (as CN)	APHA 4500 CN-K	Absent	mg/L	0.05	No relaxation
15	Total Coliform	IS: 15185	Not Detected	Per 100mL	Absent	No relaxation
16	E.coli	IS: 15185	Not Detected	Per 100mL	Absent	No relaxation



Page 1 of 2



EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

We Build Relations

Competence | Quality | Service

TEST REPORT

Water Sample Analysis

Test Report No. : EKO/E-022/050624

Issue Date : 10/06/2024


Issued To : ASF INSIGNIA SEZ PVT. LTD.
 Village -Gwal Pahari
 Gurgaon Faridabad Road
 Gurgaon (Haryana) -122003

Sample Description : Ground Water
 Sample Drawn on : 05/06/2024
 Sample Drawn by : EPEPL (Mr. Mohd. Shakir)
 Sample Received on : 05/06/2024
 Sampling Location : From Building No.-3
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 1.0 Litre
 Environmental Conditions : Normal
 Analysis Duration : 05/06/2024 To 10/06/2024
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per IS:10500-2012 (Amd.No.3 Feb-2021)	
					Acceptable	Permissible
1	Colour	IS: 3025 (P-4)	<1.0	Hazen	5.0	15.0
2	Odour	IS: 3025 (P-5)	Agreeable	-	Agreeable	Agreeable
3	Taste	IS: 3025 (P-7)	Agreeable	-	Agreeable	Agreeable
4	Turbidity	IS: 3025 (P-10)	<1.0	NTU	1.0	5.0
5	pH	IS: 3025 (P-11)	7.15	-	6.5-8.5	No relaxation
6	Total Hardness (as CaCO ₃)	IS: 3025 (P-21)	230.0	mg/L	200.0	600.0
7	Iron (as Fe)	IS: 3025 (P-53)	<0.1	mg/L	1.0	No relaxation
8	Chloride (as Cl)	IS: 3025 (P-32)	61.8	mg/L	250.0	1000.0
9	Residual Free Chlorine	IS: 3025 (P-26)	<0.1	mg/L	0.2	1.0
10	Fluoride (as F)	IS: 3025 (P-60)	<1.0	mg/L	1.0	1.5
11	Total Dissolved Solids	IS: 3025 (P-16)	324.0	mg/L	500.0	2000.0
12	Total Alkalinity (as CaCO ₃)	IS: 3025 (P-23)	174.0	mg/L	200.0	600.0
13	Phenolic Compounds (as C ₆ H ₅ OH)	IS: 3025 (P-43)	<0.001	mg/L	0.001	0.002
14	Cyanide (as CN)	APHA 4500 CN-K	Absent	mg/L	0.05	No relaxation
15	Total Coliform	IS: 15185	Not Detected	Per 100mL	Absent	No relaxation
16	E. coli	IS: 15185	Not Detected	Per 100mL	Absent	No relaxation

Remark:- Standard Applicable only for Drinking Water.



Page 1 of 2



EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Contact: +91-9810248870

We Build Relations

Competence | Quality | Service

TEST REPORT

Water Sample Analysis

Test Report No. : EKO/E-021/050624


Issue Date : 10/06/2024

Issued To : ASF INSIGNIA SEZ PVT. LTD.
Village -Gwal Pahari
Gurgaon Faridabad Road
Gurgaon (Haryana) -122003

Sample Description : Ground Water
Sample Drawn on : 05/06/2024
Sample Drawn by : EPEPL (Mr. Mohd. Shakir)
Sample Received on : 05/06/2024
Sampling Location : Borewell (IDR)
Sampling Plan & Procedure : SOP-W/66
Sample Quantity : 1.0 Litre
Environmental Conditions : Normal
Analysis Duration : 05/06/2024 To 10/06/2024
Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per IS:10500-2012 (Amd.No.3 Feb-2021)	
					Acceptable	Permissible
1	Colour	IS: 3025 (P-4)	<1.0	Hazen	5.0	15.0
2	Odour	IS: 3025 (P-5)	Agreeable	-	Agreeable	Agreeable
3	Taste	IS: 3025 (P-7)	Agreeable	-	Agreeable	Agreeable
4	Turbidity	IS: 3025 (P-10)	<1.0	NTU	1.0	5.0
5	pH	IS: 3025 (P-11)	7.18	-	6.5-8.5	No relaxation
6	Total Hardness (as CaCO ₃)	IS: 3025 (P-21)	230.0	mg/L	200.0	600.0
7	Iron (as Fe)	IS: 3025 (P-53)	<0.1	mg/L	1.0	No relaxation
8	Chloride (as Cl)	IS: 3025 (P-32)	60.5	mg/L	250.0	1000.0
9	Residual Free Chlorine	IS: 3025 (P-26)	<0.1	mg/L	0.2	1.0
10	Fluoride (as F)	IS: 3025 (P-60)	<1.0	mg/L	1.0	1.5
11	Total Dissolved Solids	IS: 3025 (P-16)	348.0	mg/L	500.0	2000.0
12	Total Alkalinity (as CaCO ₃)	IS: 3025 (P-23)	177.0	mg/L	200.0	600.0
13	Phenolic Compounds (as C ₆ H ₅ OH)	IS: 3025 (P-43)	<0.001	mg/L	0.001	0.002
14	Cyanide (as CN)	APHA 4500 CN-K	Absent	mg/L	0.05	No relaxation
15	Total Coliform	IS: 15185	Not Detected	Per 100mL	Absent	No relaxation
16	E.coli	IS: 15185	Not Detected	Per 100mL	Absent	No relaxation



Page 1 of 2



EKO TESTING LABS®

Eko Pro Engineers Pvt. Ltd.

Contact: +91 - 9610249370

We Build Relations

Competence | Quality | Service

TEST REPORT


Water Sample Analysis

Test Report No. : EKO/E-547/050624 Issue Date : 10/06/2024
 Issued To : ASF INSIGNIA SEZ PVT. LTD.
 Village -Gwal Pahari
 Gurgaon Faridabad Road
 Gurgaon (Haryana) -122003

Sample Description : Ground Water
 Sample Drawn on : 05/06/2024
 Sample Drawn by : EPEPL (Mr. Mohd. Shakir)
 Sample Received on : 05/06/2024
 Sampling Location : From Stand By Borewell
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 1.0 Litre
 Environmental Conditions : Normal
 Analysis Duration : 05/06/2024 To 10/06/2024
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per IS:10500-2012 (Amd.No.3 Feb-2021)	
					Acceptable	Permissible
1	Colour	IS: 3025 (P-4)	<1.0	Hazen	5.0	15.0
2	Odour	IS: 3025 (P-5)	Agreeable	-	Agreeable	Agreeable
3	Taste	IS: 3025 (P-7)	Agreeable	-	Agreeable	Agreeable
4	Turbidity	IS: 3025 (P-10)	<1.0	NTU	1.0	5.0
5	pH	IS: 3025 (P-11)	7.32	-	6.5-8.5	No relaxation
6	Total Hardness (as CaCO ₃)	IS: 3025 (P-21)	275.0	mg/L	200.0	600.0
7	Iron (as Fe)	IS: 3025 (P-53)	<0.1	mg/L	1.0	No relaxation
8	Chloride (as Cl)	IS: 3025 (P-32)	90.5	mg/L	250.0	1000.0
9	Residual Free Chlorine	IS: 3025 (P-26)	<0.1	mg/L	0.2	1.0
10	Fluoride (as F)	IS: 3025 (P-60)	<1.0	mg/L	1.0	1.5
11	Total Dissolved Solids	IS: 3025 (P-16)	410.0	mg/L	500.0	2000.0
12	Total Alkalinity (as CaCO ₃)	IS: 3025 (P-23)	188.0	mg/L	200.0	600.0
13	Phenolic Compounds (as C ₆ H ₅ OH)	IS: 3025 (P-43)	<0.001	mg/L	0.001	0.002
14	Cyanide (as CN)	APHA 4500 CN-K	Absent	mg/L	0.05	No relaxation
15	Total Coliform	IS: 15185	Not Detected	Per 100mL	Absent	No relaxation
16	E.coli	IS: 15185	Not Detected	Per 100mL	Absent	No relaxation



Page 1 of 2



B-1

From

Chairman, T.C.C.
Cum Additional Deputy Commissioner, Gurgaon.

To

Conston Buildwell Pvt Ltd, 3623/3 ASF Centre Ndyog vishodh

No. 1011 dated

IV
Gurgaon

Sub:
Memo.

N.O.C. for regularization of existing tubewells for drinking & domestic purpose.

With reference to your application no _____ dated
2-8-2010 on the above cited subject the Technical Core Committee
has no objection for withdrawal of ground water from existing Eight
tubewell located at Village Gawal Pahari.

The N.O.C. is subject to the following terms & conditions :-

- 1 The ground water from the tubewell shall be exclusively used for drinking & domestic purpose only and not for construction or any other purposes. The applicant will have to submit the undertaking on affidavit for the same.
- 2 The applicant shall take up Rain Water Harvesting scheme in the project area.
- 3 Treated waste water shall be utilized for gardening and flushing purposes by providing dual water supply system.
- 4 Photograph of the recharge structure is to be submitted immediately after completion to the chairman T.C.C. Gurgaon.
- 5 After getting the drinking water supply from concerned Private/Govt agency, the applicant would not be allowed abstraction of ground water through this tubewell.
- 6 The applicant will have to submit the depth, diameter, H.P. of primemover and exact location (Khasra no., Killa no.) as per revenue record of the permitted tubewell alongwith photograph within 15 days after getting permission letter, otherwise the permission will be withdrawn. No further drilling or deeping of the tubewell should be carried out.
- 7 The ground water level in the tubewells is to be monitored atleast quarterly (January, May, August & November) in a year on regular basis and ground water quality is to be monitored twice in a year during pre & post monsoon period and data to be submitted to Hydrologist office, Ground Water Cell Gurgaon on regular basis.
- 8 Violation of the above mentioned conditions, T.C.C. Gurgaon reserves its rights to withdraw/cancel the permission of the said tubewell at any time without assigning any reason, if the contingency so demand.

Chairman, T.C.C.

Cum Additional Deputy Commissioner, Gurgaon.

No. 1012 dated


A copy is forwarded to Member Secretary, C.G.W.A. New Delhi for favour of information & necessary action please.

Chairman, T.C.C.

Cum Additional Deputy Commissioner, Gurgaon.

Approved by
B. S. YADAV
25/3/16

B. S. YADAV HAS-II
Asst. Geologist
Ground Water Cell, Gurgaon



As per record available the copy
has been compared with the original
office copy and found correct

13
25/3/16

Date: 25.03.2016



To,

or

The Chairman-TCC
Cum Addl. Dy. Commissioner,
Vikas Sadan
Gurgaon

Sub.: Request for providing original copy/ certified copy of the NOC dated 23.11.2010 granted to Canton Buildwell Pvt. Ltd.(Now) ASF Insignia SEZ Pvt. Ltd.) for 8 tubewells for drinking and domestic purposes.

Ref.: Your NOC vide Memo No. 1011 dated 23.11.2010

Dear Sir,

This has reference to the above referred NOC dated 23.11.2010 issued to Canton Buildwell Pvt. Ltd. (now known as ASF Insignia SEZ Pvt Ltd.). This is to bring to your kind notice that the original copy of the above mentioned NOC is somehow not traceable in our records, and perhaps it was never received by us, and we are having only a copy of the office copy of the Deptt. in our records.

It is therefore requested that we may kindly be provided with the original copy of the said NOC issued in our favour vide Memo No. 1011 dated 23.11.2010.

In the alternate, we may be provided with a duly authenticated /certified copy of the said NOC at the earliest.

Thanking you,

Yours faithfully,
For ASF INSIGNIA SEZ PVT.LTD.
(formerly known as Canton Buildwell Pvt. Ltd.)

AUTHORIZED SIGNATORY

Encl. Photocopy of NOC vide Memo No. 1011 dated 23.11.2010.

Hydrologist To supply
URGENT certified copy
Put up on.....
urgently.
KDC

ASF INSIGNIA SEZ PRIVATE LIMITED
Corp. Office: ASF Centre, 362-363, Udyog Vihar, Phase-IV, Gurgaon- 122016 (India)
t: +91 124 4777200 f: +91 124 4234110 e: corporate@asfinfrastructure.com w: www.asfinfrastructure.com
Regd. Office: 11, Babar Lane, Bengali Market, New Delhi-110001 T: +91 11 23353511 F: +91 1123739298
CIN U45201DL2005PTC140409

Creating Intelligent Spaces®



ANNEXURE - VIII



olc

04.03.2024

To,

The Regional Officer,
Haryana State Pollution Control Board
Gurgaon

Sub.: Submission of Form- V, Environmental Statement for the financial year 01.04.2023 to 31.03.2024

Dear Sir,

We are enclosing herewith Form-V for the period from **01.04.2023 to 31.03.2024** i.e. Environmental Statement for the financial year 2023 to 2024 for our site at Village Gwal Pahari, Tehsil Wazirabad Dist. Gurgaon (Haryana).

Thanking you,
Yours faithfully,

For ASF INSIGNIA SEZ PVT.LTD.


Authorized Signatory

Encl: As Above

CC: The Chairman
Haryana State Pollution Control Board,
C-11, Sector-6, Panchkula

ED6305014971N IVR:6966300501493
SP PATPARGANJ SD (110091)
Counter No:1,19/04/2024,09:30
To:REGIONAL OFFICER,
PIN:122001, Gurgaon HD
From:ASF INSIGNIA,ASF CENTRE UDHYO
Wt:70gms
Amt:27.50(Cash)Tax:4.50



(Track on www.indiaospf.gov.in)
(Dial) 18002660000 (Wear Masks, Stay Safe)

ED6305010563N IVR:6966300501055
SP PATPARGANJ SD (110091)
Counter No:1,19/04/2024,09:30
To:HARYANA STATE,
PIN:134107, Panchkula Sector 6 S.D
From:ASF INSIGNIA,ASF CENTRE UDHYO
Wt:70gms
Amt:47.20(Cash)Tax:7.20



(Track on www.indiaospf.gov.in)
(Dial) 18002660000 (Wear Masks, Stay Safe)

ASF INSIGNIA SEZ PRIVATE LIMITED

Site Office : ASF Insignia SEZ (IT/ITES), Vatsal Valley (Gwal Pahari), off Gurugram-Faridabad Road, Gurugram-122003, Haryana

t: +91 124 4777200 f: +91 124 4234110 e: corporate@asfinfrastructure.com w: www.asfinfrastructure.com

Regd. Office : 11, Beber Lane, Bengali Market, New Delhi-110001 t: +91 11 29355511 f: +91 1123738298

Corp. Office : ASF Centre, 3B2-3B3, Udyog Vihar, Phase-IV, Gurugram-122016 (India)

CIN U45201DL2006PTC140408

Creating Intelligent Spaces®



FORM - V
(See Rule-14)

Environmental Statement for the financial year 01.04.2023 - 31.03.2024

Part-A

- (i) Name and address of owner/occupier of the Industry, operation or process : ASF Insignia SEZ Pvt. Ltd.
Village Gwal Pahari, Sub-Tehsil
Wazirabad, Distt. Gurgaon, Haryana
- (ii) Industry category: Primary (STC code) : IT/ ITES Special Economic Zone
Secondary- (SIC Code)
- (iii) Production capacity: Units : Not Applicable
- (iv) Year of establishment : November, 2011
- (v) Date of last environmental statement submitted :

Part - B

Water and Raw material consumption

(i) Water consumption m³/day:

- Process : NIL
Cooling : 79.48 m³ /day (79.48 m³ /day treated sewage)
Domestic : 307 m³/day (307 m³/day extracted from ground through approved tube well)
Horticulture : 157.46 m³ /day (157.46 m³ /day treated sewage)

HUDA WATER SOURCE NOT PROVIDED YET

S. No.	Name of Products	Process water consumption per unit of product output	
		During the previous financial year	During the current financial year
1.	Not Applicable	Not Applicable	Not Applicable

(ii) Raw Material consumption : Not Applicable

S. No.	*Name of Raw Material	Name of Products	Consumption of raw material per unit output	
			During the previous financial year	During the current financial year
1.				
2.				
3.				

* Industry may use if disclosing details of raw material would violate contractual obligations; otherwise all industries have to name the raw material used.



Part - C

Pollution discharged to environment /unit of output
(Parameters as specified in the consent issued)

	Pollutants	Quantity of pollutants discharged (mass/day)	Concentration of pollutants in discharges (mass/volume)	Percentage variation from prescribed standards with reasons
(a) Water	Zero Discharge Unit. No pollutants discharged into the environment as the entire sewage is treated and the entire (100%) treated effluent from STP is used for cooling towers and horticulture. The monitoring report of STP effluent is enclosed as <i>Annexure - I</i> .	Not Applicable	Not Applicable	Not Applicable
(b) Air	Emissions from stacks of back-up DG sets (operated only during power failure) The Stack Emission monitoring report is attached as an <i>Annexure - II</i>	The results of monitoring of DG stack emissions from approved laboratory is enclosed as Annex 2		

Part - D

Hazardous Wastes

(As specified under Hazardous Wastes (Management, Handling and Trans-boundary Movement) Rules,

	Hazardous Wastes	Total Quantity (kg)	
		During the previous financial year	During the current financial year
(a) From process	Used Oil from DG sets	3300 L	3080 L
(b) From Process	E-Waste (Burnt lights, hardware etc)	NIL	NIL
(c) From pollution control facilities	Not Applicable	Not Applicable	Not Applicable

Part - E

Solid Wastes

	Solid Wastes	Total Quantity (kg)	
		During the previous financial year	During the current financial year
(a) From process (IT/ITES Special Economic Zone)	1) Wet Garbage	27795 KG	73467 KG
	2) Dry Garbage	238295 KG	281388 KG
	3) Scrap	NIL	NIL
(b) From pollution control	STP Sludge	37495 KG	72800 KG



facility			
(c) (1) Quantity recycled or re-utilizes within the unit	1) Dewatered STP Sludge is used as manure in horticulture	<u>NIL</u>	<u>NIL</u>
(2) Sold	1) Scrap		<u>NIL</u>
(3) Disposed	1) Wet Garbage is disposed to Govt. of Haryana authorized vendor.	27795 KG	73467 KG
	2) Dry Garbage is disposed to Govt. of Haryana authorized vendor	238295 KG	281388 KG

Part – F

Please specify the characterizations (in terms of composition of quantum) of hazardous as well as solid wastes and indicate disposal practice adopted for both these categories of wastes.

Solid wastes	Solid Wastes are segregated into organic biodegradable wastes (Waste vegetables, food, etc) , non-biodegradable wastes ([paper, plastic, glass, etc) and Domestic Hazardous waste (sanitary & other non recyclable & non combustible waste) and collected in separate bins. The said wastes are disposed to MCG/ State Govt. Approved vendor.
Hazardous wastes	The used oil from DG sets is sold to authorized waste recyclers.

Part – G

Impact of the pollution abatement measures taken on conservation of natural resources and the cost of production.

Treated effluent from STP is recycled for use in toilet flushing, Air-conditioning and horticulture

Part – H

Additional measures/investment proposal for environmental protection including abatement of pollution, prevention of pollution.

All measures for environmental protection and abatement/ prevention of pollution have already been taken. Therefore, no additional measure is envisaged.

Part – I

Any other particulars for improving the quality of the environment:

1. The entire sewage is treated up to the tertiary level in the STP.
2. The entire (100%) treated effluent from STP is recycled for use in HVAC, toilet flushing & horticulture.
3. Required stack height for DG sets provided as per norms to reduce air pollution.
4. Acoustic treatment of DG room for reduction/control of noise as per norms.
5. Adequate tree plantation has been carried out for dust control, noise control ,protection from pollutants in air , shading and aesthetics.
6. Rainwater harvesting pits have been provided for recharge of groundwater.
7. Solid wastes are segregated and recycled through authorized vendors.



Tax Invoice


34

Supplier Company ASF INSIGNIA SEZ PRIVATE LIMITED ASF INSIGNIA SEZ ITeS, Village GwalPahariGurgaon Faridabad Road District - SubTeh Wazirabad, Gurgaon PinCode - 122003 GSTIN - 06AACCC7148L1ZG Place of Supply: Haryana Name of State (State Code): Haryana(07)	Invoice No: 001023500002 SAP Document Number: 91300250 Date of Issue: 02.11.2023 Vehicle No: RJ40GA-2066
Recipient: SHIV SHAKTI OIL & LUBRICANTS F-557; RIICO Ind. Area Chopanki, post Tapokara, Tizara Alwar 301017 GSTIN - 08ABFFS4464G1ZZ Whether TAX is Payable on Reverse Charge - No	Order No. Date Permission No. 91600159 Dated 30.10.2023 Delivery: 91700281 Buyer (if other than consignee) Same As Consignee

Mark/Nos./Kind of packages	Description of goods	HSN / SAC	Quantity	UOM	Rate Rs.	Amount Rs.
1	Disposal of Used Oil with Drum	27109900	3,080.000	L	20.89	64,341.20
N. Wt:	0.000 KG					
G. Wt:	0.000 KG					
TOTAL			3,080.000			64,341.20
	BCD			5.00 %		3,217.06
	SWS			10.00 %		321.71
	CGST					
	SGST					
	IGST			18.00 %		12,218.39
	Net Invoice Value					80,098.36

Total: RUPEES EIGHTY THOUSAND NINETY EIGHT Rupees THIRTY SIX Paise ONLY.

We certify that the above particulars are true & correct.

For ASF INSIGNIA SEZ PVT LTD
 For ASF Insignia SEZ Pvt. Ltd.

 Signature / DSC
 Authorised Signatory

ASF Insignia SEZ Pvt. Ltd.
INWARD/ OUTWARD ENTRY
 SI No.....237.....
 Time In.....
 Time Out.....14:30.....
 Date.....02/11/2023.....
 Sign. (Security).....[Signature].....




FORM 10

[See Rule 19 (1)]

MANIFEST FOR HAZARDOUS AND OTHER WASTE

273

1.	Sender's name and mailing address (including Phone no. and e-mail)	ASF Insignia SEZ Pvt. Ltd Gurgaon- Faridabad Road, VIII- Gwal Pahari, Teh-Schna District Gurgaon (Haryana)			
2.	Sender's Authorisation No.				
3.	Manifest Documents No.	SSOL / HW / 01 / 2023-24 / ASF..... / Dt. 02-11-23			
4.	Transporter's name and address: (including Phone No. and e-mail)	M/s. Shiv Shakti Oil & Lubricants ,			
5.	Type of vehicle	(Truck/Tankers/Special Vehicle) ✓			
6.	Transporter's registration No.	Self			
7.	Vehicle registration No.	RJ-40 GA - 2066			
8.	Receiver's name and mailing address (including Phone No. and e-mail)	SHIV SHAKTI OIL & LUBRICANTS F-557 & F-693 (Unit 3), RIICO Industrial Area Chopanki, Post: Tapukara Teh. Tijara, Distt. Alwar - 301707 (Rajasthan) INDIA Ph.: +91-9310003389, 9350003389 E: shivshakti_lub07@yahoo.co.in			
9.	Receiver's Authorisation No.	RSPCB / HWM / 20 23-2024 / HSW / HSW / 08 RSPCB / HWM / 20 19-2020 / HSW / HSW / 106 (Unit 3)			
10.	Waste description	<input checked="" type="checkbox"/> Used Lube Oil, Used Cutting Coolant Oil (Cat. 5.1) ✓ <input checked="" type="checkbox"/> Used Hydraulic Oil, Used Transformer Oil (Cat. 5.2) X <input checked="" type="checkbox"/> Waste or Residues Containing Oil (Cat. 33.1) (Unit-3) ✓ <input checked="" type="checkbox"/> Containers/ Barrels/ Drums Contaminated with Hazardous Wastes/ Chemicals			
11.	Total quantity No. of Containers 3090 LTR m ³ or MT 04 Nos.			
12.	Physical form	<input checked="" type="checkbox"/> Solid/Semi-Solid/Sludge <input checked="" type="checkbox"/> OILY / Tarry / Slurry / Liquid			
13.	Special handling instructions and additional information	Disposed/ sale as per Precautions/ Rules of Central Pollution Control Board/ MOEF/ SPCB to the Authorized Reg. Re-recycler/ Re-reprocessor (Handle with Care)			
14.	Sender's Certificate	 <p>I hereby declare that the contents of the consignment are fully and accurately described above by proper shipping name and are categorised, packed, marked, and labelled and are in all respects in proper condition for transport by road according to applicable national government regulations.</p>			
Name & stamp:		Signature	Month	Day	Year
			11	02	2023
15.	Transporter acknowledgement of receipt of Wastes				
Name & stamp:		Signature	Month	Day	Year
			11	02	2023
16.	Receiver's certification for receipt of hazardous and other waste				
Name & stamp:		Signature	Month	Day	Year
			11	02	2023

COPY 1 of 7

White Copy

To be forwarded by the sender to the State Pollution Control Board



e-Way Bill



1. E-WAY BILL Details

eWay Bill No: 3916 8121 5046

Generated Date: 02/11/2023 01:51 PM

Generated By: 06AAC CC714 8L1ZG

Valid Upto: 03/11/2023

Mode: Road

Approx Distance: 42km

Type: Outward - Supply

Document Details: Tax Invoice - 1023500002 -

Transaction type: Regular

02/11/2023

2. Address Details

From

GSTIN : 06AAF CC714 8L1ZG
ASF INSIGNIA SEZ PVT LTD
OTHER COUNTRIES

:: Dispatch From ::

GAWALPAHARI
FARIDABAD ROADGURGAON
Gurugram, HARYANA-122001

To

GSTIN : 08ABF FS446 4G12Z
SHIV SHAKTI OIL & LUBRICANTS
RAJASTHAN

:: Ship To ::

F-557
CHOPANKI INDUSTRIAL AREA
CHOPANKI, BHIWADI, RAJASTHAN-301019

3. Goods Details

MSN Code	Product Name & Desc.	Quantity	Taxable Amount Rs.	Tax Rate (C+S+I+Cess+Cess Non.Adyol)
27109900	DISPOSAL OF USED OIL WITH DRUM &	3060.00 LTR	67879.97	NE+NE+18.000+0.000+0.00

Tot. Tax'ble Amt	CGST Amt	SGST Amt	IGST Amt	CESS Amt	CESS Non.Adyol Amt	Other Amt	Total Inv.Amt
67879.97	0.00	0.00	12218.30	0.00	0.00	0.00	80098.27

4. Transportation Details

Transporter ID & Name : 08ABFFS4464G1ZZ & SHIV SHAKTI OIL LUBRICANTS

Transporter Doc. No & Date : & 02/11/2023

5. Vehicle Details

Mode	Vehicle / Trans Doc No & Dt.	From	Entered Date	Entered By	CEWB No. (if any)	Multi Veh.Info (if any)
Road	RJ40GA2060	Gurugram	02-11-2023 01:51 PM	06AACCC7148L1ZG	-	-



391681215046



Authorisation Cum-Passbook for
Re-refining/Recycling of Hazardous Waste

43

Name and Address of the industry : M/s Shiv Shakti Oil & Lubricants
E-557, RIA Chopanki, Bhiwadi,
Tehsil - Tijara, District - Alwar

Telephone/Fax No. : 9918408248

E-Mail Address : shivshakti_lub07@yahoo.co.in

Authorisation No. : RPCB/HWM/2023-2024/HSW/HSW/E.

Date of issue : 11/05/2023

Validity period : 01/04/2023 To 31/03/2028

Type & quantity of the Hazardous Waste (S) permitted for procurement and recycling.

S. No.	Hazardous Waste (Used/Waste Oil) Type	Quantity (Kilolitres/Metric ton per annum)
1.	Used or spent oil (Schedule - I, code - S.1)	2000 KLA (Two Thousand KLA)
2.	Wastes or residues containing oil (Schedule - IX, code - S.2)	1600 KLA (Sixteen hundred KLA)




11.05.2023
अ. पी. गुप्ता
Authorized Signatory & Seal
अति. मुख्य पर्यावरण निदेशक

A circular stamp or seal at the bottom right corner of the page.

**Endorsement by the Auctioneer/Seller (except column no. 6 & 7)
(Condition No.3 of the Authorisation)**

Authorisation No. : APCB/MWCH/2023-2024/1 Date: 11/05/2023
MSW/MSW/8

Waste(s) Type : Used or spent oil Permitted Quantity : 2000 KLA
Waste as Castles Containers Bag Oil - 1600 KLA

S. No.	Date	Address of the Auctioneer/Seller	Type & Quantity of HW sold /Auctioned	Signature & Seal of the Auctioneer/Seller with date	Date of arrival in Recyclers premises & Challan No.	Balance Quantity (Registered - procured till date)
(1)	(2)	(3)	(4)	(5)	(6)	(7)
55						
56						
57	02/11/23	AST Dalgaria SEZ 11, Gurgaon	5.1 3080 Ltr		02/11/23 100 0010215 Form 2	
58						
59						
60						

*to be filled by the Recycler

Mur
*



ENVIRONMENT CLEARANCE

MAKE AN ENQUIRY

Documents

- Environment Extension of Validity for ASF Insignia 20 August, 2021 to 19 August, 2024
- Environmental Clearance 2021 Amendment
- Environmental Clearance 2019 Amendment
- Environmental Clearance ASF Insignia IT/ITES SEZ

Form V

- Form-V ASF Insignia SEZ Pvt. Ltd, Half Yearly 2023-2024
- Form-V ASF SEZ Half Yearly 2022-2023
- Form-V ASF Insignia 2021-2022
- Form-V Annual Report 01 April, 2020 to 31 March, 2021
- Form-V Annual Report 01 April, 2019 to 31 March, 2020 for Hazardous Wastes
- Form-V Annual Report 01 April, 2018 to 31 March, 2019
- Form-V Annual Report 01 April, 2017 to 31 March, 2018

Six Monthly

- Six Monthly Report October 2023 to March 2024
- Six Monthly Report April 2023 to September 2023
- Six Monthly Report October 2022 to March 2023
- Six Monthly Report April 2022 to September 2022
- Six Monthly Report October 2021 to March 2022
- Six Monthly Report April 2021 to Sept 2021
- Six Monthly Report October 2019 to March 2020
- Six Monthly Report April 2019 to September 2019
- Six Monthly Report October 2018 to March 2019
- Six Monthly Report April 18 to Sept 2018

Form IV

- Annual Report 01 April, 2020 to 31 March, 2021
- Form-IV Annual Report 01 April, 2019 to 31 March, 2020 for Hazardous Wastes
- Form-IV Annual Report 01 April, 2018 to 31 March, 2019
- Form-IV Annual Report 01 April, 2017 to 31 March, 2018

Form IX

- Form IX April 2024 to September 2024
- Form IX October 2023 to March 2024
- Form IX April 2023 to September 2023
- Form IX October 2022 to March 2023
- Form IX October 2021 to March 2022
- Form IX April 2021 to September 2021
- Form IX Report April 2021 to September 2021 Receipt
- Form IX Half Yearly Return Used Batteries October 2020 to March 2021





ENVIRONMENTAL POLICY

ASF Group is extremely sensitive to protection of the environment and actively undertakes to continuously indoctrinate measures, existing and new, to conserve the environment. ASF Group strives to carry out its Business activities and operations in a manner that not only diligently refrains from causing any adverse impact on the environment but also take preemptive measures to reduce & mitigate any adverse impact on environment owing to externalities associated with its business/operations. We are conscious of our responsibility and uphold the philosophy to protect and conserve the environment with utmost accountability.

Our Policy will be to :

- strictly comply with all applicable environmental laws and regulations
- promote concept of Reduce, Recycle and Reuse
- maximize Green cover in our real estate projects

Our approach to achieve the guidelines of our policy :

- Submission of all the compliance reports with regard to air, water , noise pollution to the competent authorities
- Use of natural, recycled material to large extent
- Zero discharge of water through its buildings by recycling and treatment of water
- Maximum provision of green cover with local species of shrubs , trees , plants
- Carrying out environment audits
- Adopting environmental friendly design of the buildings with its orientation, use of façade glass, paints, block works, concrete , STPs etc
- Use of efficient plant and machinery
- Using eco friendly cleaning agents in house keeping
- Use of renewable sources of power to extent possible
- Use of LED Light fixtures
- Promote use of environmental safeguards among our employees & stake holders



Anil Saraf
Chairman and Managing Director
ASF Insignia SEZ Pvt. Ltd

ASF INSIGNIA SEZ PRIVATE LIMITED

Site Office : ASF Insignia SEZ IT/TeS, Village Gwalpahari, off Gurgaon-Faridabad Road, Gurgaon, Sohna-122003, Haryana

t: +91 124 4777200 f: +91 124 4234110 e: corporate@asfInfrastructure.com w: www.asfInfrastructure.com

Regd. Office : 11, Babar Lane, Bengali Market, New Delhi-110001 t: +91 11 23355511 f: +91 1123739298

Corp. Office : ASF Centre, 362-363, Udyog Vihar, Phase-IV, Gurgaon-122016 (India)

CIN U45201DL2005PTAC140408

Creating Intelligent Spaces®
